

CONTRACT TIME FOR COMPLETION


Wisconsin Department of Transportation DT1923 04/2020

Project ID 8949-00-71/8949-00-74
Work Type Rehabilitation

Highway USH 12
County St. Croix

Project Title Hudson - Baldwin
Project Limits 165 North to USH 63 North/USH 63 North to USH 63 S

Date of Letting July 13, 2021
Probable Date of Beginning August 9, 2021

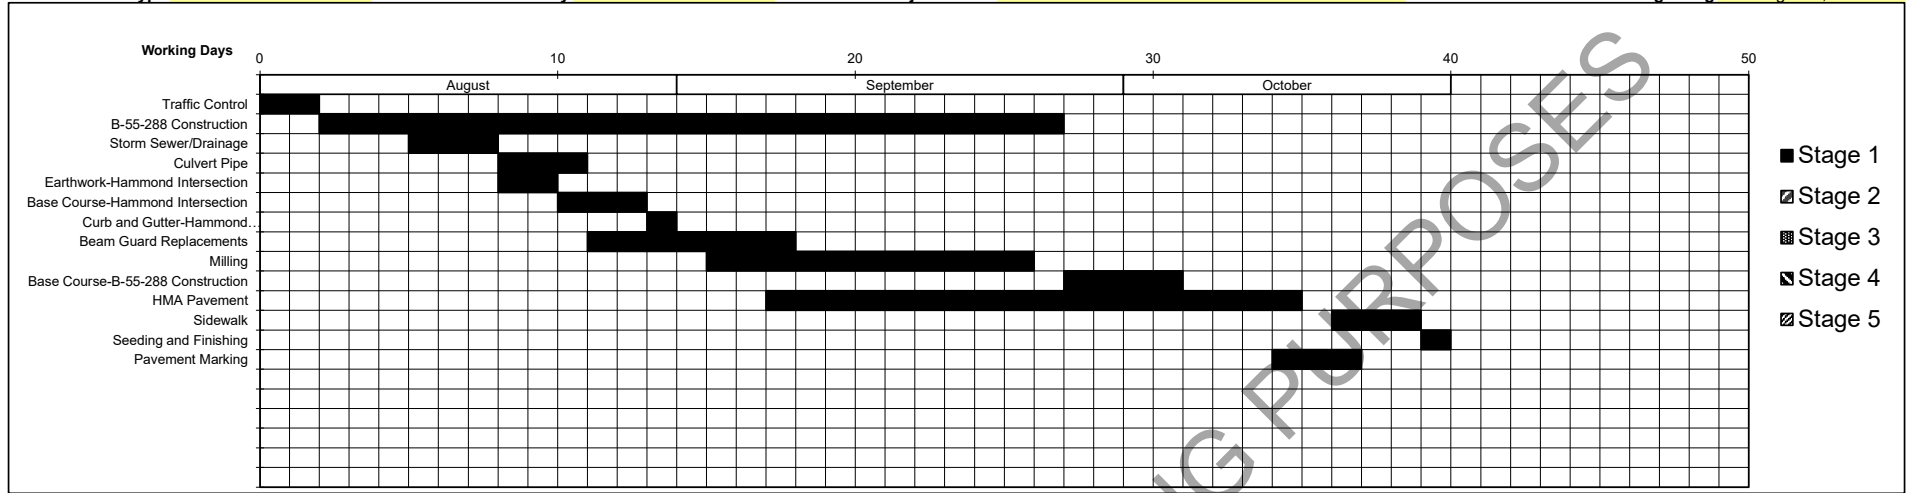

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5	
	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
Traffic Control	2					2	DAY	1	2 / / / /	0	2								
B-55-288 Construction	25					25	DAY	1	25 / / / /	2	27								
Storm Sewer/Drainage	3					3	DAY	1	3 / / / /	5	8								
Culvert Pipe	250					250	LF	100	3 / / / /	8	11								
Earthwork-Hammond Intersection	1,480					1,480	CY	920	2 / / / /	8	10								
Base Course-Hammond Intersection	2,350					2,350	TON	810	3 / / / /	10	13								
Curb and Gutter-Hammond Intersection	650					650	LF	850	1 / / / /	13	14								
Beam Guard Replacements	1,850					1,850	LF	300	7 / / / /	11	18								
Milling	175,900					175,900	SY	17000	11 / / / /	15	26								
Base Course-B-55-288 Construction	3,200					3,200	TON	810	4 / / / /	27	31								
HMA Pavement	33,500					33,500	TON	1900	18 / / / /	17	35								
Sidewalk	4,030					4,030	SF	1800	3 / / / /	36	39								
Seeding and Finishing	1					1	DAY	1	1 / / / /	39	40								
Pavement Marking	168,000					168,000	LF	60000	3 / / / /	34	37								
									/ / / /										
									/ / / /										
									/ / / /										
									/ / / /										
									/ / / /										
									/ / / /										

Month	Date		Days			Possible Work Days	Probable Working Days %	Probable Working Days	
	Begin	End	Month	Total	Holiday			Month	Total
August	8/9/2021	8/31/2021	23	23	0	17	85	14	14
September	9/1/2021	9/30/2021	30	53	1	21	70	15	29
October	10/1/2021	10/29/2021	29	82	0	21	50	11	40
			0	82		0		0	40
			0	82		0		0	40
			0	82		0		0	40
			0	82		0		0	40
			0	82		0		0	40
			0	82		0		0	40
			0	82		0		0	40
			0	82		0		0	40
			0	82		0		0	40
			0	82		0		0	40
			0	82		0		0	40

REMARKS

Construct Structure B-55-288, Hammond Intersection Reconstruction, Culvert Replacements, Beam Guard Replacements, Hammond Drainage Improvements, Mill and Overlay, Curb Ramp Upgrades, Finish Work

Contract Work Type		
☐ Calendar Days		74
☐ Working Days		37
☒ Completion Date		October 29, 2021
Prepared By		JPM 2/1/21

CONSTRUCTION YEAR: 2021
