


CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2020

Project ID	1166-12-89	Highway	IH 39	Project Title	Plainfield - Stevens Point	Date of Letting	August 10, 2021
Work Type	Bridge Rehabilitation	County	Portage	Project Limits	Structures B-49-14, 15, 16, 17	Probable Date of Beginning	October 11, 2021

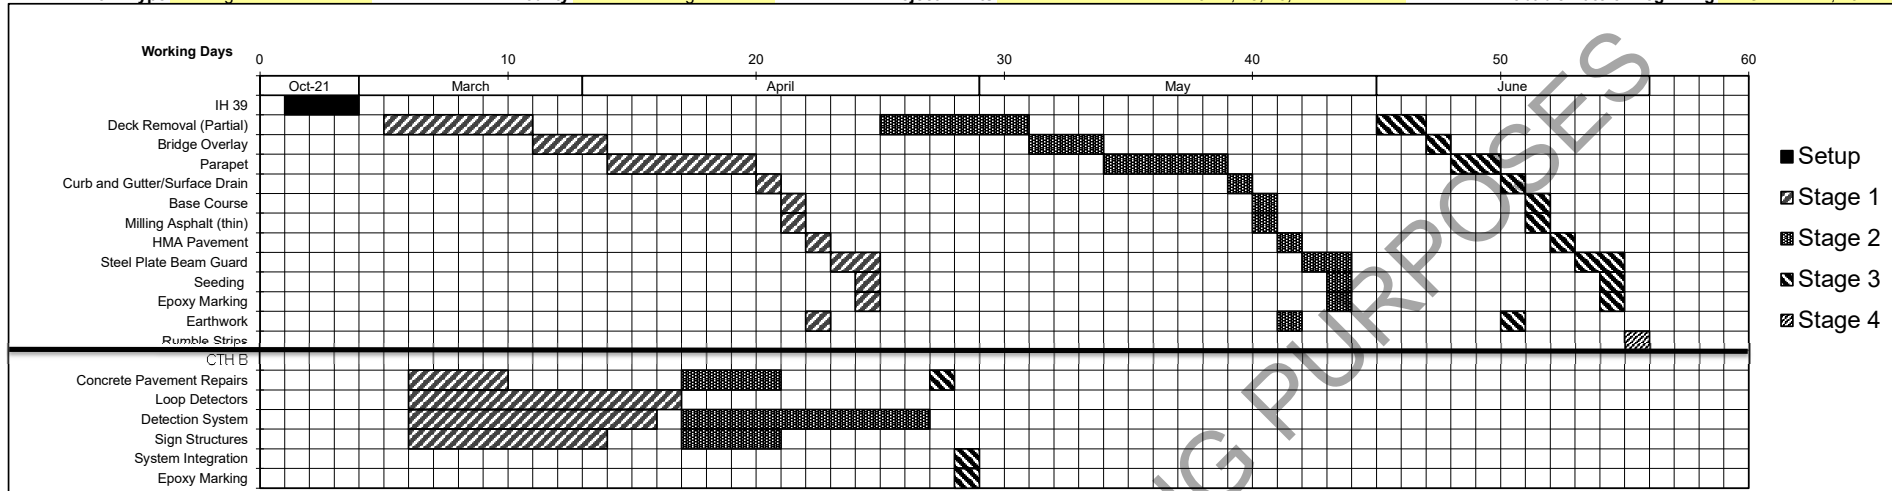

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Setup		Stage 1		Stage 2		Stage 3		Stage 4	
	Setup	Stage 1	Stage 2	Stage 3	Stage 4					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
IH 39	3					3	DAY	1	3 / / / / /	1	4								
Deck Removal (Partial)		15,147	15,147	3,821		34,115	SF	2700	/ 6 / 6 / 2 /			5	11	25	31	45	47		
Bridge Overlay		1,683	1,683	425		3,791	SY	750	/ 3 / 3 / 1 /			11	14	31	34	47	48		
Parapet		723	543	180		1,446	LF	125	/ 6 / 5 / 2 /			14	20	34	39	48	50		
Curb and Gutter/Surface Drain		108	54	54		215	LF	850	/ 1 / 1 / 1 /			20	21	39	40	50	51		
Base Course		138	138	185		461	Ton	490	/ 1 / 1 / 1 /			21	22	40	41	51	52		
Milling Asphalt (thin)		2,662	2,662	1,662		6,987	SY	16000	/ 1 / 1 / 1 /			21	22	40	41	51	52		
HMA Pavement		453	453	453		1,360	Tons	1400	/ 1 / 1 / 1 /			22	23	41	42	52	53		
Steel Plate Beam Guard		759	759	759		2,278	LF	420	/ 2 / 2 / 2 /			23	25	42	44	53	55		
Seeding		2,370	2,370	2,370		7,110	SY	4600	/ 1 / 1 / 1 /			24	25	43	44	54	55		
Epoxy Marking		5,000	5,000	5,000		15,000	LF	60000	/ 1 / 1 / 1 /			24	25	43	44	54	55		
Earthwork		320	320	320		959	CY	920	/ 1 / 1 / 1 /			22	23	41	42	50	51		
Rumble Strips					7,184	7,184	LF	35000	/ / / / 1									55	56
CTH B									/ / / /										
Concrete Pavement Repairs		949	949	10		1,908	SY	250	/ 4 / 4 / 1 /			6	10	17	21	27	28		
Loop Detectors		22				22	Each	2	/ 11 / / /			6	17						
Detection System		1	1			1	LS	0.05	/ 10 / 10 / /			6	16	17	27				
Sign Structures		2	1			3	Each	0.25	/ 8 / 4 / /			6	14	17	21				
System Integration				1		1	LS	1	/ / / 1 /							28	29		
Epoxy Marking				500		500	LF	41000	/ / / 1 /							28	29		

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday			%	Total
			0	0		0		0	0
Oct-21	10/11/2021	10/31/2021	21	21	1	14	27	4	4
March	3/14/2022	3/31/2022	18	39		14	65	9	13
April	4/1/2022	4/30/2022	30	69		21	77	16	29
May	5/1/2022	5/31/2022	31	100	2	20	80	16	45
June	6/1/2022	6/20/2022	20	120		14	80	11	56
			0	120		0		0	56
			0	120		0		0	56
			0	120		0		0	56
			0	120		0		0	56
			0	120		0		0	56
			0	120		0		0	56

REMARKS

Contract Work Type	
Calendar Days	
Working Days	
Completion Date	June 20, 2022
Prepared By	Andrew Casper

CONSTRUCTION YEAR: 2022
