

CONTRACT TIME FOR COMPLETION (STH 100)


Wisconsin Department of Transportation DT1923 04/2011

Project ID 2150-00-72, 2270-04-70, 2565-07-70
Work Type Modernization

Highway WIS 57
County Milwaukee/Ozaukee

Project Title STH 57 - Vil Brown Deer & City Mequon
Project Limits Teutonia Avenue to Mequon Road

Date of Letting September 14, 2021
Probable Date of Beginning November 1, 2021

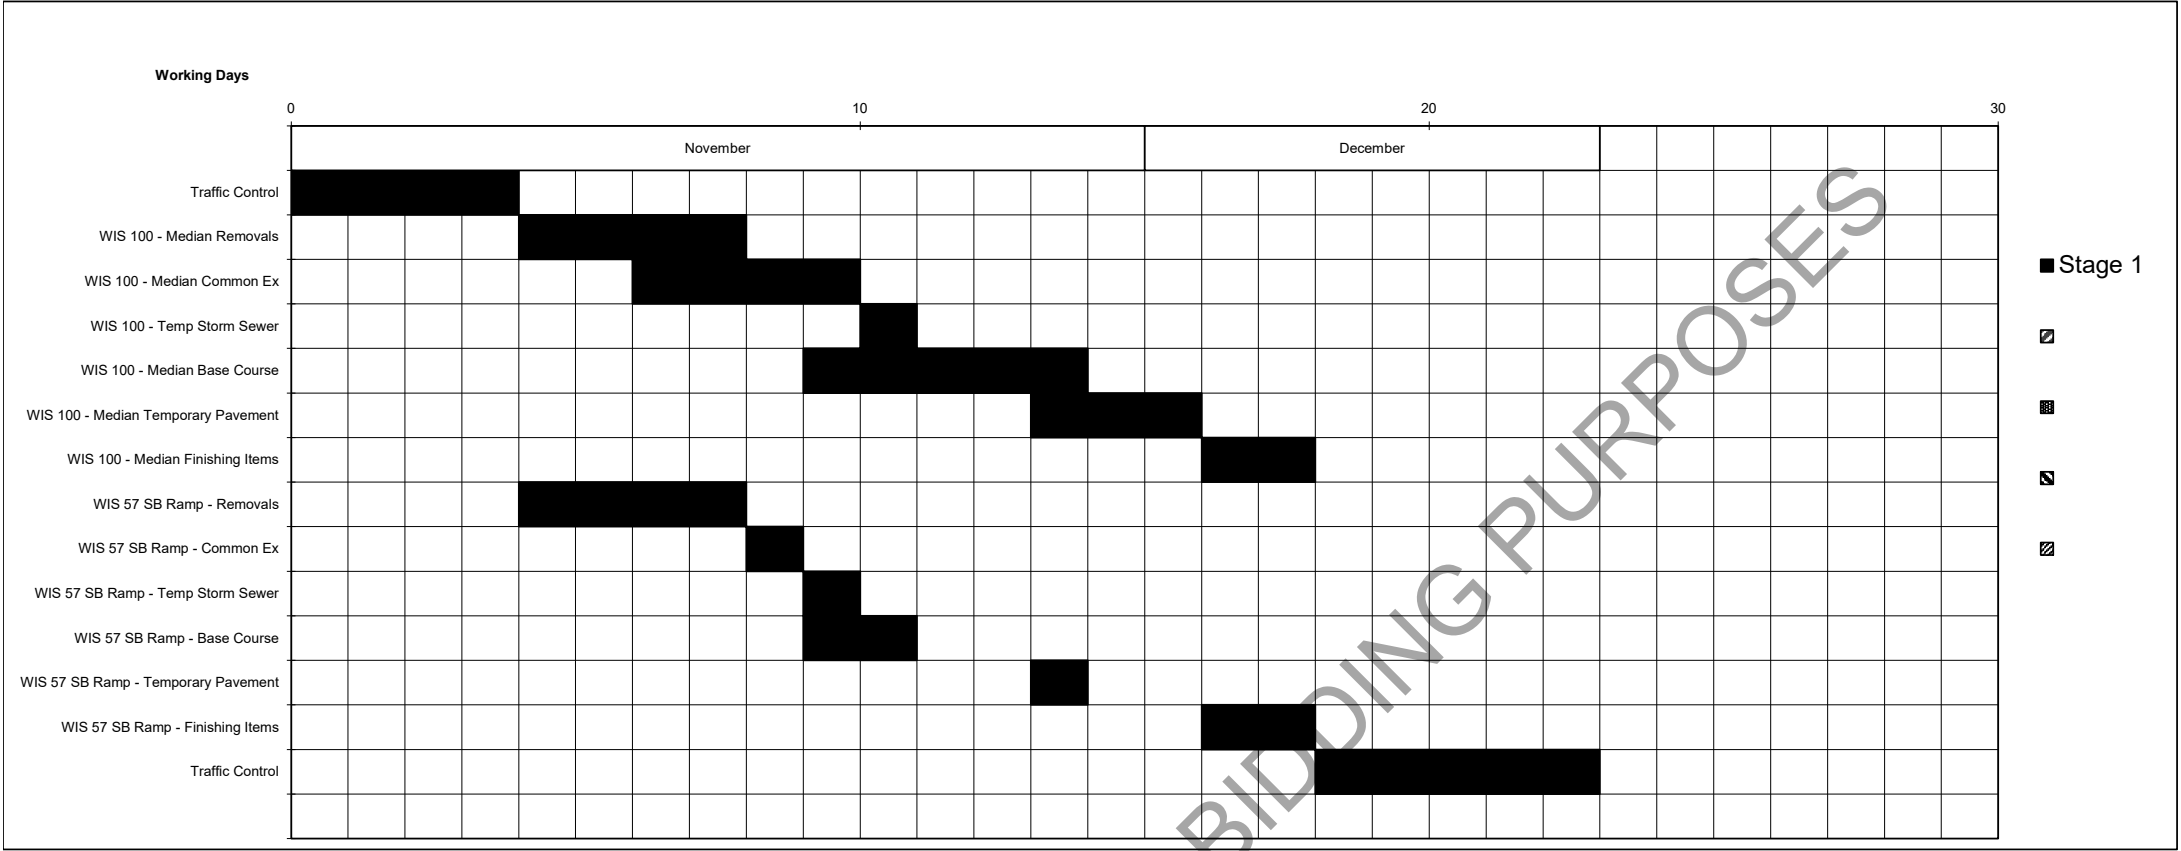

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1									
	Stage 1		0	0	0					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
Traffic Control	4					4	DAY	1	4 / / / / /	0	4								
WIS 100 - Median Removals	4					4	DAY	1	4 / / / / /	4	8								
WIS 100 - Median Common Ex	3,416					3,416	CY	920	4 / / / / /	6	10								
WIS 100 - Temp Storm Sewer	1					1	EA	1	1 / / / / /	10	11								
WIS 100 - Median Base Course	3,271					3,271	TON	810	5 / / / / /	9	14								
WIS 100 - Median Temporary Pavement	1,687					1,687	TON	730	3 / / / / /	13	16								
WIS 100 - Median Finishing Items	1					1	DAY	0.5	2 / / / / /	16	18								
WIS 57 SB Ramp - Removals	4					4	DAY	1	4 / / / / /	4	8								
WIS 57 SB Ramp - Common Ex	873					873	CY	920	1 / / / / /	8	9								
WIS 57 SB Ramp - Temp Storm Sewer	1					1	EA	1	1 / / / / /	9	10								
WIS 57 SB Ramp - Base Course	900					900	TON	810	2 / / / / /	9	11								
WIS 57 SB Ramp - Temporary Pavement	478					478	TON	730	1 / / / / /	13	14								
WIS 57 SB Ramp - Finishing Items	1					1	DAY	0.5	2 / / / / /	16	18								
Traffic Control	5					5	DAY	1	5 / / / / /	18	23								
									/ / / / /										

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0	61	0	0
			0	0		0	65	0	0
			0	0		0	65	0	0
			0	0		0	77	0	0
			0	0		0	80	0	0
			0	0		0	80	0	0
			0	0		0	85	0	0
			0	0		0	85	0	0
			0	0		0	80	0	0
			0	0		0	73	0	0
November	11/1/2021	11/30/2021	30	30	1	21	70	15	15
December	12/1/2021	12/17/2021	17	47		13	58	8	23

REMARKS

This sheet shows Stage 1 in Fall 2021

Calendar Days 47
Working Days 23
Completion Date June 30, 2023
Prepared By Chris Quesnell

CONSTRUCTION YEAR: 2021
