


CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2011

Project ID	6430-12-71	Highway	STH 76	Project Title	USH 41 - CTH JJ	Date of Letting	November 12, 2019
Work Type	Reconstruction	County	Winnebago	Project Limits	STH 76 Divided Ends - CTH JJ	Probable Date of Beginning	April 6, 2020

WIS 76 OVERALL PROJECT

Working Days

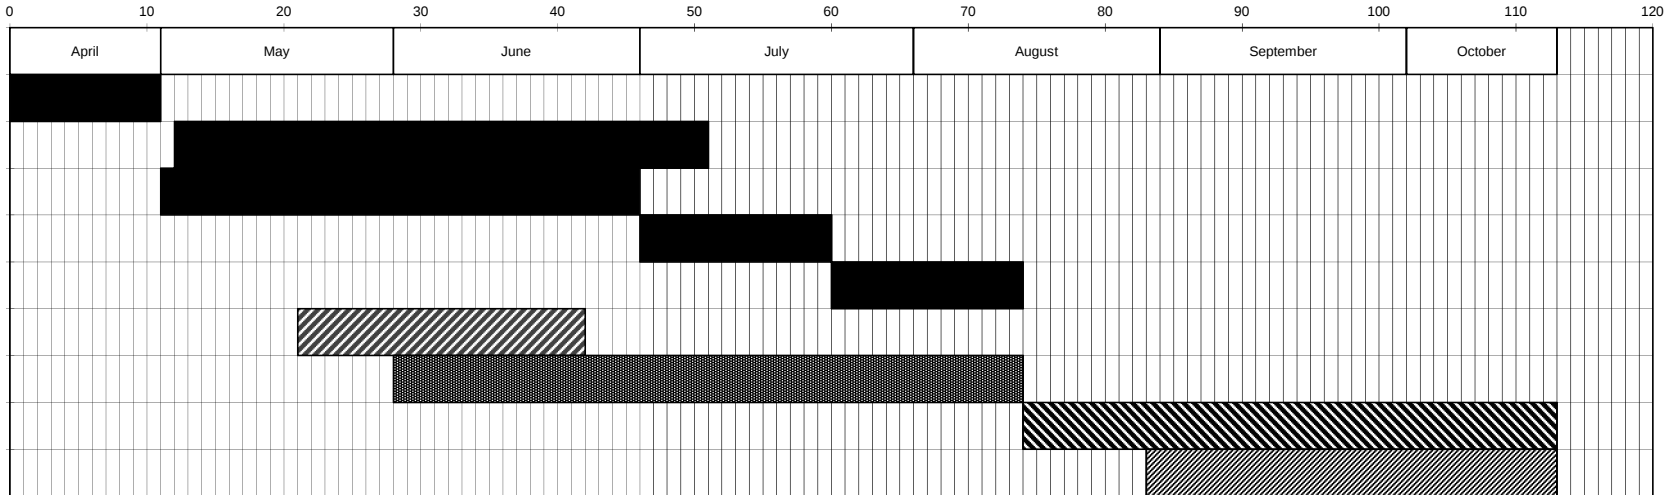

Note: Roundabout Intersections include approaches

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1 and 2		Stage 3		Stage 4		Stage 5		Stage 6	
	Stage 1 and 2	Stage 3	Stage 4	Stage 5	Stage 6					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
STAGE 1 (BYPASS LANES CTH JJ)	11					11	LS	1	11 / / / / /	0	11								
STAGE 2 (CTH GG)	39					39	LS	1	39 / / / / /	12	51								
STAGE 2A (CTH JJ)	35					35	LS	1	35 / / / / /	11	46								
STAGE 2B (CTH JJ)	14					14	LS	1	14 / / / / /	46	60								
STAGE 2C (CTH JJ)	14					14	LS	1	14 / / / / /	60	74								
STAGE 3 (STH 76 - south to CTH GG)		21				21	LS	1	/ 21 / / /			21	42						
STAGE 4 (STH 76 - CTH GG to CTH G)			46			46	LS	1	/ / 46 / /					28	74				
STAGE 5 (CTH G)				39		39	LS	1	/ / / 39 /							74	113		
STAGE 6 (STH 76 - CTH G to CTH JJ)					30	30	LS	1	/ / / / 30									83	113
Total working days per stage										74		21		46		39		30	

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
April	4/6/2020	4/30/2020	25	25		19	58	11	11
May	5/1/2020	5/31/2020	31	56		21	80	17	28
June	6/1/2020	6/30/2020	30	86		22	80	18	46
July	7/1/2020	7/31/2020	31	117		23	85	20	66
August	8/1/2020	8/31/2020	31	148		21	85	18	84
September	9/1/2020	9/30/2020	30	178		22	80	18	102
October	10/1/2020	10/21/2020	21	199		15	73	11	113
November			0	199		0		0	113
			0	199		0		0	113

REMARKS

Calendar Days
Working Days
Completion Date
Prepared By

199
113
October 23, 2020

CONSTRUCTION YEAR: 2020

CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2011

Project ID
Work Type

6430-12-71
Reconstruction

Highway
County

STH 76
Winnebago

Project Title
Project Limits


USH 41 - CTH JJ
STH 76 Divided Ends - CTH JJ

Date of Letting
Probable Date of Beginning

November 12, 2019
April 6, 2020

CTH JJ INTERSECTION

Working Days

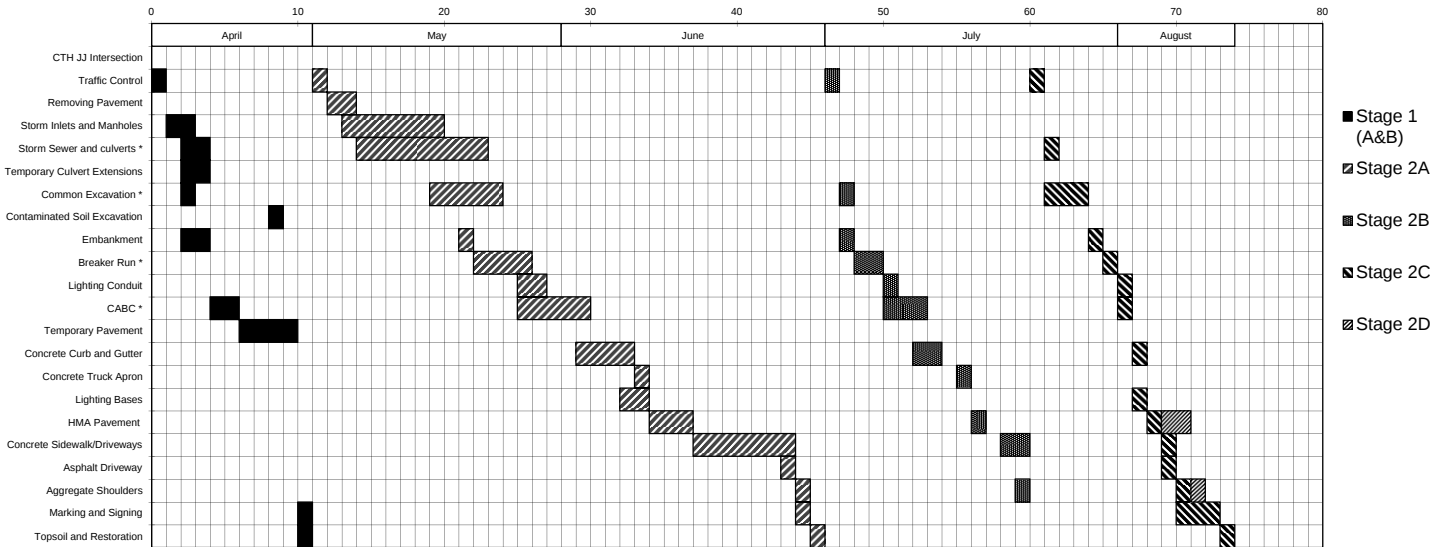

Note: Roundabout Intersections include approaches

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1 (A&B)		Stage 2A		Stage 2B		Stage 2C		Stage 2D	
	Stage 1 (A&B)	Stage 2A	Stage 2B	Stage 2C	Stage 2D					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
CTH JJ Intersection																			
Traffic Control	1	1	1	1		4	DAYS	1	1 / 1 / 1 / 1 /	0	1	11	12	46	47	60	61		
Removing Pavement		7,200				7,200	SY	3600	/ 2 / / /			12	14						
Storm Inlets and Manholes	6	35				41	EACH	5	2 / 7 / / /	1	3	13	20						
Storm Sewer and culverts *	410	2,050		55		2,515	LF	250	2 / 9 / / 1 /	2	4	14	23			61	62		
Temporary Culvert Extensions	380					380	LF	250	2 / / / / /	2	4								
Common Excavation *	1,870	13,100	3,000	8,850		26,820	CY	3000	1 / 5 / 1 / 3 /	2	3	19	24	47	48	61	64		
Contaminated Soil Excavation	295					295	TON	1000	1 / / / / /	8	9								
Embankment	3,400	750	100	1,620		5,870	CY	2000	2 / 1 / 1 / 1 /	2	4	21	22	47	48	64	65		
Breaker Run *		11,980	5,480	630		18,090	TON	3000	/ 4 / 2 / 1 /			22	26	48	50	65	66		
Lighting Conduit		515	105	390		1,010	LF	500	/ 2 / 1 / 1 /			25	27	50	51	66	67		
CABC *	4,820	15,900	6,760	1,190		28,670	TON	3200	2 / 5 / 3 / 1 /	4	6	25	30	50	53	66	67		
Temporary Pavement	8,100					8,100	SY	2100	4 / / / / /	6	10								
Concrete Curb and Gutter		4,735	2,025	200		6,960	LF	1200	/ 4 / 2 / 1 /			29	33	52	54	67	68		
Concrete Truck Apron		325	110			435	SY	1000	/ 1 / 1 / /			33	34	55	56				
Lighting Bases		5		3		8	Each	4	/ 2 / / 1 /			32	34			67	68		
HMA Pavement		2,603	1,195	142	1,600	5,540	TON	1250	/ 3 / 1 / 1 / 2			34	37	56	57	68	69	69	71
Concrete Sidewalk/Driveways		21,145	3,360	2,590		27,095	SF	3050	/ 7 / 2 / 1 /			37	44	58	60	69	70		
Asphalt Driveway		130		7		137	TON	320	/ 1 / / 1 /			43	44			69	70		
Aggregate Shoulders		200	40	10	320	570	TON	1000	/ 1 / 1 / 1 / 1			44	45	59	60	70	71	70	71
Marking and Signing	1	1		3		5	DAYS	1	1 / 1 / / 3 /	10	11	44	45			70	73		
Topsoil and Restoration	4,000	6,120		4,610		14,730	SY	15000	1 / 1 / / 1 /	10	11	45	46			73	74		

*Including quantities associated with bypass lanes

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
April	4/6/2020	4/30/2020	25	25		19	58	11	11
May	5/1/2020	5/31/2020	31	56		21	80	17	28
June	6/1/2020	6/30/2020	30	86		22	80	18	46
July	7/1/2020	7/31/2020	31	117		23	85	20	66
August	8/1/2020	8/13/2020	13	130		9	85	8	74
			0	130		0		0	74
			0	130		0		0	74
			0	130		0		0	74
			0	130		0		0	74

CONSTRUCTION YEAR: 2020

REMARKS

Stage 1 - Bypass lanes construction; Stage 2A - Construction of south portion of roundabout; Stage 2B - Construction of north portion of roundabout; Stage 2C - Construction of remainder of north portion of roundabout and removal of bypass lanes; (STA. 490+00 to 503+92); Stage 2D - Construction of upper layer HMA for the entire intersection

Calendar Days
Working Days
Completion Date
Prepared By


130
74
August 13, 2020

CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2011

Project ID 6430-12-71 Highway STH 76 Project Title USH 41 - CTH JJ Date of Letting November 12, 2019
Work Type Reconstruction County Winnebago Project Limits STH 76 Divided Ends - CTH JJ Probable Date of Beginning April 20, 2020

CTH GG INTERSECTION

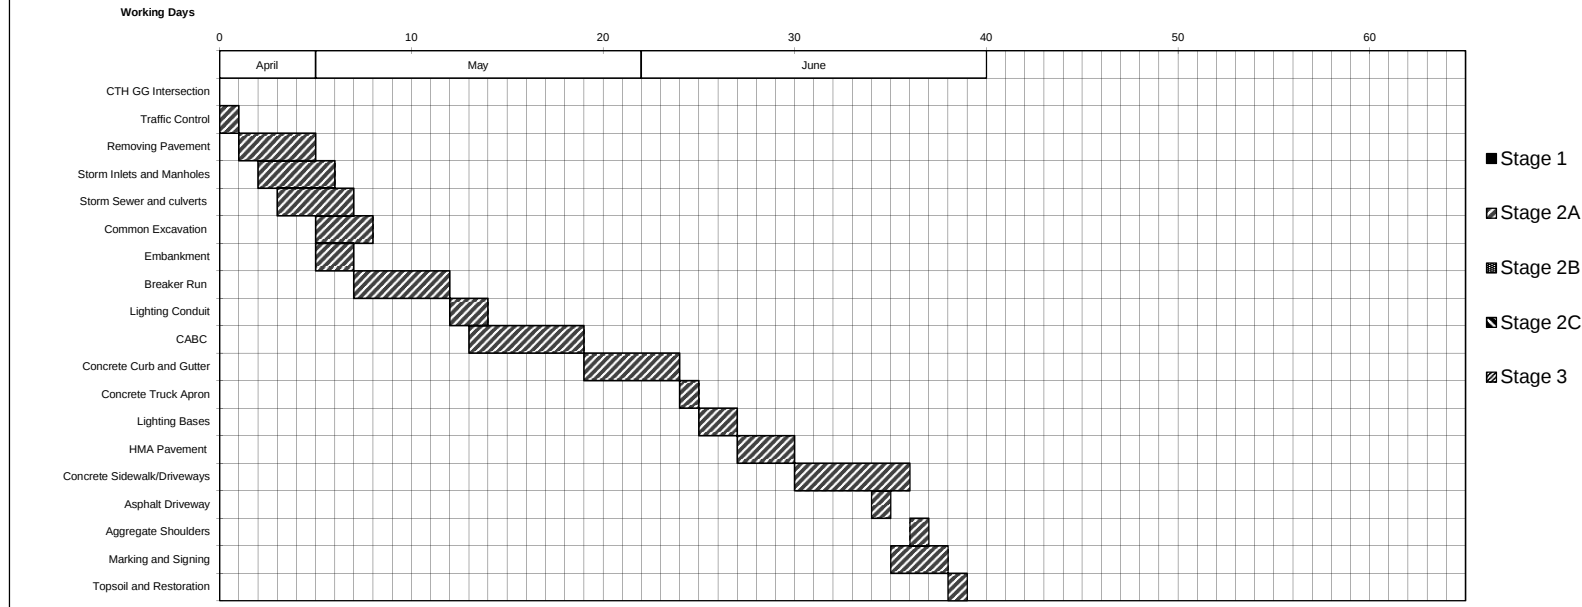

Note: Roundabout Intersections include approaches

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2A		Stage 2B		Stage 2C		Stage 3	
	Stage 1	Stage 2A	Stage 2B	Stage 2C	Stage 3					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
CTH GG Intersection																			
Traffic Control		1				1	DAYS	1	/ / / / /			0	1						
Removing Pavement		19,800				19,800	SY	5000	/ 4 / / /			1	5						
Storm Inlets and Manholes		17				17	EACH	5	/ 4 / / /			2	6						
Storm Sewer and culverts		810				810	LF	250	/ 4 / / /			3	7						
Common Excavation		9,370				9,370	CY	4000	/ 3 / / /			5	8						
Embankment		2,700				2,700	CY	2000	/ 2 / / /			5	7						
Breaker Run		13,280				13,280	TON	3000	/ 5 / / /			7	12						
Lighting Conduit		990				990	LF	500	/ 2 / / /			12	14						
CABC		19,320				19,320	TON	3250	/ 6 / / /			13	19						
Concrete Curb and Gutter		6,375				6,375	LF	1275	/ 5 / / /			19	24						
Concrete Truck Apron		645				645	SY	1000	/ 1 / / /			24	25						
Lighting Bases		8				8	Each	4	/ 2 / / /			25	27						
HMA Pavement		4,130				4,130	TON	1600	/ 3 / / /			27	30						
Concrete Sidewalk/Driveways		16,480				16,480	SF	3000	/ 6 / / /			30	36						
Asphalt Driveway		15				15	TON	320	/ 1 / / /			34	35						
Aggregate Shoulders		390				390	TON	1000	/ 1 / / /			36	37						
Marking and Signing		3				3	DAYS	1	/ 3 / / /			35	38						
Topsoil and Restoration		12,010				12,010	SY	15000	/ 1 / / /			38	39						

39

REMARKS

Construct the CTH GG roundabout with the intersection closed (~STA. 329+00 to STA 341+00).

Calendar Days
Working Days
Completion Date
Prepared By

72
40
June 30, 2020

CONSTRUCTION YEAR: 2020

CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2011


Project ID 6430-12-71
Work Type Reconstruction

Highway STH 76
County Winnebago

Project Title USH 41 - CTH JJ
Project Limits STH 76 Divided Ends - CTH JJ

Date of Letting November 12, 2019
Probable Date of Beginning August 10, 2020

CTH G INTERSECTION

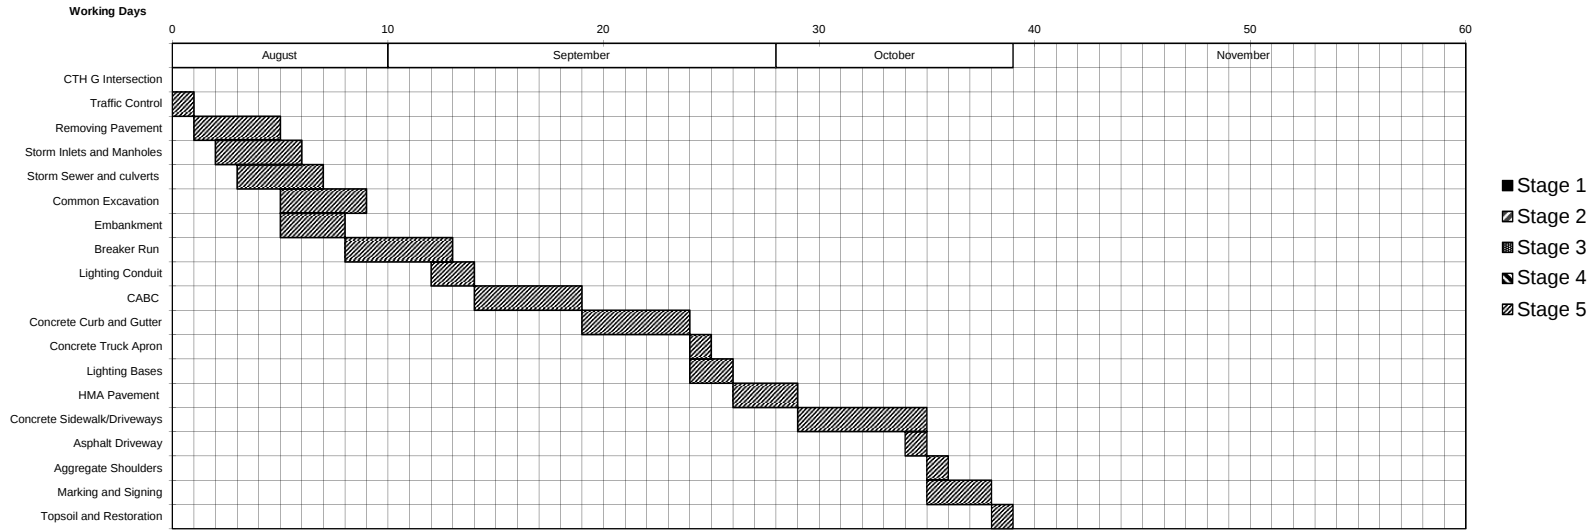

Note: Roundabout Intersections include approaches

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5	
	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
CTH G Intersection																			
Traffic Control					1	1	DAYS	1	/ / / / / 1									0	1
Removing Pavement					18,900	18,900	SY	5000	/ / / / / 4									1	5
Storm Inlets and Manholes					16	16	EACH	5	/ / / / / 4									2	6
Storm Sewer and culverts					900	900	LF	250	/ / / / / 4									3	7
Common Excavation					15,290	15,290	CY	4000	/ / / / / 4									5	9
Embankment					4,510	4,510	CY	2000	/ / / / / 3									5	8
Breaker Run					13,980	13,980	TON	3000	/ / / / / 5									8	13
Lighting Conduit					980	980	LF	500	/ / / / / 2									12	14
CABC					16,300	16,300	TON	3300	/ / / / / 5									14	19
Concrete Curb and Gutter					5,935	5,935	LF	1200	/ / / / / 5									19	24
Concrete Truck Apron					535	535	SY	1000	/ / / / / 1									24	25
Lighting Bases					8	8	Each	4	/ / / / / 2									24	26
HMA Pavement					3,420	3,420	TON	1600	/ / / / / 3									26	29
Concrete Sidewalk/Driveways					17,410	17,410	SF	3000	/ / / / / 6									29	35
Asphalt Driveway					25	25	TON	320	/ / / / / 1									34	35
Aggregate Shoulders					210	210	TON	1000	/ / / / / 1									35	36
Marking and Signing					3	3	DAYS	1	/ / / / / 3									35	38
Topsoil and Restoration					10,250	10,250	SY	15000	/ / / / / 1									38	39

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
August	8/14/2020	8/31/2020	18	18		12	85	10	10
September	9/1/2020	9/30/2020	30	48		22	80	18	28
October	10/1/2020	10/21/2020	21	69		15	73	11	39
November			0	69		0	43	0	39
			0	69		0		0	39

REMARKS

Construct the CTH G roundabout with the intersection closed (~STA. 435+00 to STA. 446+00).

Calendar Days
Working Days
Completion Date
Prepared By

69
39
October 21, 2020

CONSTRUCTION YEAR: 2020

CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2011


Project ID 6430-12-71
Work Type Reconstruction

Highway STH 76
County Winnebago

Project Title USH 41 - CTH JJ
Project Limits STH 76 Divided Ends - CTH JJ

Date of Letting November 12, 2019
Probable Date of Beginning May 11, 2020

WIS 76: SOUTH LIMITS TO CTH GG

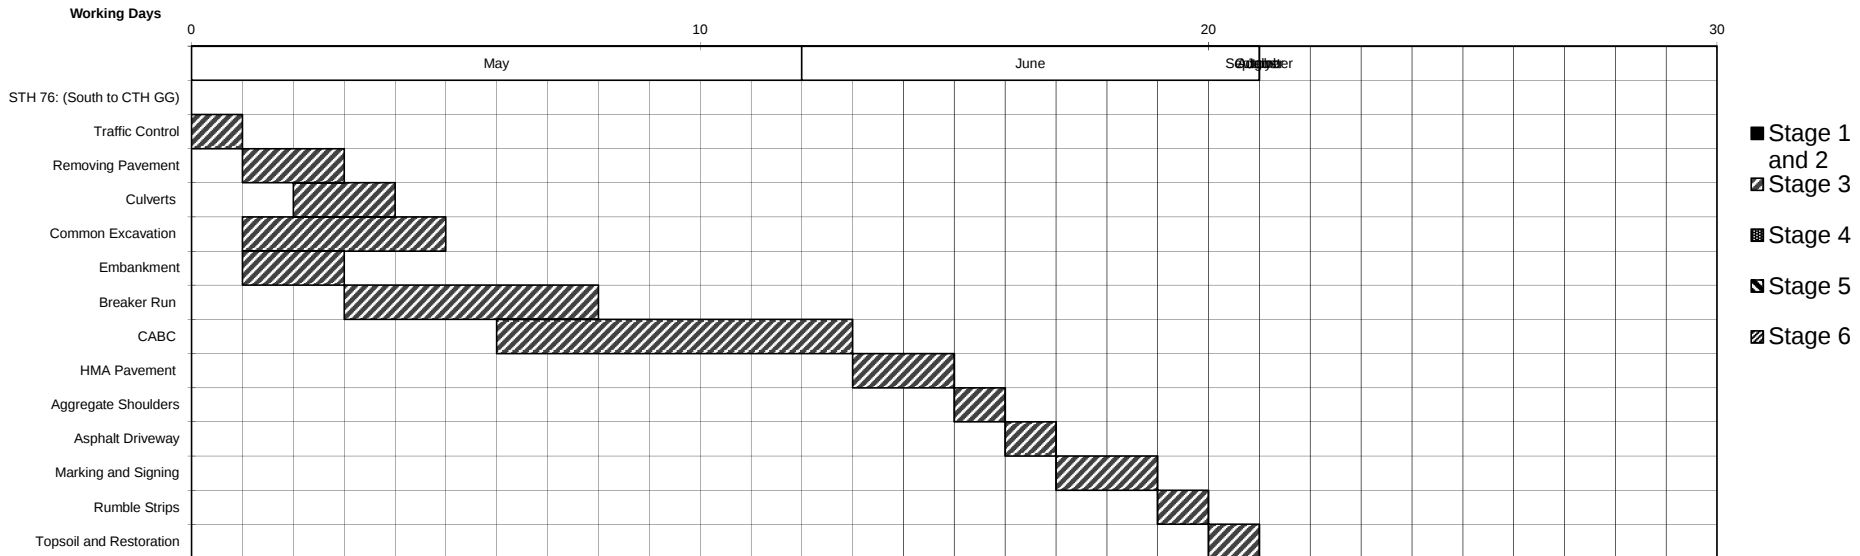

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1 and 2		Stage 3		Stage 4		Stage 5		Stage 6	
	Stage 1 and 2	Stage 3	Stage 4	Stage 5	Stage 6					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
STH 76: (South to CTH GG)																			
Traffic Control		1				1	DAYS	1	/ 1 / / /			0	1						
Removing Pavement		4,930				4,930	SY	4000	/ 2 / / /			1	3						
Culverts		410				410	LF	250	/ 2 / / /			2	4						
Common Excavation		12,400				12,400	CY	4000	/ 4 / / /			1	5						
Embankment		2,600				2,600	CY	2000	/ 2 / / /			1	3						
Breaker Run		11,270				11,270	TON	2500	/ 5 / / /			3	8						
CABC		17,050				17,050	TON	2500	/ 7 / / /			6	13						
HMA Pavement		3,200				3,200	TON	1600	/ 2 / / /			13	15						
Aggregate Shoulders		690				690	TON	1000	/ 1 / / /			15	16						
Asphalt Driveway		100				100	TON	250	/ 1 / / /			16	17						
Marking and Signing		2				2	DAYS	1	/ 2 / / /			17	19						
Rumble Strips		5,900				5,900	DAYS	60000	/ 1 / / /			19	20						
Topsoil and Restoration		10,440				10,440	SY	15000	/ 1 / / /			20	21						

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
April			0	0		0	58	0	0
May	5/11/2020	5/31/2020	21	21		15	80	12	12
June	6/1/2020	6/15/2020	15	36		11	80	9	21
July			0	36		0	85	0	21
August			0	36		0	85	0	21
September			0	36		0	80	0	21
October			0	36		0	73	0	21
			0	36		0		0	21
			0	36		0		0	21

REMARKS

Construct STH 76 from the south project limits to the CTH GG intersection(=STA. 304+83 to 329+00).

Calendar Days
Working Days
Completion Date
Prepared By

36
21
June 15, 2020

CONSTRUCTION YEAR: 2020

CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2011

Project ID 6430-12-71
Work Type Reconstruction


Highway STH 76
County Winnebago

Project Title USH 41 - CTH JJ
Project Limits STH 76 Divided Ends - CTH JJ

Date of Letting November 12, 2019
Probable Date of Beginning May 20, 2020

WIS 76: CTH GG TO CTH G

Working Days

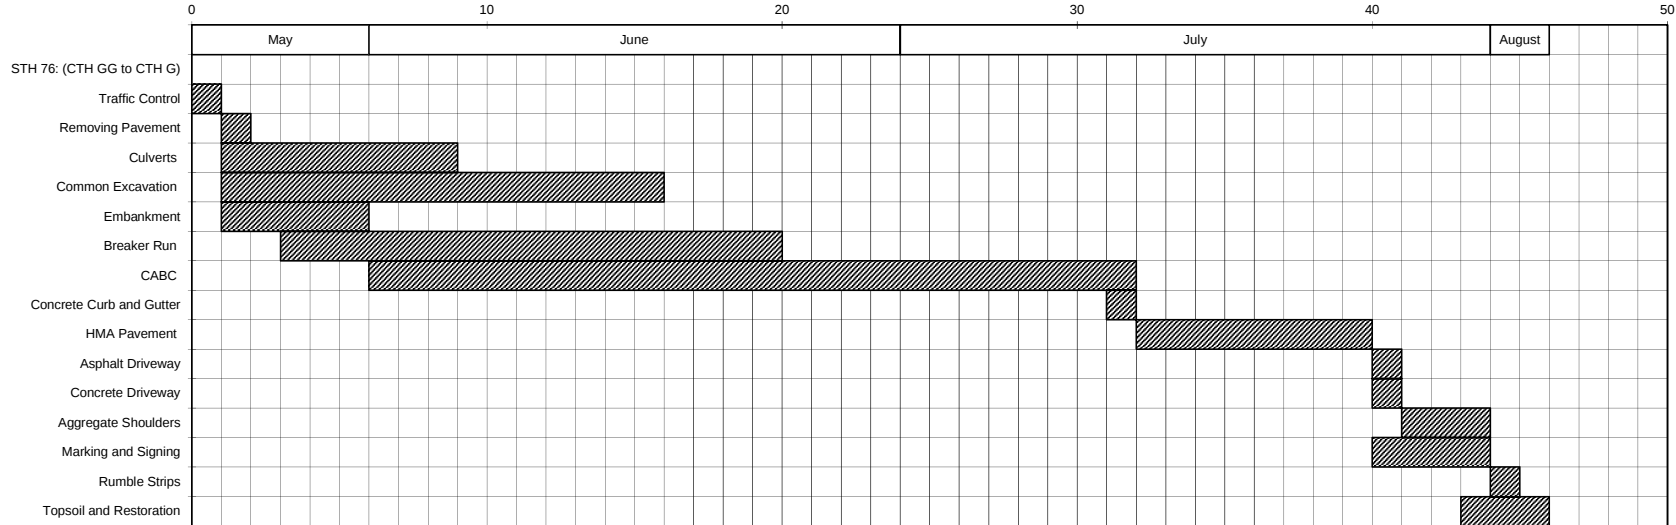

- Stage 1 and 2
- ▨ Stage 3
- ▩ Stage 4
- ▧ Stage 5
- ▦ Stage 6

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1 and 2		Stage 3		Stage 4		Stage 5		Stage 6	
	Stage 1 and 2	Stage 3	Stage 4	Stage 5	Stage 6					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
STH 76: (CTH GG to CTH G)																			
Traffic Control					1	1	DAYS	1	/ / / / 1									0	1
Removing Pavement					1,900	1,900	SY	4000	/ / / / 1									1	2
Culverts					1,820	1,820	LF	250	/ / / / 8									1	9
Common Excavation					58,950	58,950	CY	4000	/ / / / 15									1	16
Embankment					8,400	8,400	CY	2000	/ / / / 5									1	6
Breaker Run					41,020	41,020	TON	2500	/ / / / 17									3	20
CABC					64,860	64,860	TON	2500	/ / / / 26									6	32
Concrete Curb and Gutter					240	240	LF	1000	/ / / / 1									31	32
HMA Pavement					12,690	12,690	TON	1600	/ / / / 8									32	40
Asphalt Driveway					100	100	TON	250	/ / / / 1									40	41
Concrete Driveway					110	110	TON	250	/ / / / 1									40	41
Aggregate Shoulders					2,380	2,380	TON	1000	/ / / / 3									41	44
Marking and Signing					4	4	DAYS	1	/ / / / 4									40	44
Rumble Strips					19,300	19,300	DAYS	60000	/ / / / 1									44	45
Topsoil and Restoration					37,240	37,240	SY	15000	/ / / / 3									43	46

Month	Date		Days			Possible Work Days	Probable Working Days		Total
	Begin	End	Month	Total	Holiday		%	Month	
			0	0		0	0	0	0
			0	0		0	0	0	0
			0	0		0	58	0	0
			0	0		0	58	0	0
May	5/20/2020	5/31/2020	12	12		8	80	6	6
June	6/1/2020	6/30/2020	30	42		22	80	18	24
July	7/1/2020	7/31/2020	31	73		23	85	20	44
August	8/1/2020	8/4/2020	4	77		2	85	2	46
September			0	77		0	80	0	46
October			0	77		0	73	0	46
November			0	77		0	43	0	46
			0	77		0	0	0	46

REMARKS

Construct STH 76 from the CTH GG intersection to the CTH G intersection (~STA. 341+00 to 435+00).

Calendar Days
Working Days
Completion Date
Prepared By

77
46
August 4, 2020

CONSTRUCTION YEAR: 2020

CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2011


Project ID 6430-12-71
Work Type Reconstruction

Highway STH 76
County Winnebago

Project Title USH 41 - CTH JJ
Project Limits STH 76 Divided Ends - CTH JJ

Date of Letting November 12, 2019
Probable Date of Beginning August 29, 2020

WIS 76: CTH G TO CTH JJ

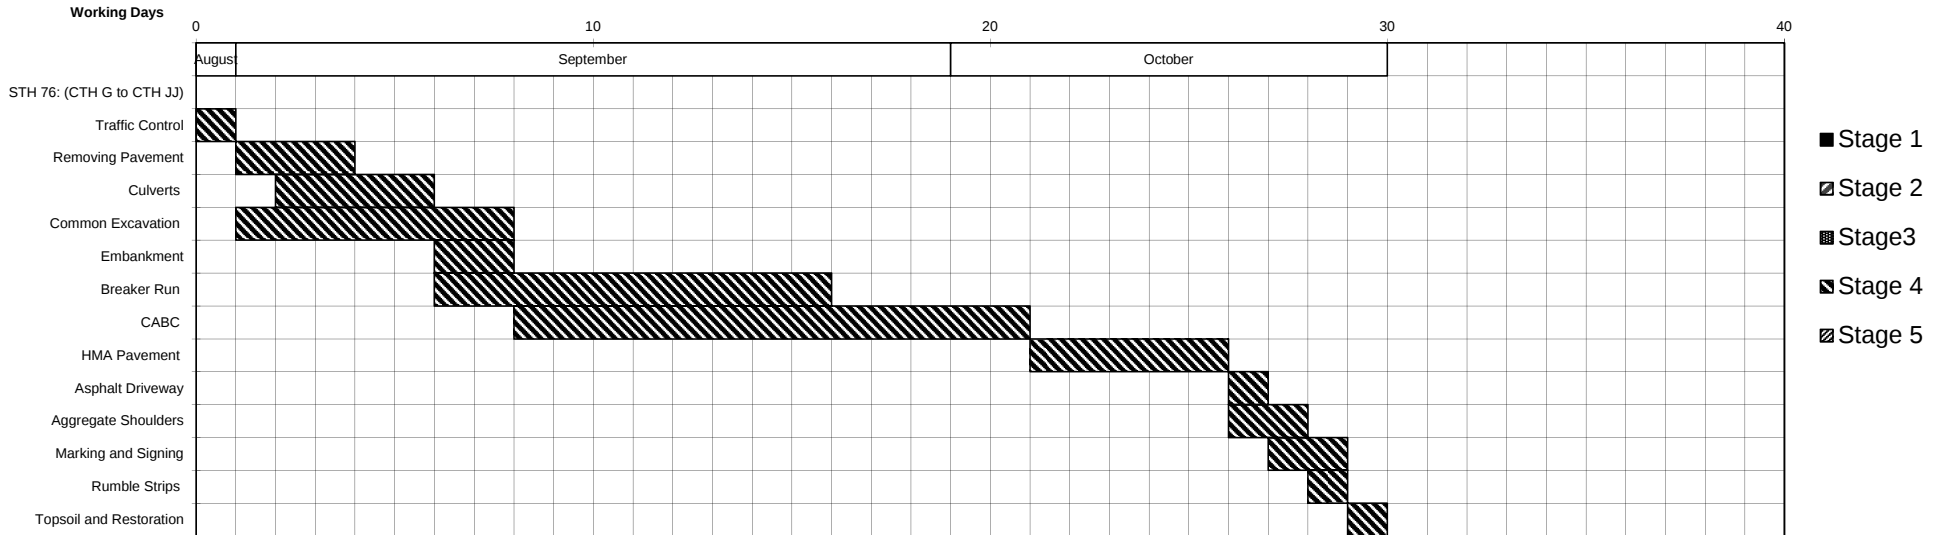

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5	
	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
STH 76: (CTH G to CTH JJ)																			
Traffic Control				1		1	DAYS	1	/ / / 1 /							0	1		
Removing Pavement				8,800		8,800	SY	4000	/ / / 3 /							1	4		
Culverts			960			960	LF	250	/ / / 4 /							2	6		
Common Excavation			24,500			24,500	CY	4000	/ / / 7 /							1	8		
Embankment			3,780			3,780	CY	2000	/ / / 2 /							6	8		
Breaker Run			24,230			24,230	TON	2500	/ / / 10 /							6	16		
CABC			35,220			35,220	TON	2800	/ / / 13 /							8	21		
HMA Pavement			7,230			7,230	TON	1600	/ / / 5 /							21	26		
Asphalt Driveway			185			185	TON	250	/ / / 1 /							26	27		
Aggregate Shoulders			1,180			1,180	TON	1000	/ / / 2 /							26	28		
Marking and Signing			2			2	DAYS	1	/ / / 2 /							27	29		
Rumble Strips			10,600			10,600	LF	60,000	/ / / 1 /							28	29		
Topsoil and Restoration			12,550			12,550	SY	15000	/ / / 1 /							29	30		

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
			0	0		0	58	0	0
			0	0		0	80	0	0
			0	0		0	80	0	0
			0	0		0	85	0	0
August	8/29/2020	8/31/2020	3	3		1	85	1	1
September	9/1/2020	9/30/2020	30	33		22	80	18	19
October	10/1/2020	10/21/2020	21	54		15	73	11	30
			0	54		0		0	30
			0	54		0		0	30

REMARKS

Construct STH 76 from CTH G to CTH JJ (~STA. 446+00 to 490+00).

Calendar Days
Working Days
Completion Date
Prepared By

54
30
October 21, 2020

CONSTRUCTION YEAR: 2020
