

CONTRACT TIME FOR COMPLETION


Wisconsin Department of Transportation DT1923 04/2011

Project ID 8357-01-72
Work Type Resurfacing/Minor Reconditioning

Highway Local Street
County Bayfield

Project Title T Russell, Little Sand Bay Road
Project Limits Old CTH K - Termini

Date of Letting August 8, 2017
Probable Date of Beginning September 18, 2017

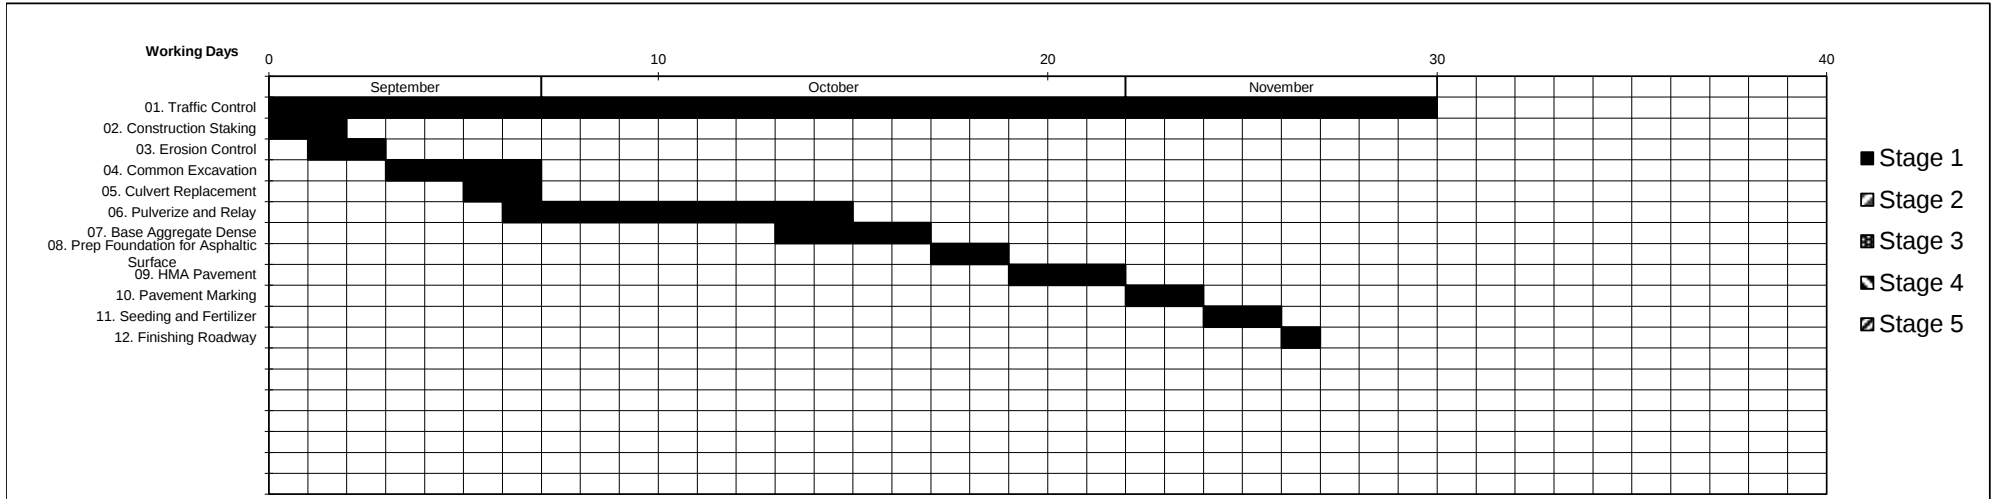

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5	
	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
01. Traffic Control	1					1	LS	0.034	30 / / / / /	0	30								
02. Construction Staking	13,890					13,890	LF	10000	2 / / / / /	0	2								
03. Erosion Control	1					1	LS	0.5	2 / / / / /	1	3								
04. Common Excavation	3,934					3,934	CY	1000	4 / / / / /	3	7								
05. Culvert Replacement	2					2	EACH	1	2 / / / / /	5	7								
06. Pulverize and Relay	43,185					43,185	SY	5000	9 / / / / /	6	15								
07. Base Aggregate Dense	11,050					11,050	TON	3000	4 / / / / /	13	17								
08. Prep Foundation for Asphaltic Surface	1					1	LS	0.5	2 / / / / /	17	19								
09. HMA Pavement	3,190					3,190	TON	1500	3 / / / / /	19	22								
10. Pavement Marking	41,640					41,640	LF	21000	2 / / / / /	22	24								
11. Seeding and Fertilizer	39,280					39,280	SY	20000	2 / / / / /	24	26								
12. Finishing Roadway	1					1	EACH	1	1 / / / / /	26	27								
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0	0	0	0
			0	0		0	0	0	0
			0	0		0	60	0	0
			0	0		0	60	0	0
			0	0		0	72	0	0
			0	0		0	80	0	0
			0	0		0	85	0	0
			0	0		0	85	0	0
September	9/18/2017	9/30/2017	13	13		10	72	7	7
October	10/1/2017	10/31/2017	31	44		22	70	15	22
November	11/1/2017	11/16/2017	16	60		12	65	8	30
			0	60		0	58	0	30

REMARKS

This project is a Completion Date Contract with a required completion date of November 16, 2017.

Calendar Days
Working Days
Completion Date
Prepared By

60
30
November 16, 2017
WAE

CONSTRUCTION YEAR: 2017
