


CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2011

Project ID	3240-17-60	Highway	STH 32	Project Title	STH 32 - STORM SEWER REPAIR	Date of Letting	May 12, 2020
Work Type	Storm Sewer Repair	County	KENOSHA	Project Limits	7th Place, 875 Sheridan Rd, 11th Pl	Probable Date of Beginning	July 6, 2020

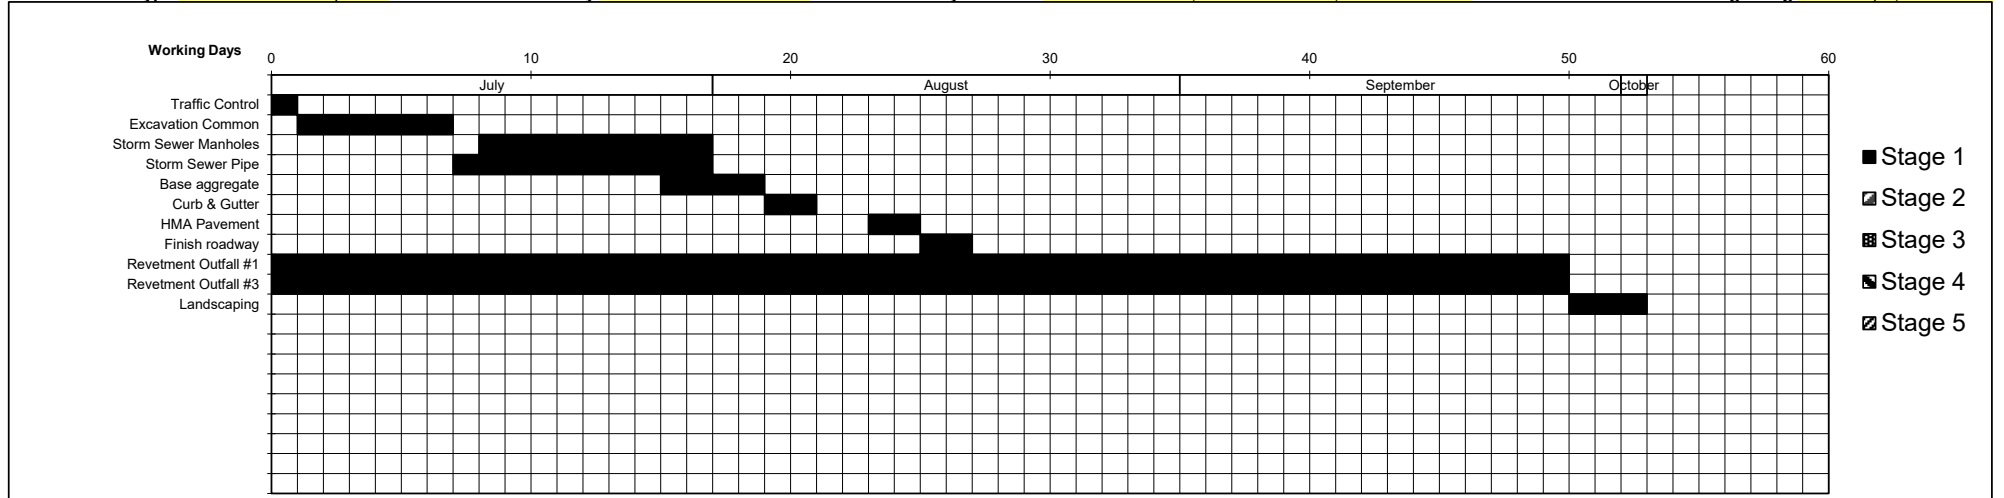

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5	
	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
Traffic Control	1					1	LS	1	1 / / / / /	0	1								
Excavation Common	2,012					2,012	CY	400	6 / / / / /	1	7								
Storm Sewer Manholes	9					9	EACH	1	9 / / / / /	8	17								
Storm Sewer Pipe	1,872					1,872	LF	200	10 / / / / /	7	17								
Base aggregate	1,602					1,602	TON	450	4 / / / / /	15	19								
Curb & Gutter	1,484					1,484	TON	850	2 / / / / /	19	21								
HMA Pavement	908					908	TON	730	2 / / / / /	23	25								
Finish roadway	1					1	LS	0.5	2 / / / / /	25	27								
Revetment Outfall #1	1					1	LS	0.02	50 / / / / /	0	50								
Revetment Outfall #3	1					1	LS	0.02	50 / / / / /	0	50								
Landscaping	6,129					6,129	SY	2100	3 / / / / /	50	53								
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
July	7/6/2020	7/31/2020	26	26		20	85	17	17
August	8/1/2020	8/31/2020	31	57		21	85	18	35
September	9/1/2020	9/30/2020	30	87		22	75	17	52
October	10/1/2020	10/1/2020	1	88		1	75	1	53
			0	88		0	50	0	53
			0	88		0	50	0	53

REMARKS

Calendar Days	88
Working Days	53
Completion Date	October 1, 2020
Prepared By	GRAEF

CONSTRUCTION YEAR: 2020
