

CONTRACT TIME FOR COMPLETION


Wisconsin Department of Transportation DT1923 04/2011

Project ID 1067-02-74
Work Type Bridge Replacement

Highway IH 94
County Jefferson

Project Title Lake Mills - Oconomowoc
Project Limits Hillside Drive Bridge, B-28-188

Date of Letting February 12, 2019
Probable Date of Beginning April 15, 2019

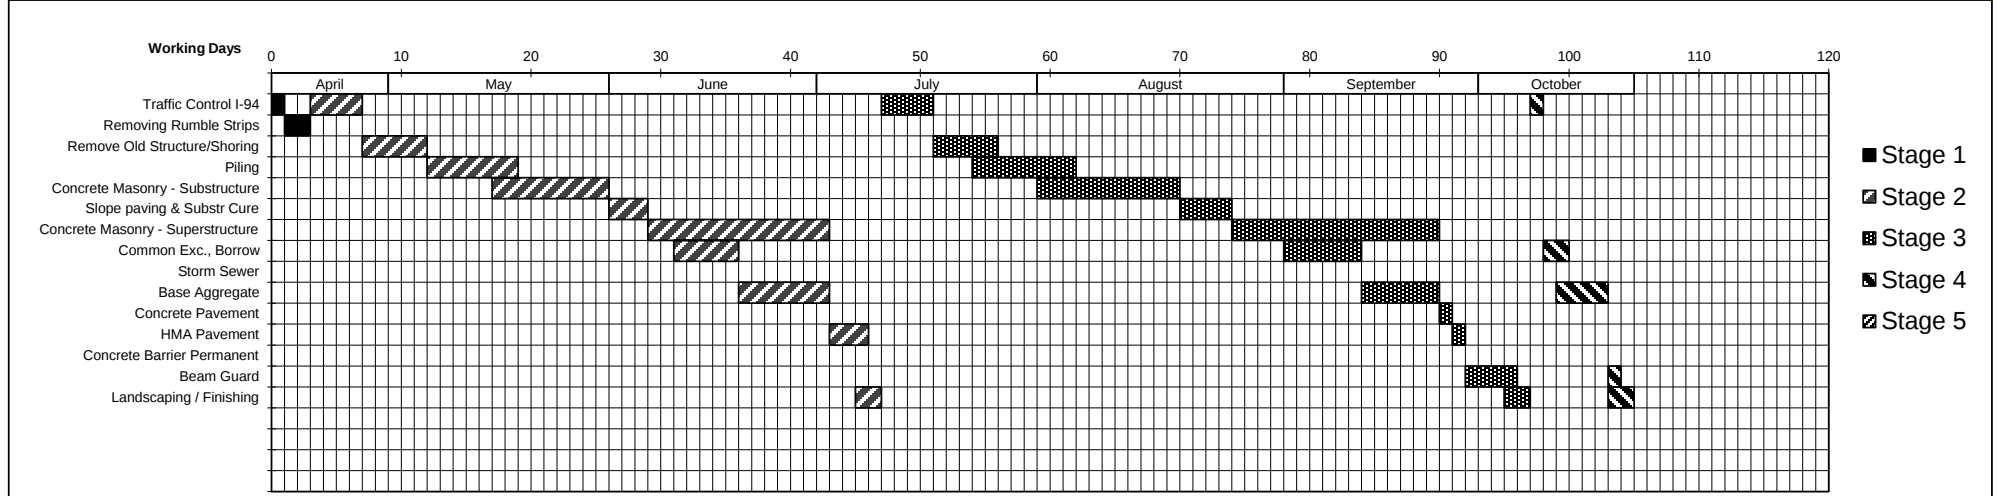

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5	
	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
Traffic Control I-94	0	1	1	0		3	LS	0.25	1 / 4 / 4 / 1 /	0	1	3	7	47	51	97	98		
Removing Rumble Strips	1	0	0	0		1	LS	0.5	2 / 0 / 0 / 0 /	1	3	7	7	51	51	98	98		
Remove Old Structure/Shoring		1	1	0		2	LS	0.2	/ 5 / 5 / 0 /			7	12	51	56	98	98		
Piling		2,470	3,020	0		5,490	LF	400	/ 7 / 8 / 0 /			12	19	54	62	98	98		
Concrete Masonry - Substructure		135	165	0		300	CY	15	/ 9 / 11 / 0 /			17	26	59	70	98	98		
Slope paving & Substr Cure		250	310	0		560	SY	100	/ 3 / 4 / 0 /			26	29	70	74	98	98		
Concrete Masonry - Superstructure		330	400	0		730	CY	25	/ 14 / 16 / 0 /			29	43	74	90	98	98		
Common Exc., Borrow		4,809	5,723	1,008		11,540	CY	1000	/ 5 / 6 / 2 /			31	36	78	84	98	100		
Storm Sewer		0	0	0		0	LS	250	/ 0 / 0 / 0 /			36	36	84	84	100	100		
Base Aggregate		16,380	13,670	9,380		39,430	TON	2500	/ 7 / 6 / 4 /			36	43	84	90	99	103		
Concrete Pavement		0	4,424	0		4,424	SY	5000	/ 0 / 1 / 0 /			43	43	90	91	103	103		
HMA Pavement		3,050	870	0		3,920	TON	1200	/ 3 / 1 / 0 /			43	46	91	92	103	103		
Concrete Barrier Permanent		0	0	0		0	LF	500	/ 0 / 0 / 0 /			46	46	92	92	103	103		
Beam Guard		0	1,850	265		2,115	LF	500	/ 0 / 4 / 1 /			46	46	92	96	103	104		
Landscaping / Finishing		1	1	1		3	LS	0.5	/ 2 / 2 / 2 /			45	47	95	97	103	105		
									/ / / /										
									/ / / /										
									/ / / /										
									/ / / /										

Month	Date		Days			Possible Work Days	Probable Working Days	
	Begin	End	Month	Total	Holiday		%	Month Total
			0	0		0		0
			0	0		0		0
April	4/15/2019	4/30/2019	16	16		12	77	9
May	5/1/2019	5/31/2019	31	47	2	21	80	17
June	6/1/2019	6/30/2019	30	77		20	80	16
July	7/1/2019	7/31/2019	31	108	3	20	85	17
August	8/1/2019	8/31/2019	31	139		22	85	19
September	9/1/2019	9/30/2019	30	169	2	19	80	15
October	10/1/2019	10/22/2019	22	191		16	73	12
			0	191		0		0
			0	191		0		0
			0	191		0		0

REMARKS

Completion date 10/20/19 or 105 working days??
 Stage 1 - Removing Rumble Strips
 Stage 2 - construct median portion
 Stage 3 - construct outside portion
 Stage 4 - remove temporary median

Calendar Days 191
Working Days 105
Completion Date
Prepared By OMNNI Associates

CONSTRUCTION YEAR: 2019
