

CONTRACT TIME FOR COMPLETION


Wisconsin Department of Transportation DT1923 04/2011

Project ID 3080-09-60, 3080-09-61
Work Type Resurfacing

Highway USH 18
County Jefferson

Project Title Jefferson - Wales
Project Limits CTH Y to Gruennert Street and
Helenville Rd to W Limit V Sullivan

Date of Letting May 14, 2019
Probable Date of Beginning June 25, 2019

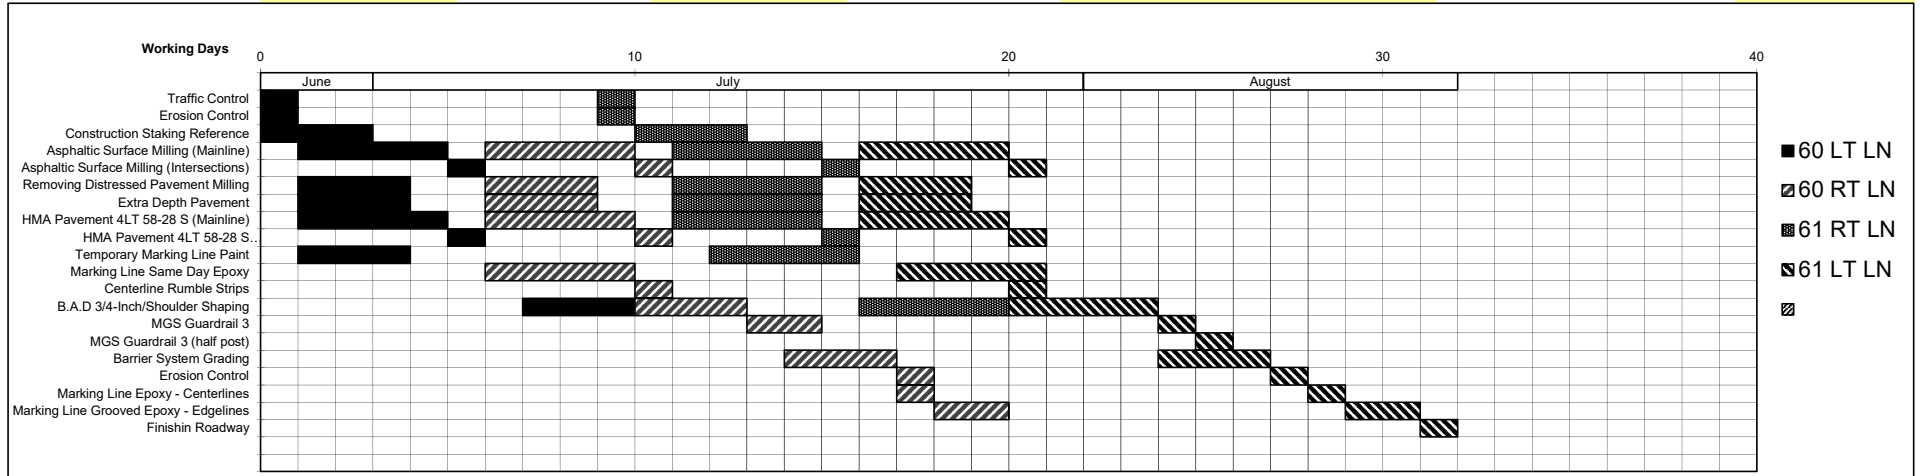

ITEM ANALYSIS

Item	Contract Quantity per Stage				Total Quantity	Unit	Production Rate	Working Days (per Stage)	60 LT LN		60 RT LN		61 RT LN		61 LT LN			
	60 LT LN	60 RT LN	61 RT LN	61 LT LN					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
Traffic Control	1		1		2	DAYS	1	1 / / 1 / /	0	1			9	10				
Erosion Control	1		1		2	DAYS	1	1 / / 1 / /	0	1			9	10				
Construction Staking Reference	3		3		6	DAYS	1	3 / / 3 / /	0	3			10	13				
Asphaltic Surface Milling (Mainline)	38,585	38,585	44,803	44,348	166,321	SY	12000	4 / 4 / 4 / 4 /	1	5	6	10	11	15	16	20		
Asphaltic Surface Milling (Intersections)	1,970	660	2,014	1,658	6,302	SY	9000	1 / 1 / 1 / 1 /	5	6	10	11	15	16	20	21		
Removing Distressed Pavement Milling	7,390	7,390	12,006	8,269	35,055	SY	3500	3 / 3 / 4 / 3 /	1	4	6	9	11	15	16	19		
Extra Depth Pavement	845	845	1,346	927	3,963	TON	400	3 / 3 / 4 / 3 /	1	4	6	9	11	15	16	19		
HMA Pavement 4LT 58-28 S (Mainline)	4,125	4,125	5,114	5,049	18,413	TON	1300	4 / 4 / 4 / 4 /	1	5	6	10	11	15	16	20		
HMA Pavement 4LT 58-28 S (Intersections)	200	200	226	186	812	TON	500	1 / 1 / 1 / 1 /	5	6	10	11	15	16	20	21		
Temporary Marking Line Paint	26,640		32,324		58,964	LF	10000	3 / / 4 / /	1	4			12	16				
Marking Line Same Day Epoxy		30,330		32,324	62,654	LF	10000	/ 4 / / 4 /			6	10			17	21		
Centerline Rumble Strips		21,725		23,518	45,243	LF	30000	/ 1 / / 1 /			10	11			20	21		
B.A.D 3/4-Inch/Shoulder Shaping	1,125	1,125	1,533	1,485	5,268	TON	470	3 / 3 / 4 / 4 /	7	10	10	13	16	20	20	24		
MGS Guardrail 3		710		312.5	1,022.5	LF	430	/ 2 / / 1 /			13	15			24	25		
MGS Guardrail 3 (half post)				112.5	112.5	LF	215	/ / / 1 /							25	26		
Barrier System Grading		3		3	6	DAYS	1	/ 3 / / 3 /			14	17			24	27		
Erosion Control		1		1	2	DAYS	1	/ 1 / / 1 /			17	18			27	28		
Marking Line Epoxy - Centerlines		27,160		32,543	59,703	LF	50000	/ 1 / / 1 /			17	18			28	29		
Marking Line Grooved Epoxy - Edgelines		43,450		51,409	94,859	LF	30000	/ 2 / / 2 /			18	20			29	31		
Finishin Roadway				1	1	DAYS	1	/ / / 1 /							31	32		
								/ / / / /										

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
June	6/25/2019	6/30/2019	6	6		4	81	3	3
July	7/1/2019	7/31/2019	31	37	1	22	85	19	22
August	8/1/2019	8/16/2019	16	53		12	85	10	32
			0	53		0		0	32
			0	53		0		0	32
			0	53		0		0	32
			0	53		0		0	32

REMARKS

Calendar Days 53
Working Days 32
Completion Date
Prepared By TJD

CONSTRUCTION YEAR: 2019
