

CONTRACT TIME FOR COMPLETION


Wisconsin Department of Transportation DT1923 04/2020

Project ID 5215-03-80
Work Type Bridge Replacement

Highway STH 81
County Grant

Project Title Cassville - Lancaster
Project Limits Hackett Branch Bridge, B-22-292

Date of Letting August 10, 2021
Probable Date of Beginning June 16, 2022

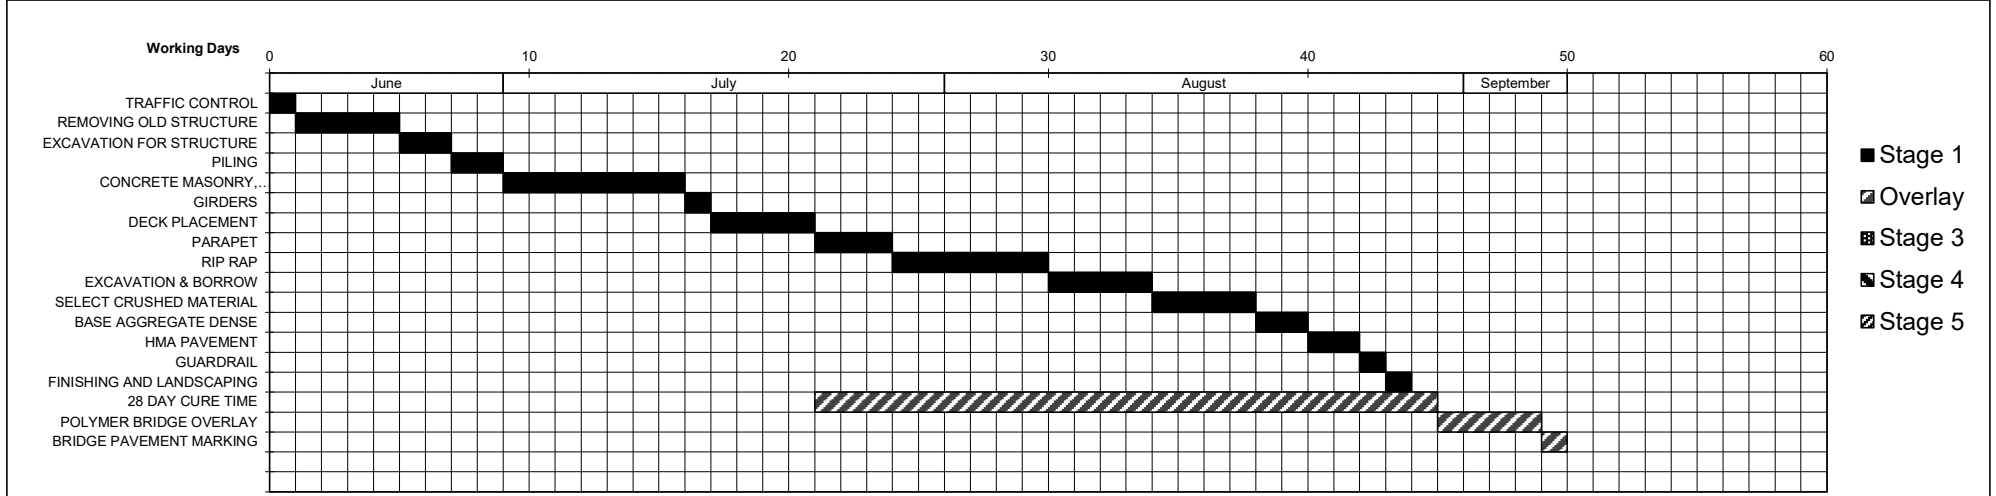

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Overlay		Stage 3		Stage 4		Stage 5	
	Stage 1	Overlay	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
TRAFFIC CONTROL	1					1	LS	1	1 / / / / /	0	1								
REMOVING OLD STRUCTURE	1					1	LS	0.25	4 / / / / /	1	5								
EXCAVATION FOR STRUCTURE	1					1	LS	0.5	2 / / / / /	5	7								
PILING	480					480	LF	300	2 / / / / /	7	9								
CONCRETE MASONRY, SUBSTR	100					100	CY	15	7 / / / / /	9	16								
GIRDERS	6					6	EACH	6	1 / / / / /	16	17								
DECK PLACEMENT	3,696					3,696	SF	1000	4 / / / / /	17	21								
PARAPET	188					188	LF	75	3 / / / / /	21	24								
RIP RAP	510					510	SY	100	6 / / / / /	24	30								
EXCAVATION & BORROW	2,914					2,914	CY	900	4 / / / / /	30	34								
SELECT CRUSHED MATERIAL	2,467					2,467	TON	800	4 / / / / /	34	38								
BASE AGGREGATE DENSE	1,340					1,340	TON	800	2 / / / / /	38	40								
HMA PAVEMENT	485					485	TON	400	2 / / / / /	40	42								
GUARDRAIL	608					608	LF	620	1 / / / / /	42	43								
FINISHING AND LANDSCAPING	1					1	LS	1	1 / / / / /	43	44								
28 DAY CURE TIME		28				28	LS	1.2	/ 24 / / / /			21	45						
POLYMER BRIDGE OVERLAY		1				1	LS	0.25	/ 4 / / / /			45	49						
BRIDGE PAVEMENT MARKING		1				1	LS	1	/ 1 / / / /			49	50						
									/ / / / /										

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	80	0	0
June	6/16/2022	6/30/2022	15	15		11	80	9	9
July	7/1/2022	7/31/2022	31	46	1	20	85	17	26
August	8/1/2022	8/31/2022	31	77		23	85	20	46
September	9/1/2022	9/9/2022	9	86	1	6	70	4	50
			0	86		0	50	0	50
			0	86		0	50	0	50
			0	86		0	50	0	50

REMARKS

Note: Contract work cannot begin before 7:00 AM Thursday, June 16, 2022 except to complete installation of bird deterrent system at B-22-0827. A conditional notice to start contract work will be required for installation of bird deterrent system since it is required to be installed before April 15, 2022. All instream work that could adversely impact water quality should be completed after June 15. Contract time rounded to nearest five days.

☐ Contract Work Type
☐ Calendar Days
☒ Working Days
☐ Completion Date
 Prepared By

86
 50
 September 9, 2022
 Strand Associates, Inc.

CONSTRUCTION YEAR: 2022
