


CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2020

Project ID	1112-06-74	Highway	USH 151	Project Title	Beaver Dam - Fond Du Lac	Date of Letting	August 10, 2021
Work Type	Resurfacing	County	Dodge & Fond Du Lac	Project Limits	STH 49 Interchange	Probable Date of Beginning	April 4, 2022

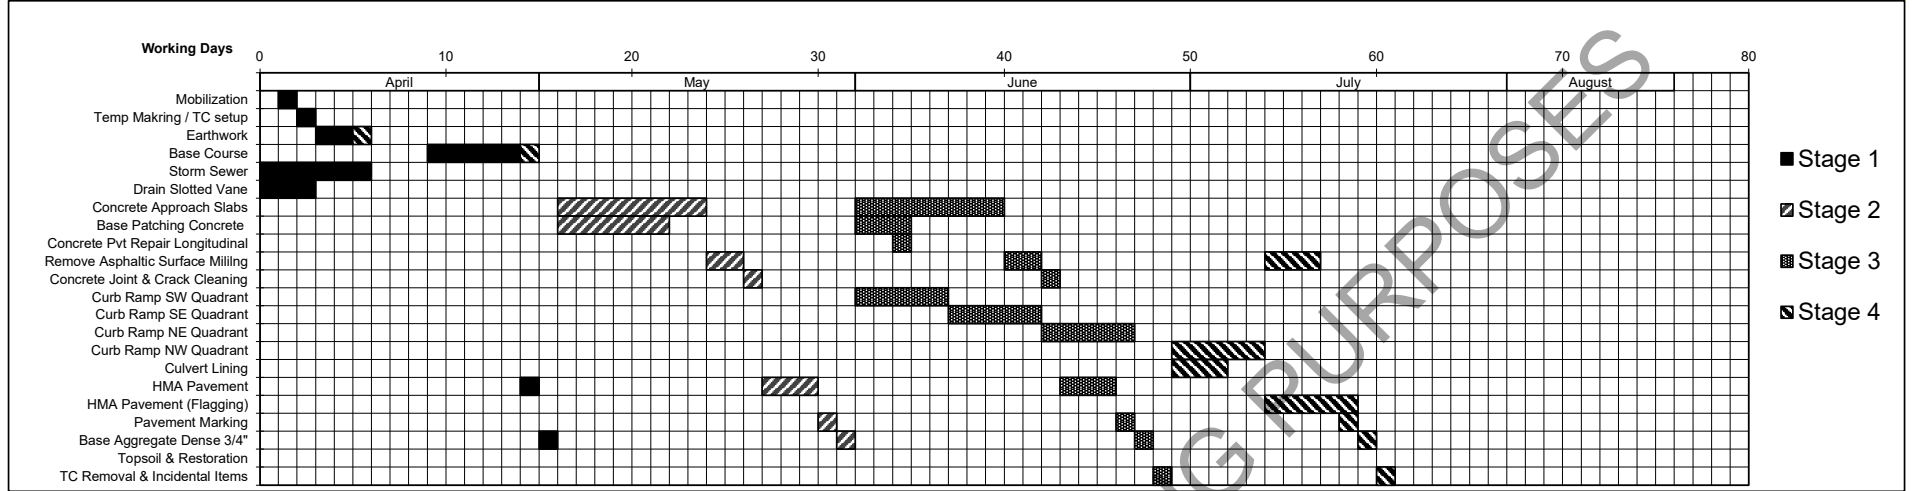

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5	
	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
Mobilization	1					1	Day	1	1 / / / / /	1	2								
Temp Makring / TC setup	15,200					15,200	LF	40000	1 / / / / /	2	3								
Earthwork	4,140			222		4,362	CY	3000	2 / / / 1 /	3	5								
Base Course	4,248			369		4,617	TON	1000	5 / / / 1 /	9	14								
Storm Sewer	881					881	LF	150	6 / / / / /	3	9								
Drain Slotted Vane	407					407	LF	150	3	6	9								
Concrete Approach Slabs		144	155			299	Day	20	/ 8 / 8 / /			16	24	32	40				
Base Patching Concrete		1,920	960			2,880	SY	380	/ 6 / 3 / /			16	22	32	35				
Concrete Pvt Repair Longitudinal			1,040			1,040	LF	1040	/ / 1 / /					34	35				
Remove Asphaltic Surface Milling		22,016	20,362	33,524		75,902	SY	12000	/ 2 / 2 / 3 /			24	26	40	42	54	57		
Concrete Joint & Crack Cleaning		600	780			1,380	LF	3000	/ 1 / 1 / /			26	27	42	43				
Curb Ramp SW Quadrant			5			5	Day	1	/ / 5 / /					32	37				
Curb Ramp SE Quadrant			5			5	Day	1	/ / 5 / /					37	42				
Curb Ramp NE Quadrant			5			5	Day	1	/ / 5 / /					42	47				
Curb Ramp NW Quadrant				5		5	Day	1	/ / / 5 /							49	54		
Culvert Lining				100		100	LF	34	/ / / 3 /							49	52		
HMA Pavement	1,327	3,702	3,424			8,453	TON	1400	1 / 3 / 3 / /	14	15	27	30	43	46				
HMA Pavement (Flagging)				3,873		3,873	TON	800	/ / / 5 /							54	59		
Pavement Marking		20,000	20,000	25,000		65,000	LF	60000	/ 1 / 1 / 1 /			30	31	46	47	58	59		
Base Aggregate Dense 3/4"	936	251	249	36		1,472	TON	1500	1 / 1 / 1 / 1 /	15	16	31	32	47	48	59	60		
Topsoil & Restoration							SY	7000	/ / / / /										
TC Removal & Incidental Items			1	1		2	EACH	1	/ / 1 / 1 /					48	49	60	61		

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
April	4/4/2022	4/30/2022	27	27		20	75	15	15
May	5/1/2022	5/31/2022	31	58	1	21	80	17	32
June	6/1/2022	6/30/2022	30	88		22	80	18	50
July	7/1/2022	7/31/2022	31	119	1	20	85	17	67
August	8/1/2022	8/15/2022	15	134		11	85	9	76
			0	134		0		0	76
			0	134		0		0	76
			0	134		0		0	76
			0	134		0		0	76

REMARKS

Per FDM 19.-10-30.2, rounded to the nearest 5 days.
 Stage 1: Build crossovers under single lane closures adjacent to traffic
 Stage 2: removal & paving operations NB USH 151
 Stage 3: removal & paving operations SB USH 151 and start STH 49 curb ramp work
 Stage 4: Finalize pavement marking on USH 151 and complete remaining STH 49 work
Contract Work Type
☐ Calendar Days
☒ Working Days
☐ Completion Date
 Prepared By Michael Liska

CONSTRUCTION YEAR: 2022
