

CONTRACT TIME FOR COMPLETION


Wisconsin Department of Transportation DT1923 04/2020

Project ID 4867-01-70
Work Type Bridge Replacement

Highway CTH H
County Washington

Project Title CTH H
Project Limits Bridge Over Milwaukee River B660655

Date of Letting August 10, 2021
Probable Date of Beginning November 1, 2021

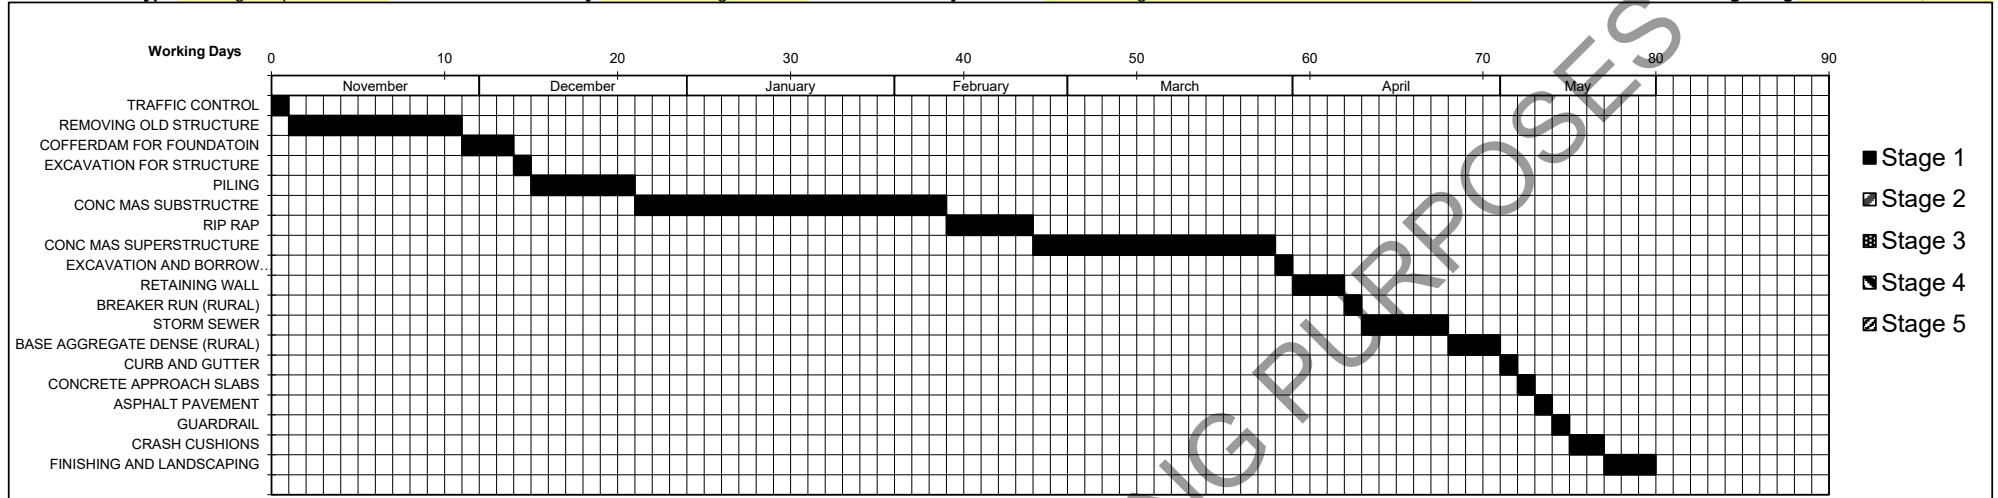

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5	
	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
TRAFFIC CONTROL	1					1	LS	1	1 / / / / /	0	1								
REMOVING OLD STRUCTURE	1					1	LS	0.1	10 / / / / /	1	11								
COFFERDAM FOR FOUNDATION	1,920					1,920	SF	650	3 / / / / /	11	14								
EXCAVATION FOR STRUCTURE	400					400	CY	500	1 / / / / /	14	15								
PILING	1,560					1,560	LF	300	6 / / / / /	15	21								
CONC MAS SUBSTRUCTURE	212					212	CY	12	18 / / / / /	21	39								
RIP RAP	360					360	CY	75	5 / / / / /	39	44								
CONC MAS SUPERSTRUCTURE	8,257					8,257	SF	600	14 / / / / /	44	58								
EXCAVATION AND BORROWING	454					454	CY	1000	1 / / / / /	58	59								
RETAINING WALL	90					90	LF	30	3 / / / / /	59	62								
BREAKER RUN (RURAL)	14					14	TON	700	1 / / / / /	62	63								
STORM SEWER	352					352	LF	75	5 / / / / /	63	68								
BASE AGGREGATE DENSE (RURAL)	1,029					1,029	TON	500	3 / / / / /	68	71								
CURB AND GUTTER	124					124	LF	400	1 / / / / /	71	72								
CONCRETE APPROACH SLABS	76					76	SY	1200	1 / / / / /	72	73								
ASPHALT PAVEMENT	216					216	TON	700	1 / / / / /	73	74								
GUARDRAIL	72					72	LF	250	1 / / / / /	74	75								
CRASH CUSHIONS	2					2	EACH	1	2 / / / / /	75	77								
FINISHING AND LANDSCAPING	459					459	SY	200	3 / / / / /	77	80								

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0		0	0
November	11/1/2021	11/30/2021	30	30	2	20	60	12	12
December	12/1/2021	12/31/2021	31	61	2	21	58	12	24
January	1/1/2022	1/31/2022	31	92	1	20	58	12	36
February	2/1/2022	2/28/2022	28	120		20	50	10	46
March	3/1/2022	3/31/2022	31	151		23	58	13	59
April	4/1/2022	4/30/2022	30	181		21	58	12	71
May	5/1/2022	5/18/2022	18	199		13	68	9	80
			0	199		0		0	80
			0	199		0		0	80
			0	199		0		0	80
			0	199		0		0	80

REMARKS

Instream work is not allowed from March 1 to June 1.

☐ Contract Work Type
☐ Calendar Days
☐ Working Days
☒ Completion Date
Prepared By

May 18, 2022
Strand Associates, Inc.

CONSTRUCTION YEAR: 2021
