

CONTRACT TIME FOR COMPLETION


Wisconsin Department of Transportation DT1923 04/2020

Project ID 1641-03-75
Work Type Reconditioning

Highway USH 14
County La Crosse

Project Title C La Crosse, Intersection Imprvmnts
Project Limits Mormon Coulee Rd / Broadview Pl Inter

Date of Letting September 14, 2021
Probable Date of Beginning April 4, 2022

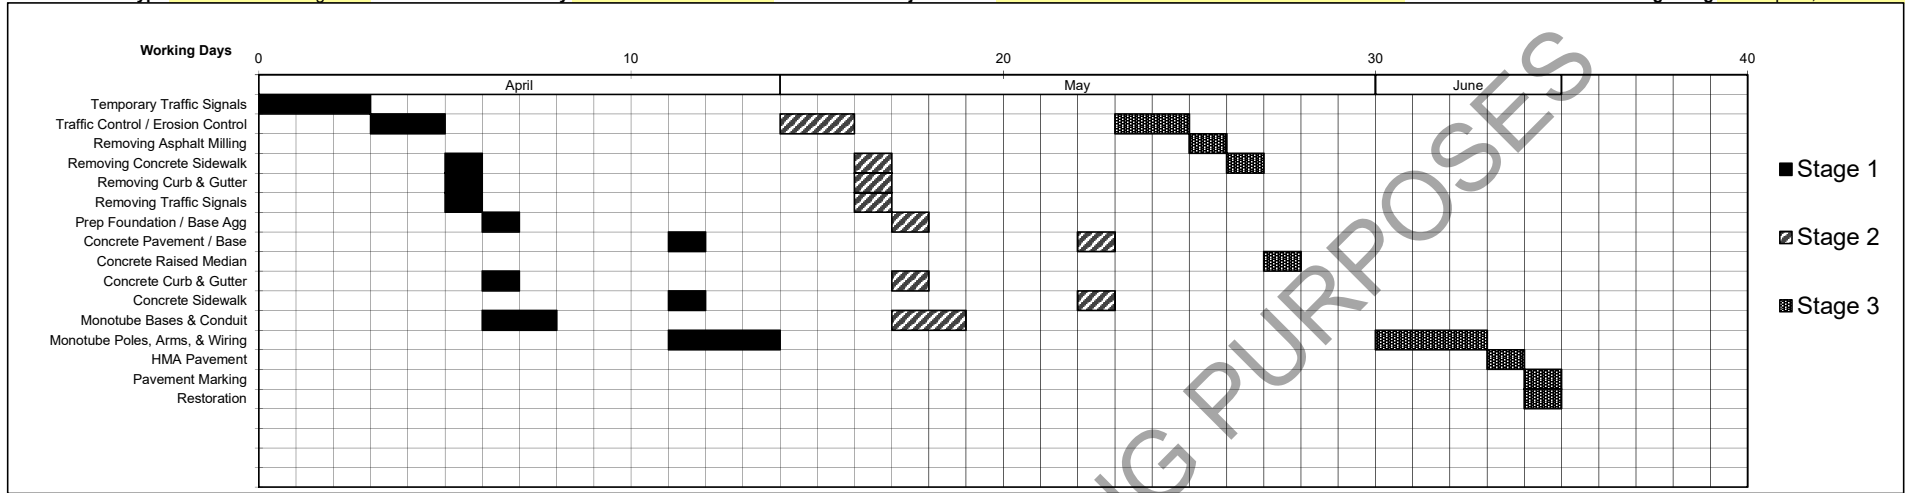

ITEM ANALYSIS

Item	Contract Quantity per Stage				Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3					
	Stage 1	Stage 2	Stage 3						Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
Temporary Traffic Signals	3				3	DAYS	1	3 / / / /	0	3								
Traffic Control / Erosion Control	2	2	2		6	DAYS	1	2 / 2 / 2 / /	3	5	14	16	23	25				
Removing Asphalt Milling			69		69	SY	600	/ / / 1 / /					25	26				
Removing Concrete Sidewalk	32	23	143		198	SY	600	1 / 1 / 1 / /	5	6	16	17	26	27				
Removing Curb & Gutter	31	38			69	LF	2000	1 / 1 / / / /	5	6	16	17						
Removing Traffic Signals	1	1			2	DAYS	1	1 / 1 / / / /	5	6	16	17						
Prep Foundation / Base Agg	9	9			18	TON	400	1 / 1 / / / /	6	7	17	18						
Concrete Pavement / Base	12	12			24	SY	1200	1 / 1 / / / /	11	12	22	23						
Concrete Raised Median			712		712	SF	860	/ / / 1 / /					27	28				
Concrete Curb & Gutter	31	38			69	LF	400	1 / 1 / / / /	6	7	17	18						
Concrete Sidewalk	326	307			633	SF	860	1 / 1 / / / /	11	12	22	23						
Monotube Bases & Conduit	2	2			4	DAYS	1	2 / 2 / / / /	6	8	17	19						
Monotube Poles, Arms, & Wiring	3		3		6	DAYS	1	3 / / 3 / / /	11	14			30	33				
HMA Pavement			28		28	TON	730	/ / 1 / / /					33	34				
Pavement Marking			543		543	LF	5000	/ / 1 / / /					34	35				
Restoration			9		9	SY	480	/ / 1 / / /					34	35				
								/ / / / /										
								/ / / / /										
								/ / / / /										
								/ / / / /										

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
April	4/4/2022	4/30/2022	27	27		20	70	14	14
May	5/1/2022	5/31/2022	31	58	1	21	75	16	30
June	6/1/2022	6/8/2022	8	66		6	85	5	35
			0	66		0		0	35
			0	66		0		0	35
			0	66		0		0	35
			0	66		0		0	35
			0	66		0		0	35
			0	66		0		0	35

REMARKS

Traffic control will be staged with one quadrant of the intersection completed at a time in stages 1 and 2 and the median completed in stage 3. Work in all stages consists of concrete sidewalk and curb & gutter removal and replacement. Work in stage 3 also consists of asphaltic surface milling, concrete base patches, and asphalt overlay.

☐ Contract Work Type
☐ Calendar Days
☐ Working Days
☒ Completion Date
 Prepared By

66
 35
 June 8, 2022
 raSmith

CONSTRUCTION YEAR: 2022
