

CONTRACT TIME FOR COMPLETION


Wisconsin Department of Transportation DT1923 04/2020

Project ID 1590-18-61 & 62
Work Type surfacing/Bridge Rehabilitation

Highway USH 8
County Forest

Project Title Monico - Laona
Project Limits Oneida County Line to Boulevard Avenue

Date of Letting September 14, 2021
Probable Date of Beginning March 14, 2022

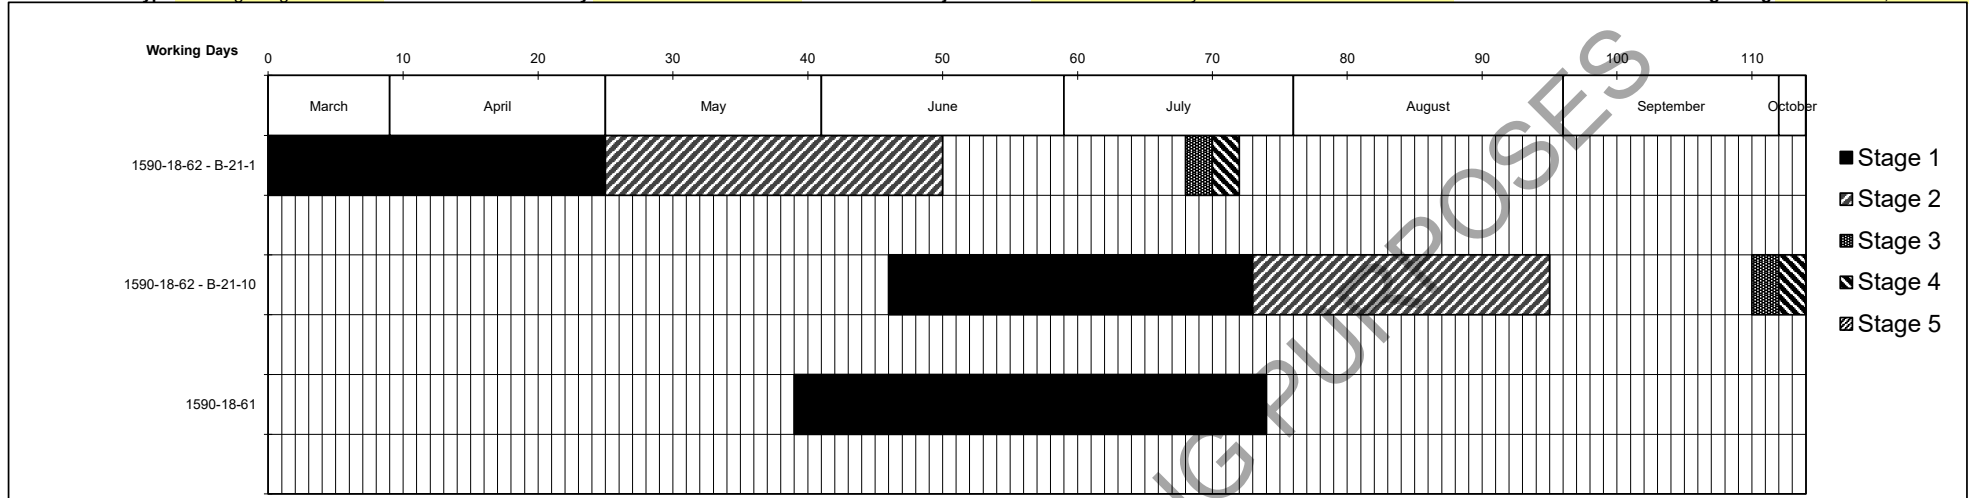

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5	
	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
1590-18-62 - B-21-1	25	25	2	2		54	DAYS	1	25 / 25 / 2 / 2 /	0	25	25	50	68	70	70	72		
1590-18-62 - B-21-10	27	22	2	2		53	DAYS	1	27 / 22 / 2 / 2 /	46	73	73	95	110	112	112	114		
1590-18-61	35					35	DAYS	1	35 / / / / /	39	74								

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0	0	0	0
			0	0		0	0	0	0
March	3/14/2022	3/31/2022	18	18		14	65	9	9
April	4/1/2022	4/30/2022	30	48		21	77	16	25
May	5/1/2022	5/31/2022	31	79	1.5	21	80	16	41
June	6/1/2022	6/30/2022	30	109		22	81	18	59
July	7/1/2022	7/31/2022	31	140	1.5	20	85	17	76
August	8/1/2022	8/31/2022	31	171		23	85	20	96
September	9/1/2022	9/30/2022	30	201	1.5	21	80	16	112
October	10/1/2022	10/6/2022	6	207		4	50	2	114
			0	207		0		0	114
			0	207		0		0	114

REMARKS

Construction to take place in 2022 construction season with a contract completion time of 100 Working Days. Friday afternoons where work is not allowed for Memorial Day and Independence Day are included as a 1/2 day holiday. Proposed improvements include bridge rehabilitation, mill and overlay, culvert and ditch cleaning, culvert replacements, gravel shouldering, pavement marking, rumble strips, and restoration.

Contract Work Type
☐ Calendar Days
☒ Working Days
☐ Completion Date
 Prepared By

205
100
October 6, 2022
CBS2 / jwm

CONSTRUCTION YEAR: 2022

CONTRACT TIME FOR COMPLETION


Wisconsin Department of Transportation DT1923 04/2020

Project ID 1590-18-62
Work Type Bridge Rehabilitation B-21-1

Highway USH 8
County Forest

Project Title Monico - Laona
Project Limits Wolf & Peshtigo Bridges B-21-1,10

Date of Letting September 14, 2021
Probable Date of Beginning March 14, 2022

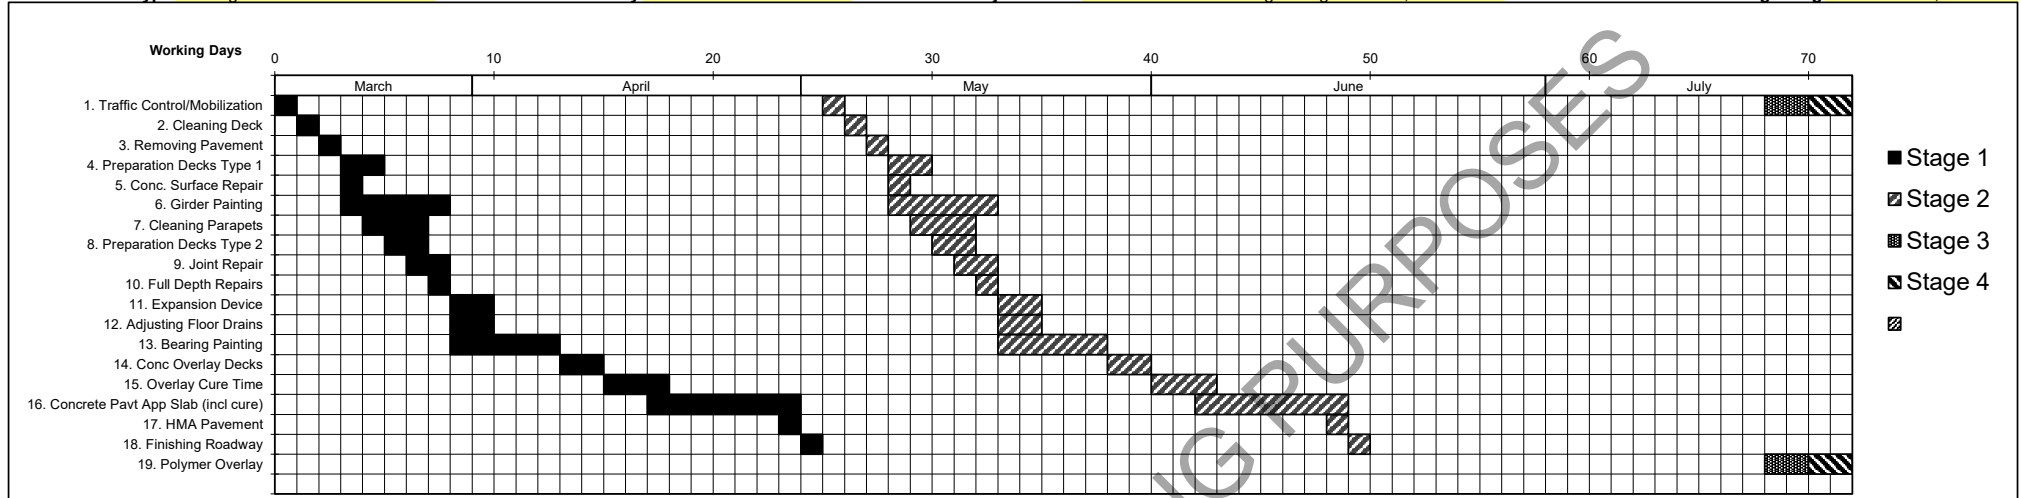

ITEM ANALYSIS

Item	Contract Quantity per Stage				Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4			
	Stage 1	Stage 2	Stage 3	Stage 4					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
1. Traffic Control/Mobilization	1	1	2	2	6	LS	1	1 / 1 / 2 / 2 /	0	1	25	26	68	70	70	72		
2. Cleaning Deck	255	255			510	SY	500	1 / 1 / / / /	1	2	26	27						
3. Removing Pavement	93	95			188	SY	200	1 / 1 / / / /	2	3	27	28						
4. Preparation Decks Type 1	26	26			52	SY	20	2 / 2 / / / /	3	5	28	30						
5. Conc. Surface Repair	10	10			20	SF	950	1 / 1 / / / /	3	4	28	29						
6. Girder Painting	1	1			2	EACH	0.2	5 / 5 / / / /	3	8	28	33						
7. Cleaning Parapets	140	140			280	LF	60	3 / 3 / / / /	4	7	29	32						
8. Preparation Decks Type 2	13	13			26	SY	10	2 / 2 / / / /	5	7	30	32						
9. Joint Repair	10	10			20	SY	5	2 / 2 / / / /	6	8	31	33						
10. Full Depth Repairs	3	3			6	SY	10	1 / 1 / / / /	7	8	32	33						
11. Expansion Device	1	1			2	LS	0.5	2 / 2 / / / /	8	10	33	35						
12. Adjusting Floor Drains	3	3			6	EACH	2	2 / 2 / / / /	8	10	33	35						
13. Bearing Painting	5	5			10	EACH	1	5 / 5 / / / /	8	13	33	38						
14. Conc Overlay Decks	20	20			40	CY	10	2 / 2 / / / /	13	15	38	40						
15. Overlay Cure Time	3	3			6	DAY	1	3 / 3 / / / /	15	18	40	43						
16. Concrete Pavt App Slab (incl cu	56	56			112	SY	9	7 / 7 / / / /	17	24	42	49						
17. HMA Pavement	205	205			410	TON	1750	1 / 1 / / / /	23	24	48	49						
18. Finishing Roadway	1	1			2	LS	1	1 / 1 / / / /	24	25	49	50						
19. Polymer Overlay			260	260	520	SY	200	/ / 2 / 2 /					68	70	70	72		
								/ / / / /										

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0		0	0
			0	0		0		0	0
March	3/14/2022	3/31/2022	18	18		14	65	9	9
April	4/4/2022	4/30/2022	27	45		20	77	15	24
May	5/2/2022	5/31/2022	30	75	1.5	21	80	16	40
June	6/1/2022	6/30/2022	30	105		22	81	18	58
July	7/1/2022	7/26/2022	26	131	1.5	17	85	14	72
			0	131		0		0	72
			0	131		0		0	72
			0	131		0		0	72
			0	131		0		0	72
			0	131		0		0	72

REMARKS

Polymer Overlay requires 28 days of cure time on concrete overlay. Completion Date represents completion of Polymer Overlay.

Contract Work Type

- ☐ Calendar Days
☐ Working Days
☐ Completion Date
Prepared By

130
55
July 26, 2022
CBS2 / jwm

CONSTRUCTION YEAR: 2022

CONTRACT TIME FOR COMPLETION


Wisconsin Department of Transportation DT1923 04/2020

Project ID 1590-18-62
Work Type Bridge Rehabilitation B-21-10

Highway County USH 8 Forest

Project Title Monico - Laona
Project Limits Wolf & Peshigo Bridges B-21-1,10

Date of Letting September 14, 2021
Probable Date of Beginning June 6, 2022

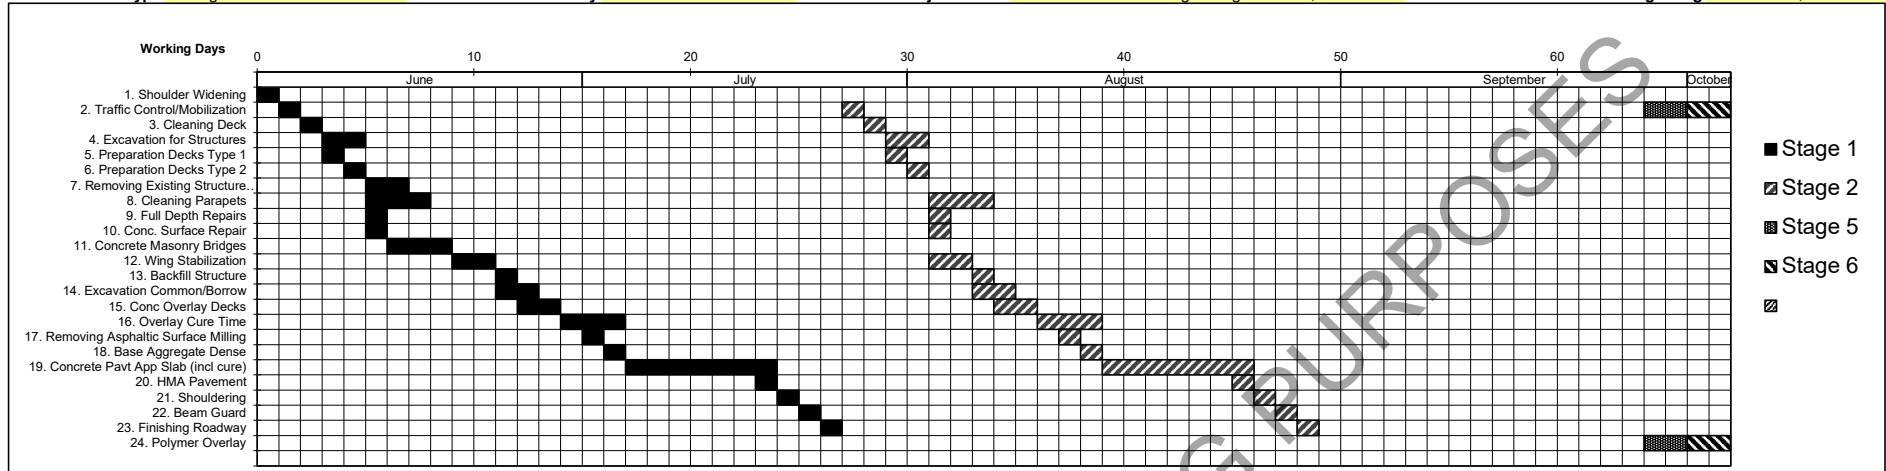

ITEM ANALYSIS

Item	Contract Quantity per Stage				Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 5		Stage 6			
	Stage 1	Stage 2	Stage 5	Stage 6					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
1. Shoulder Widening	174				174	TON	500	1 / / / / /	0	1								
2. Traffic Control/Mobilization	1	1	2	2	6	LS	1	1 / 1 / 2 / 2 /	1	2	27	28	64	66	66	68		
3. Cleaning Deck	220	220			440	SY	500	1 / 1 / / / /	2	3	28	29						
4. Excavation for Structures	1	1			2	LS	0.5	2 / 2 / / / /	3	5	29	31						
5. Preparation Decks Type 1	10	10			20	SY	20	1 / 1 / / / /	3	4	29	30						
6. Preparation Decks Type 2	4	4			8	SY	10	1 / 1 / / / /	4	5	30	31						
7. Removing Existing Structure (W)	1				1	LS	0.5	2 / / / / /	5	7								
8. Cleaning Parapets	121	121			242	LF	80	3 / 3 / / / /	5	8	31	34						
9. Full Depth Repairs	1	1			2	SY	10	1 / 1 / / / /	5	6	31	32						
10. Conc. Surface Repair	35	35			70	SF	950	1 / 1 / / / /	5	6	31	32						
11. Concrete Masonry Bridges	10				10	CY	4	3 / / / / /	6	9								
12. Wing Stabilization	1	1			2	LS	0.5	2 / 2 / / / /	9	11	31	33						
13. Backfill Structure	95	95			190	TON	100	1 / 1 / / / /	11	12	33	34						
14. Excavation Common/Borrow	465	465			930	CY	250	2 / 2 / / / /	11	13	33	35						
15. Conc Overlay Decks	14	14			28	CY	10	2 / 2 / / / /	12	14	34	36						
16. Overlay Cure Time	3	3			6	DAY	1	3 / 3 / / / /	14	17	36	39						
17. Removing Asphaltic Surface Mi	1,085	1,085			2,170	SY	16000	1 / 1 / / / /	15	16	37	38						
18. Base Aggregate Dense	280	280			560	TON	800	1 / 1 / / / /	16	17	38	39						
19. Concrete Pavt App Slab (incl cu	67	67			134	SY	10	7 / 7 / / / /	17	24	39	46						
20. HMA Pavement	166	166			332	TON	1750	1 / 1 / / / /	23	24	45	46						
21. Shouldering	33	33			66	TON	500	1 / 1 / / / /	24	25	46	47						
22. Beam Guard	354	354			708	LF	400	1 / 1 / / / /	25	26	47	48						
23. Finishing Roadway	1	1			2	LS	1	1 / 1 / / / /	26	27	48	49						
24. Polymer Overlay			220	220	440	SY	200	/ / 2 / 2 /					64	66	66	68		
								/ / / / /										

Month	Date		Days		Possible Work Days	Probable Working Days		
	Begin	End	Month	Total		%	Month	Total
			0	0	0		0	0
			0	0	0		0	0
			0	0	0		0	0
			0	0	0		0	0
			0	0	0		0	0
June	6/6/2022	6/30/2022	25	25	19	81	15	15
July	7/5/2022	7/31/2022	27	52	18	85	15	30
August	8/1/2022	8/31/2022	31	83	23	85	20	50
September	9/1/2022	9/30/2022	30	113	21	80	16	66
October	10/1/2022	10/6/2022	6	119	4	50	2	68
			0	119	0		0	68
			0	119	0		0	68

REMARKS

Polymer Overlay requires 28 days of cure time on concrete overlay. Completion Date represents completion of Polymer Overlay.

☐ Contract Work Type
☐ Calendar Days
☐ Working Days
☐ Completion Date
Prepared By

120
55
October 6, 2022
CBS2 / jwm

CONSTRUCTION YEAR: 2022

CONTRACT TIME FOR COMPLETION


Wisconsin Department of Transportation DT1923 04/2020

Project ID 1590-18-61
Work Type Resurfacing

Highway USH 8
County Forest

Project Title Monico - Laona
Project Limits Oneida County Line to Boulevard Avenue

Date of Letting September 14, 2021
Probable Date of Beginning May 25, 2022

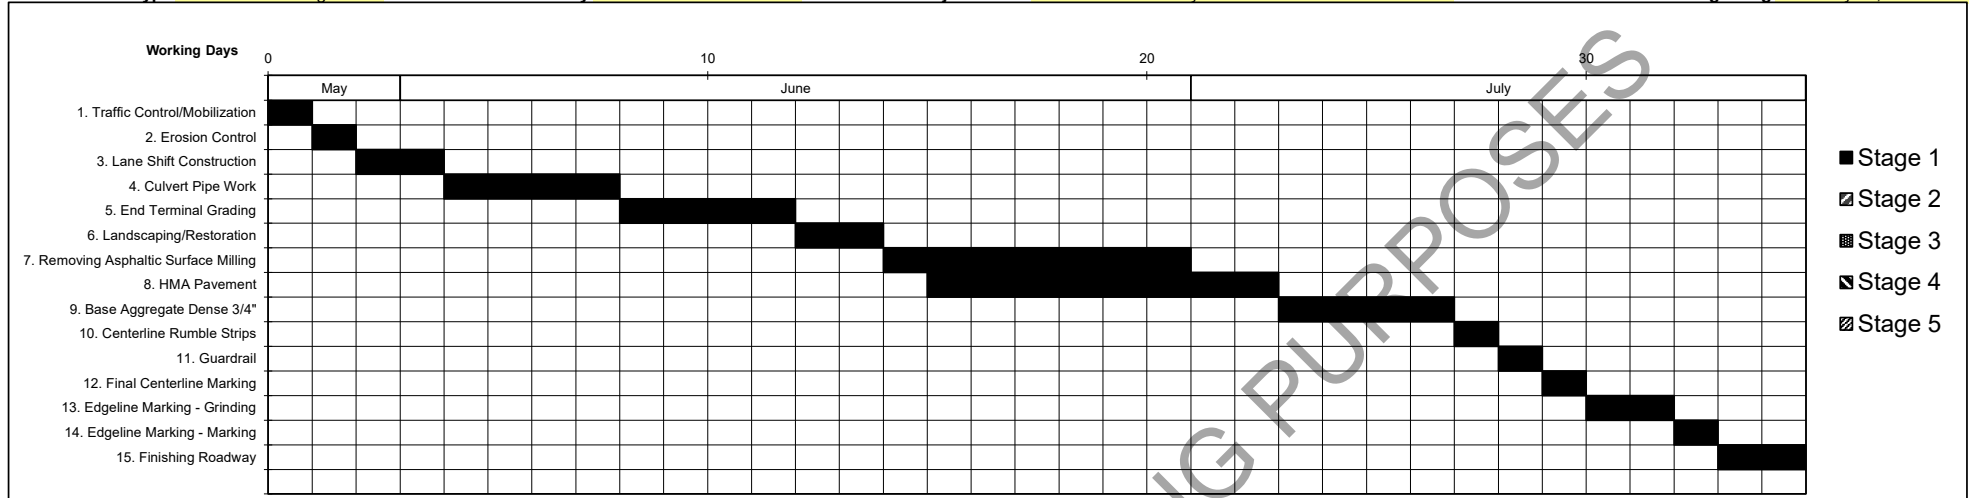

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5	
	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
1. Traffic Control/Mobilization	1					1	L.S.	1	1 / / / / /	0	1								
2. Erosion Control	1					1	L.S.	1	1 / / / / /	1	2								
3. Lane Shift Construction	4					4	Each	2	2 / / / / /	2	4								
4. Culvert Pipe Work	394					394	L.F.	125	4 / / / / /	4	8								
5. End Terminal Grading	1,900					1,900	C.Y.	500	4 / / / / /	8	12								
6. Landscaping/Restoration	4,522					4,522	S.Y.	2500	2 / / / / /	12	14								
7. Removing Asphaltic Surface Mill	118,500					118,500	S.Y.	19000	7 / / / / /	14	21								
8. HMA Pavement	13,800					13,800	Ton	1750	8 / / / / /	15	23								
9. Base Aggregate Dense 3/4"	2,017					2,017	Ton	570	4 / / / / /	23	27								
10. Centerline Rumble Strips	27,270					27,270	L.F.	125000	1 / / / / /	27	28								
11. Guardrail	196					196	L.F.	600	1 / / / / /	28	29								
12. Final Centerline Marking	15,770					15,770	L.F.	23000	1 / / / / /	29	30								
13. Edgeline Marking - Grinding	68,600					68,600	L.F.	35000	2 / / / / /	30	32								
14. Edgeline Marking - Marking	68,600					68,600	L.F.	70000	1 / / / / /	32	33								
15. Finishing Roadway	1					1	Each	0.5	2 / / / / /	33	35								

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
May	5/25/2022	5/31/2022	7	7	1.5	4	80	3	3
June	6/1/2022	6/30/2022	30	37		22	81	18	21
July	7/1/2022	7/26/2022	26	63	1.5	17	85	14	35
			0	63		0		0	35
			0	63		0		0	35
			0	63		0		0	35
			0	63		0		0	35
			0	63		0		0	35

REMARKS

Construction to take place in 2022 construction season with a contract completion time of 35 Working Days. Friday afternoons where work is not allowed for Memorial Day and Independence Day are included as a 1/2 day holiday. Proposed improvements include mill and overlay, culvert and ditch cleaning, culvert replacements, gravel shouldering, pavement marking, rumble strips, and restoration.

Contract Work Type

- ☐ Calendar Days
☒ Working Days
☐ Completion Date
 Prepared By

65
 35
 July 25, 2022
 CBS2 / jwm

CONSTRUCTION YEAR: 2022
