


CONTRACT TIME FOR COMPLETION (STH 100)

Project ID 2150-00-72, 2270-04-70, 2565-07-70
Work Type Modernization

Highway WIS 57
County Milwaukee/Ozaukee

Project Title STH 57 - Vil Brown Deer & City Mequon
Project Limits Teutonia Avenue to Mequon Road

Date of Letting September 14, 2021
Probable Date of Beginning April 1, 2023

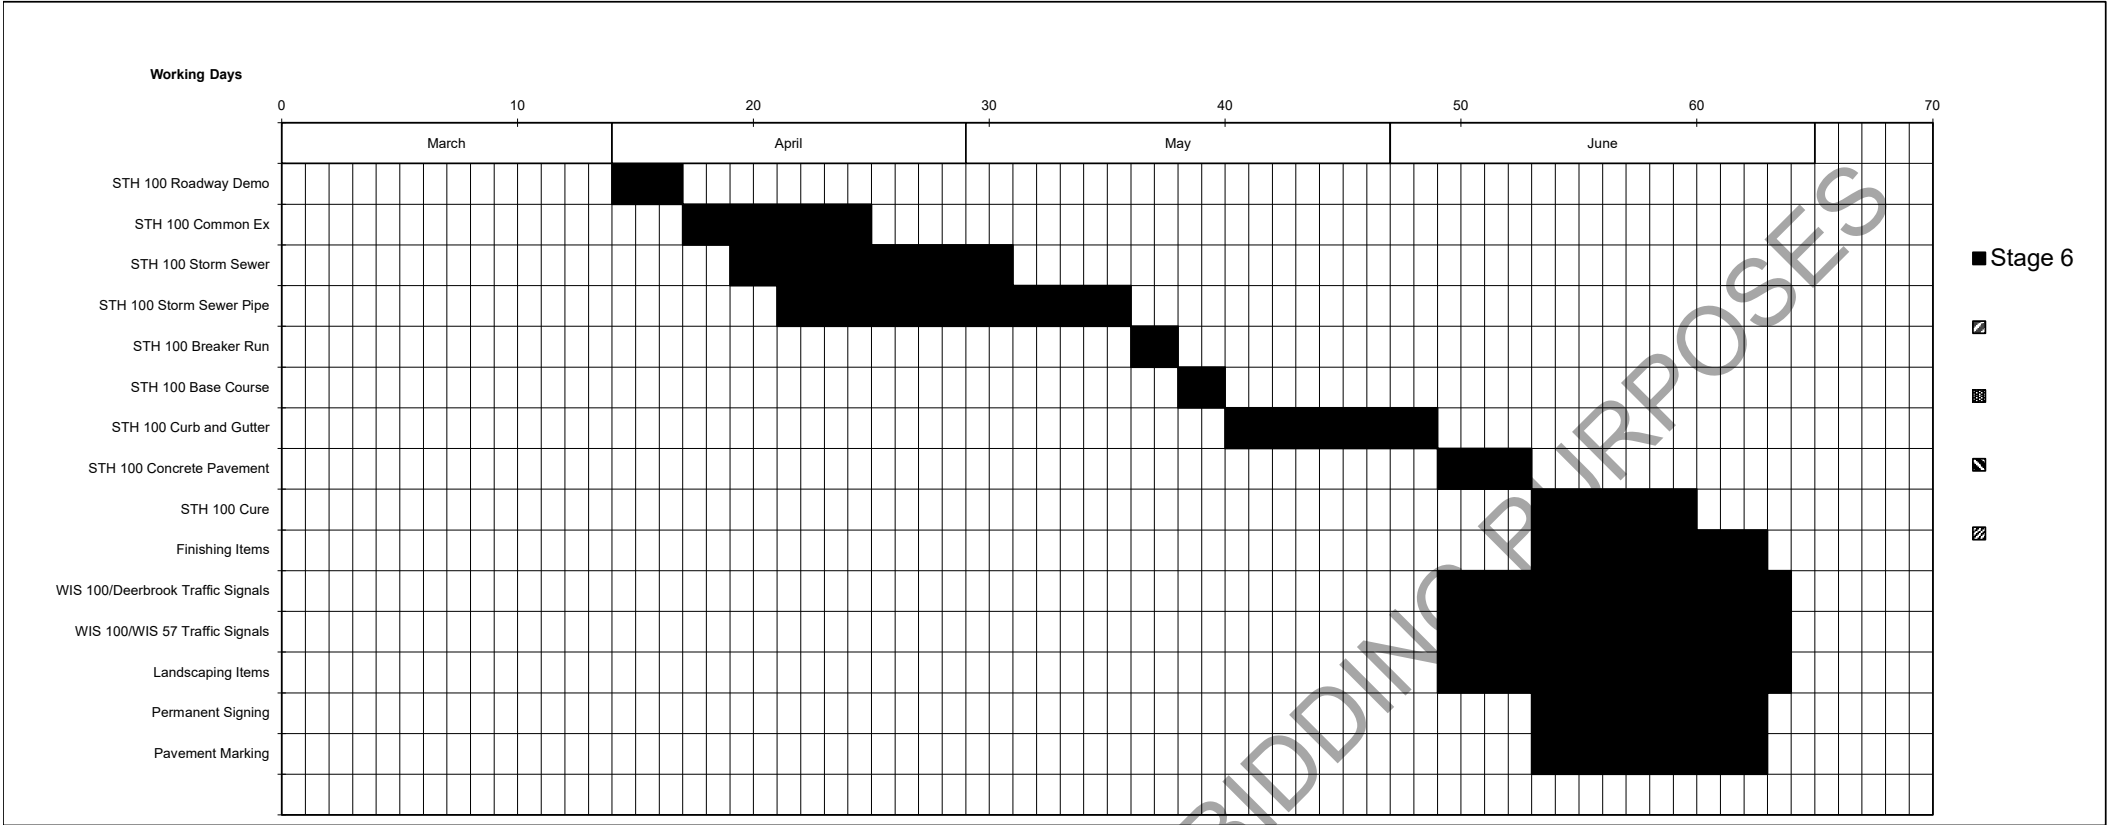

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 6									
	Stage 6									Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
STH 100 Roadway Demo	250					250	SY	100	3 / / / /	14	17								
STH 100 Common Ex	7,309					7,309	CY	920	8 / / / /	17	25								
STH 100 Storm Sewer	34					34	DAY	3	12 / / / /	19	31								
STH 100 Storm Sewer Pipe	1,497					1,497	LF	100	15 / / / /	21	36								
STH 100 Breaker Run	826					826	TON	600	2 / / / /	36	38								
STH 100 Base Course	393					393	TON	300	2 / / / /	38	40								
STH 100 Curb and Gutter	7,128					7,128	LF	850	9 / / / /	40	49								
STH 100 Concrete Pavement	3,347					3,347	SY	1000	4 / / / /	49	53								
STH 100 Cure	7					7	DAY	1	7 / / / /	53	60								
Finishing Items	10					10	DAY	1	10 / / / /	53	63								
WIS 100/Deerbrook Traffic Signals	15					15	DAY	1	15 / / / /	49	64								
WIS 100/WIS 57 Traffic Signals	15					15	DAY	1	15 / / / /	49	64								
Landscaping Items	15					15	TON	1	15 / / / /	49	64								
Permanent Signing	10					10	DAY	1	10 / / / /	53	63								
Pavement Marking	10					10	DAY	1	10 / / / /	53	63								

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0	61	0	0
			0	0		0	65	0	0
March	3/1/2023	3/30/2023	30	30		22	65	14	14
April	4/1/2023	4/30/2023	30	60		20	77	15	29
May	5/1/2023	5/31/2023	31	91	1	22	80	18	47
June	6/1/2023	6/30/2023	30	121		22	80	18	65
				121		0	85	0	65
				121		0	85	0	65
				121		0	80	0	65
				121		0	73	0	65
				121		0	70	0	65
				121		0	58	0	65

REMARKS

This sheet shows WIS 100 Stage 6 in 2023

Calendar Days
Working Days
Completion Date
Prepared By

121
65
June 30, 2023
Chris Quesnell

CONSTRUCTION YEAR: 2023
