


CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2011

Project ID	1009-30-16	Highway	Var Hwy	Project Title	Sign Bridge Replacement	Date of Letting	May 14, 2019
Work Type	Sign structure repair	County	Dane	Project Limits	Regionwide Various Routes SW	Probable Date of Beginning	September 16, 2019

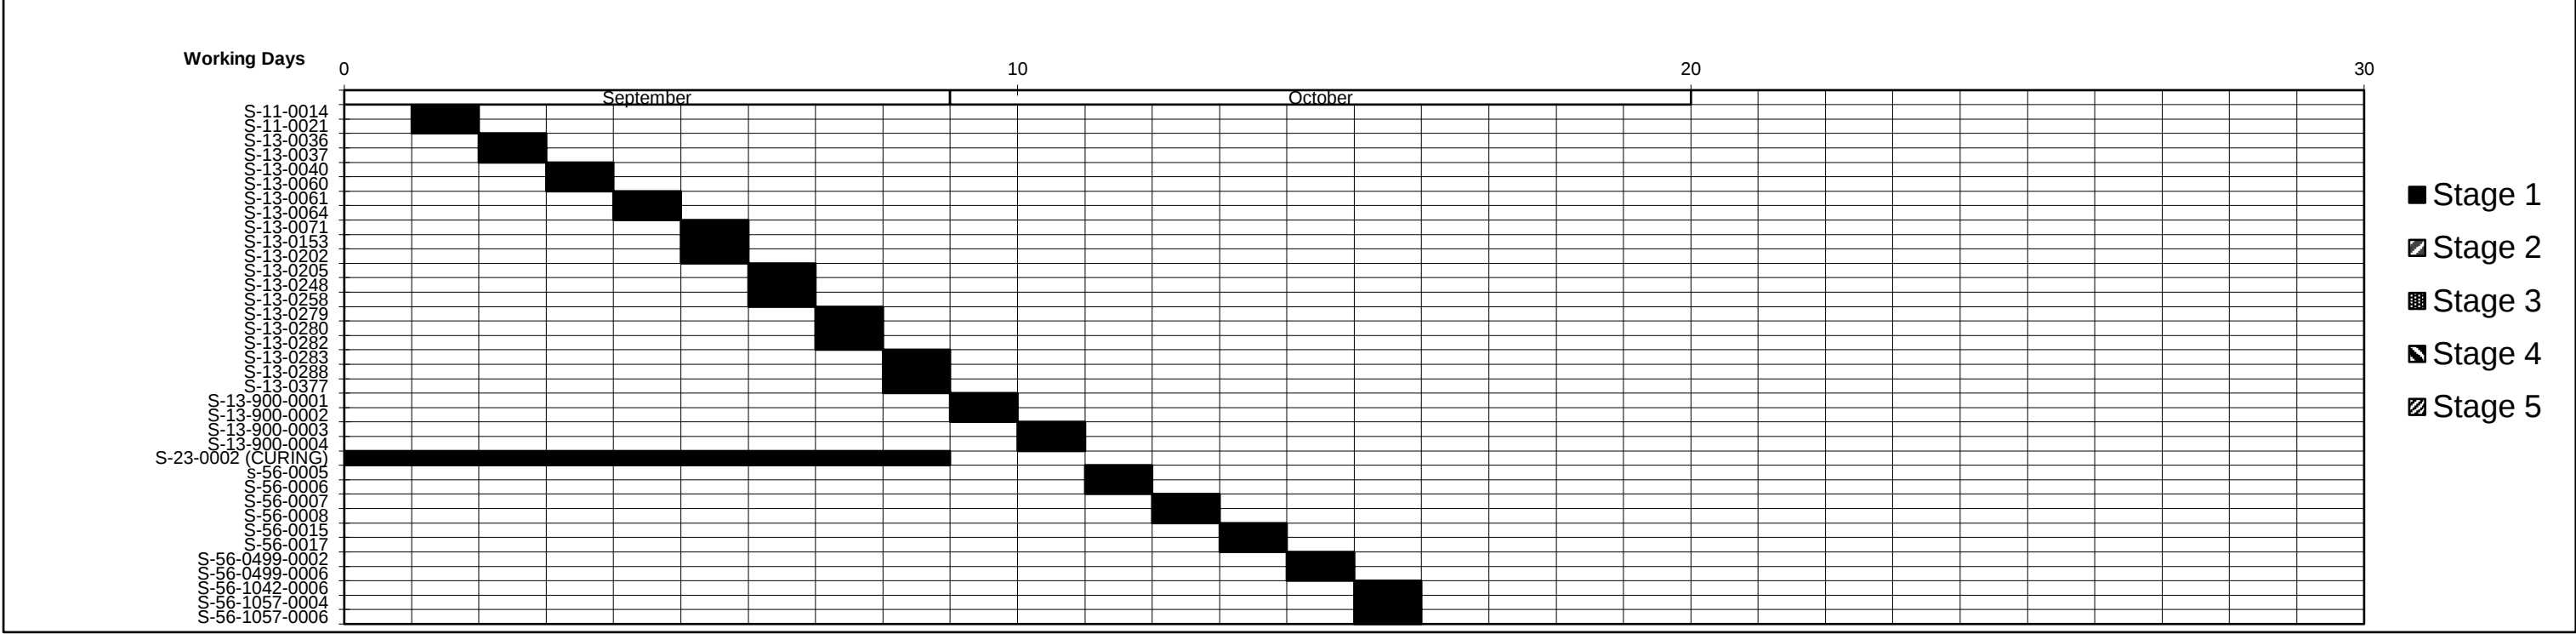

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5	
	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
S-11-0014	1					1	DAY	1	1 / / / /	1	2								
S-11-0021	1					1		1	1 / / / /	1	2								
S-13-0036	1					1		1	1 / / / /	2	3								
S-13-0037	1					1		1	1 / / / /	2	3								
S-13-0040	1					1		1	1 / / / /	3	4								
S-13-0060	1					1		1	1 / / / /	3	4								
S-13-0061	1					1		1	1 / / / /	4	5								
S-13-0064	1	1				1		1	1 / / / /	4	5								
S-13-0071	1					1		1	1 / / / /	5	6								
S-13-0153	1					1		1	1 / / / /	5	6								
S-13-0202	1					1		1	1 / / / /	5	6								
S-13-0205	1	1				1		1	1 / / / /	6	7								
S-13-0248	1					1		1	1 / / / /	6	7								
S-13-0258	1					1		1	1 / / / /	6	7								
S-13-0279	1					1		1	1 / / / /	7	8								
S-13-0280	1					1		1	1 / / / /	7	8								
S-13-0282	1					1		1	1 / / / /	7	8								
S-13-0283	1					1		1	1 / / / /	8	9								
S-13-0288	1					1		1	1 / / / /	8	9								
S-13-0377	1					1		1	1 / / / /	8	9								
S-13-900-0001	1					1		1	1 / / / /	9	10								
S-13-900-0002	1					1		1	1 / / / /	9	10								
S-13-900-0003	1	1				1		1	1 / / / /	10	11								
S-13-900-0004	1					1		1	1 / / / /	10	11								
S-23-0002 (CURING)	9					9		1	9 / / / /	0	9								
s-56-0005	1					1		1	1 / / / /	11	12								
S-56-0006	1	1				1		1	1 / / / /	11	12								
S-56-0007	1					1		1	1 / / / /	12	13								
S-56-0008	1					1		1	1 / / / /	12	13								
S-56-0015	1					1		1	1 / / / /	13	14								
S-56-0017	1	1				1		1	1 / / / /	13	14								
S-56-0499-0002	1					1		1	1 / / / /	14	15								
S-56-0499-0006	1					1		1	1 / / / /	14	15								
S-56-1042-0006	1					1		1	1 / / / /	15	16								
S-56-1057-0004	1					1		1	1 / / / /	15	16								
S-56-1057-0006	1					1		1	1 / / / /	15	16								

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
September	9/16/2019	9/30/2019	15	15		11	80	9	9
October	10/1/2019	10/21/2019	21	36		15	73	11	20
			0	36		0	80	0	20
			0	36		0	50	0	20

REMARKS

A concrete base needs to be poured and cured, preferably completed by mid October. Distance between Sign Structures and time needed to set and change lane closures will most like only allow 3-4 sign a structures a day to be completed. Round to 20 working days.

Calendar Days	36
Working Days	20
Completion Date	
Prepared By	

CONSTRUCTION YEAR: 2019
