

CONTRACT TIME FOR COMPLETION



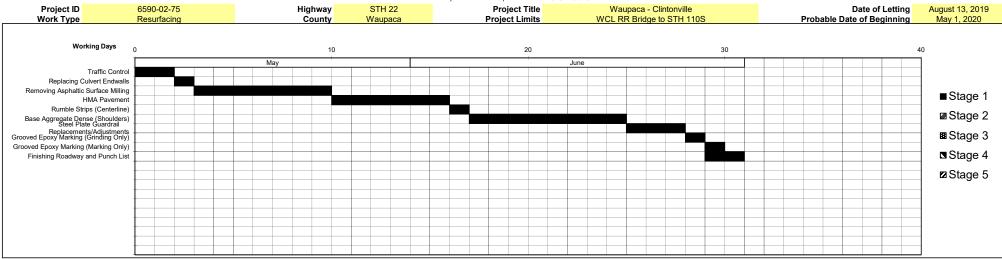

ITEM ANALYSIS

Item	Contract Quantity per Stage				Total	Unit	Production	Working Days	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5		
item	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5	Quantity	Ullit	<u>Rate</u>	(per Stage)	Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
Traffic Control	2					2	Days	1	2 / / / /	0	2								
Replacing Culvert Endwalls	2					2	EACH	4	1 / / / /	2	3								
Removing Asphaltic Surface Milling	77,130					77,130	SY	12,000	7 / / / /	3	10								
HMA Pavement	6,680					6,680	TON	1,200	6 / / / /	10	16								
Rumble Strips (Centerline)	18,685					18,685	LF	38,000	1 / / / /	16	17								
Base Aggregate Dense (Shoulders)	3,392					3,392	TON	470	8 / / / /	17	25								
Steel Plate Guardrail Replacements/Adjustments																			
	825					825	LF	300	3 / / / /	25	28								
Grooved Epoxy Marking (Grinding Only)	42,066					42,066	LF	43,000	1 / / / /	28	29								
Grooved Epoxy Marking (Marking Only)	42,066					42,066	LF	62,000	1 / / / /	29	30								
Finishing Roadway and Punch List	2					2	Days	1	2 / / / /	29	31								
									/ / / /										
									/ / / /										
									/ / / /										
									/ / / /										
									1 1 1 1										
									1 1 1 1										
									1 1 1										
									1 1 1 1										
									1 1 1										
									1 1 1 1										

	Date			Days		Possible	Probable Working Days			
Month	Begin	End	Month	Total	Holiday	Work Days	%	Month	Total	
			0	0		0	0	0	0	
			0	0		0	0	0	0	
			0	0		0	0	0	0	
			0	0		0	0	0	0	
May	5/1/2020	5/31/2020	31	31	1	20	68	14	14	
June	6/1/2020	6/29/2020	29	60	0	21	80	17	31	
			0	60		0	0	0	31	
			0	60		0	0	0	31	
			0	60		0	0	0	31	
			0	60		0	0	0	31	
			0	60		0	0	0	31	
			0	60		0	0	0	31	

REMARKS Construction to take place in 2020 construction season with a completion date of July 2, 2020.

Calendar Days Working Days Completion Date Prepared By

60 31 July 2, 2020 Tammy Tucker

CONSTRUCTION YEAR: 2020
