



DISASTER DAMAGE AID MEMORANDUM

DT2084 9/2013

Wisconsin Department of Transportation

Date: 3/11/2015
(m/d/yyyy)

To: Lorrie Olson, Disaster Damage Aids Manager
Bureau of Transit, Local Roads, Railroads and Harbors
Room 951, HFSTB

From: Lance Burger
NW Region - Superior Regional Office

Subject: Disaster Damage Aids Recommendations

Attached are the Petition, Payment Recommendation, Investigation and Cost Statement for *Disaster Damage Aid* for your review:

Municipality	<u>Town of Jackson</u>	County	<u>Burnett</u>
Muni-Code	<u>07-012</u>		
Date of Flood (m/d/yyyy)	<u>7/2/2011</u>		
Date of Petition (m/d/yyyy)	<u>12/30/2013</u>		

All damage locations have been inspected and reviewed by this office:

Number of Damage sites that qualify for aid.	<u>11</u>
Number of Damage sites that do not qualify for aid.	<u>0</u>
Recommended maximum Disaster Damage Aid amount.	<u>\$ 6,411</u>

Comments:

This is the second claim submission for the Town of Jackson (Round 1- page 2).

Attachments: Petition
Payment Recommendation
Investigation and Cost Statement
Location Map(s)

DISASTER DAMAGE AIDS PAYMENT RECOMMENDATION

DT2068 9/2013

RECEIVED Wisconsin Department of Transportation

FEB 24 2015

Office Use Only
Claim No. _____

WISDOT NW SUPERIOR

Local Government Town of Jackson		County Burnett
Date of Disaster 07/02/2011	Date of Petition 12/30/2013	Date of Investigation 08/24/2014

List Eligible Sites Only

SITE NUMBER	ROAD NAME AND LOCATION	PROJECT COSTS	
		REPLACEMENT	IMPROVEMENT
57	Morning Star Rd (T40N-R15W-Sec 15)	\$ 688.04	\$
58	Kovarik Rd (T40N-R15W-Sec 25)	\$ 699.68	\$
59	Green Trail (T40N-R15W-Sec 26)	\$ 535.10	\$
60	Winter Hill Terr (T40N-R15W-Sec 23)	\$ 653.23	\$
61	Moro Rd (T40N-R15W-Sec 8)	\$ 1,766.39	\$
64	Wilderness Way (T40N-R15W-Sec 10)	\$ 768.38	\$
70	Bent Tree Way (T40N-R15W-Sec 25)	\$ 852.50	\$
72	Thompson Rd (T40N-R15W-Sec 25)	\$ 547.56	\$
76	Pratt Rd (T40N-R15W-Sec 27)	\$ 712.77	\$
82	Bridle Rd (T40N-R15W-Sec 22)	\$ 775.55	\$
84	Moro Rd (T40N-R15W-Sec 8)	\$ 1,159.85	\$
Totals		\$ 9,159.05	\$


Payment Calculation (Choose A or B)

☒ Final Costs	Replacement X 75%	\$
	Improvement X 50%	\$
	Replacement X 70% Damage to highway in response to event § 86.34(1g)(2)	\$ 6,411.34
	Total	\$ 6,411.34
☐ Estimated Costs (Must be \$15,000 or less)	Replacement X 75%	\$
	Improvement X 75%	\$
	Replacement X 70% Damage to highway in response to event § 86.34(1g)(2)	\$
	Total	\$

Note: If applicant accepts the Department of Transportation cost estimate as specified in § 86.34(2m) Wis. Stats. the payment is final and precludes the applicant from receiving any other aid on this claim.

Municipality/County Signature

I certify that I have full authority to act on behalf of the local government identified above regarding this claim.

X  Supervisor 2/20/15
(Authorized Representative) (Title) (Date)

Roger Larson Rogerlar@centurytel.net
(Print Name) (Email Address)

Payment Approvals

Recommended Payment		Approved Payment		Authorize Payment	
Date	Amount	Date	Amount	Date	Amount
2/24/2015	\$ 6,411.34		\$		\$
X <u></u> (Transportation Regional Office Signature)		X (Bureau of Highway Maintenance Signature)		X (Bureau of Transit, Local Roads, Railroads and Harbors – Signature)	

Wisconsin Department of Transportation
DT2069 9/2013

Claim No. _____

Equipment					
Equipment Description/Type	Size or HP	Hours	Rate	Replacement	Improvement
Tandem -118		1.0	\$ 57.00	\$ 57.00	\$
444H JD Loader - 207		3.0	\$ 52.50	\$ 157.50	\$
Pickup Truck (101)		1.0	\$ 13.86	\$ 13.86	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
Equipment Total		5.0		\$ 228.36	\$

1 of 2

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENT *(continued)*

Wisconsin Department of Transportation DT2069

Materials				
Materials Description/Type	Quantity	Rate/Unit	Replacement	Improvement
Gravel	21.8 ton	\$ 8.65	\$ 188.57	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Materials Total			\$ 188.57	\$

Contract or Force Account Work		
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
Contract or Force Account Work Total	\$	\$

Site Number <u>2011-10(59)</u> : Total Cost of Damage	\$ 535.10	\$
--	------------------	-----------

PLEASE ATTACH ALL INVOICES

Town of Jackson, Burnett County

DATE	EMPLOYEE Name	EQUIPMENT (Class)	MATERIAL	LABOR HOURS	EQUIPMENT HOURS	MATERIALS	UNIT COST	LABOR COSTS	EQUIPMENT COSTS	MATERIAL COSTS	TOTAL COST	Replace %	Replace \$ Value	70% Reimburse	Non- participating Improvement
2011	Guy Lohman	ROAD FOREMAN		4.0			\$ 26.24	\$ 104.96	\$ -	\$ -	\$ 104.96	100.0%	\$ 104.96	\$ 73.47	\$ -
	Brad Huser	LABORER		1.0			\$ 13.21	\$ 13.21	\$ -	\$ -	\$ 13.21	100.0%	\$ 13.21	\$ 9.25	\$ -
		DUMP TRUCK 1118)			1.0		\$ 57.00	\$ -	\$ 57.00	\$ -	\$ 57.00	100.0%	\$ 57.00	\$ 39.90	\$ -
		J.D. GRADER (308)			0.0		\$ 71.44	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		F350 PICKUP(101)			1.0		\$ 13.86	\$ -	\$ 13.86	\$ -	\$ 13.86	100.0%	\$ 13.86	\$ 9.70	\$ -
		FRONT END LOADER(206)			3.0		\$ 52.50	\$ -	\$ 157.50	\$ -	\$ 157.50	100.0%	\$ 157.50	\$ 110.25	\$ -
		Col Patch				0	\$ 51.73	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		3/4" GRAVEL (CU YDS)				21.80	\$ 8.65	\$ -	\$ -	\$ 188.57	\$ 188.57	100.0%	\$ 188.57	\$ 132.00	\$ -
				5.0	5.0	21.8		\$ 118.17	\$ 228.36	\$ 188.57	\$ 535.10		\$ 535.10	\$ 374.57	\$ -

**Total Roadway width stayed the same. Patched then chipsealed


100.0% =Gravel

Hired Services

Hopkinsd Sand & Gravel - Added Town gravel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	--------	------	------	------	------

	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	------	------	------	------	------

Guy Lohman	\$ 26.24	4.0	\$ 104.96	\$ 104.96	\$ -	TOTAL COST	\$ 535.10	\$ 535.10	\$ 374.57	\$ -
	\$ -	0.0	\$ -	\$ -	\$ -			100%	70%	0%
Brad Huser	\$ 13.21	1.0	\$ 13.21	\$ 13.21	\$ -	Replace	\$ 535.10			
	\$ -	0.0	\$ -	\$ -	\$ -	Improve	\$ -	100.0%	\$ 118.17	\$ 82.72
			\$ 118.17	\$ 118.17	\$ -		\$ 535.10			
DUMP TRUCK	\$ 57.00	1.0	\$ 57.00	\$ 57.00	\$ -					
FRONT END LOADER(206)	\$ 52.50	3.0	\$ 157.50	\$ 157.50	\$ -					
J.D. GRADER (308)	\$ 71.44	0.0	\$ -	\$ -	\$ -					
F350 PICKUP(101)	\$ 13.86	1.0	\$ 13.86	\$ 13.86	\$ -			100.0%	\$ 228.36	\$ 159.85
			\$ 228.36	\$ 228.36	\$ -					
3/4" GRAVEL (ton)	\$ 8.65	21.80	\$ 188.57	\$ 188.57	\$ -			100.0%	\$ 188.57	\$ 132.00
Col Patch	\$ 51.73	0	\$ -					70% REIMBURSEMENT =	\$ 374.57	

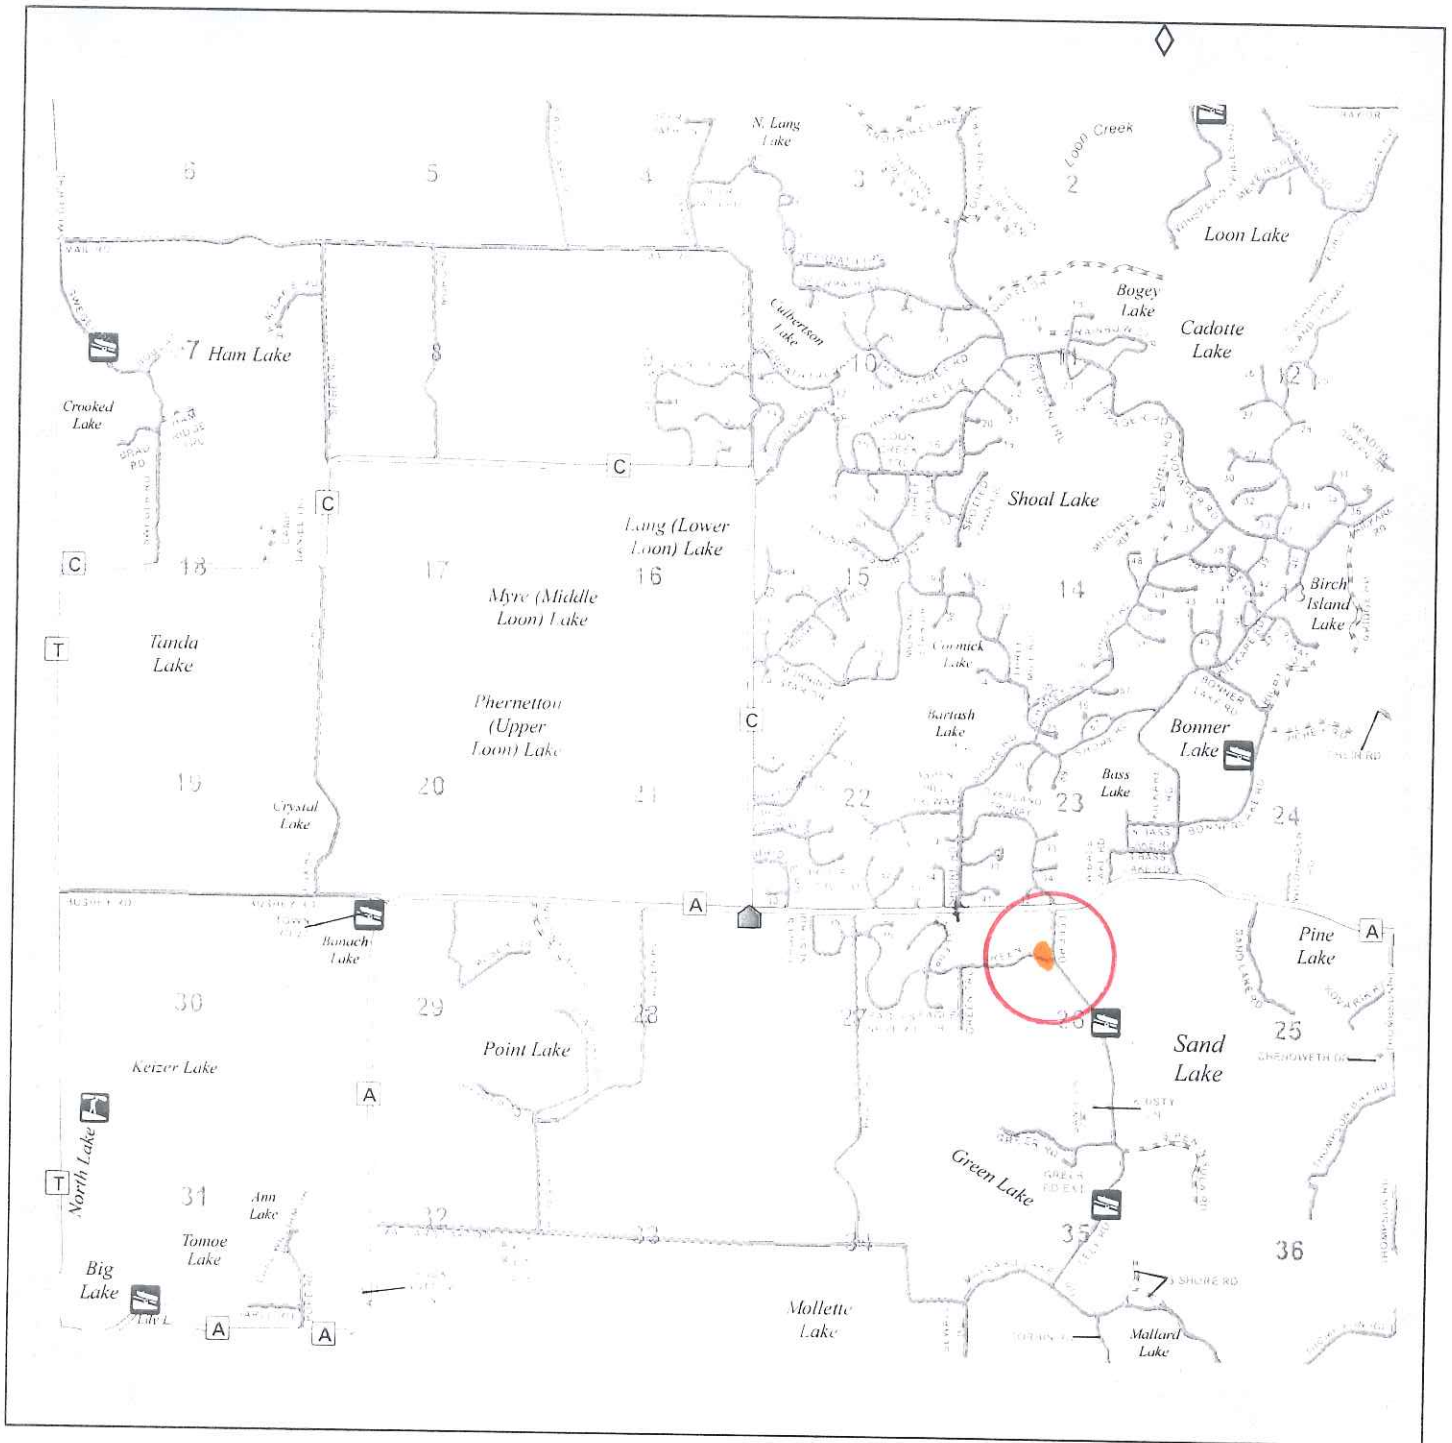

Wisconsin Department of Transportation
DT2069 9/2013

Claim No.

Equipment					
Equipment Description/Type	Size or HP	Hours	Rate	Replacement	Improvement
Tandem -118		1.5	\$ 57.00	\$ 85.50	\$
444H JD Loader - 207		2.5	\$ 52.50	\$ 131.25	\$
772D JD Grader - 308		2.0	\$ 71.44	\$ 142.88	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
Equipment Total		6.0		\$ 359.63	\$

1 of 2

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENT *(continued)*

Wisconsin Department of Transportation DT2069

Materials				
Materials Description/Type	Quantity	Rate/Unit	Replacement	Improvement
Gravel (Ton)	18.0	\$ 8.65	\$ 155.70	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Materials Total			\$ 155.70	\$

Contract or Force Account Work		
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
Contract or Force Account Work Total	\$	\$

Site Number <u>2011-11 (60)</u> : Total Cost of Damage	\$ 653.23	\$
---	------------------	-----------

PLEASE ATTACH ALL INVOICES

Town of Jackson, Burnett County

DATE	EMPLOYEE Name	EQUIPMENT (Class)	MATERIAL	LABOR HOURS	EQUIPMENT HOURS	MATERIALS	UNIT COST	LABOR COSTS	EQUIPMENT COSTS	MATERIAL COSTS	TOTAL COST	Replace %	Replace \$ Value	70% Reimburse	Non- participating Improvement
2011	Guy Lohman	ROAD FOREMAN		4.5			\$ 26.24	\$ 118.08	\$ -	\$ -	\$ 118.08	100.0%	\$ 118.08	\$ 82.66	\$ -
	Brad Huser	LABORER		1.5			\$ 13.21	\$ 19.82	\$ -	\$ -	\$ 19.82	100.0%	\$ 19.82	\$ 13.87	\$ -
		DUMP TRUCK 1118)			1.5		\$ 57.00	\$ -	\$ 85.50	\$ -	\$ 85.50	100.0%	\$ 85.50	\$ 59.85	\$ -
		J.D. GRADER (308)			2.0		\$ 71.44	\$ -	\$ 142.88	\$ -	\$ 142.88	100.0%	\$ 142.88	\$ 100.02	\$ -
		F350 PICKUP(101)					\$ 13.86	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		FRONT END LOADER(206)			2.5		\$ 52.50	\$ -	\$ 131.25	\$ -	\$ 131.25	100.0%	\$ 131.25	\$ 91.88	\$ -
		Col Patch					\$ 51.73	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		3/4" GRAVEL (Ton)				18.00	\$ 8.65	\$ -	\$ -	\$ 155.70	\$ 155.70	100.0%	\$ 155.70	\$ 108.99	\$ -
				6.0	6.0	18.0		\$ 137.90	\$ 359.63	\$ 155.70	\$ 653.23		\$ 653.23	\$ 457.26	\$ -

**Total Roadway width stayed the same.


100.0% =Gravel

Hired Services

Hopkinsd Sand & Gravel - Added Town gravel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	--------	------	------	------	------

	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	------	------	------	------	------

Guy Lohman	\$ 26.24	4.5	\$ 118.08	\$ 118.08	\$ -	TOTAL COST	\$ 653.23	\$ 653.23	\$ 457.26	\$ -
	\$ -	0.0	\$ -	\$ -	\$ -			100%	70%	0%
Brad Huser	\$ 13.21	1.5	\$ 19.82	\$ 19.82	\$ -	Replace	\$ 653.23			
	\$ -	0.0	\$ -	\$ -	\$ -	Improve	\$ -	100.0%	\$ 137.90	\$ 96.53
			\$ 137.90	\$ 137.90	\$ -		\$ 653.23			
DUMP TRUCK	\$ 57.00	1.5	\$ 85.50	\$ 85.50	\$ -					
FRONT END LOADER(206)	\$ 52.50	2.5	\$ 131.25	\$ 131.25	\$ -					
J.D. GRADER (308)	\$ 71.44	2.0	\$ 142.88	\$ 142.88	\$ -					
F350 PICKUP(101)	\$ 13.86	0.0	\$ -	\$ -	\$ -			100.0%	\$ 359.63	\$ 251.74
			\$ 359.63	\$ 359.63	\$ -					
3/4" GRAVEL (ton)	\$ 8.65	18.00	\$ 155.70	\$ 155.70	\$ -			100.0%	\$ 155.70	\$ 108.99
Col Patch	\$ 51.73	0	\$ -					70% REIMBURSEMENT =	\$ 457.26	

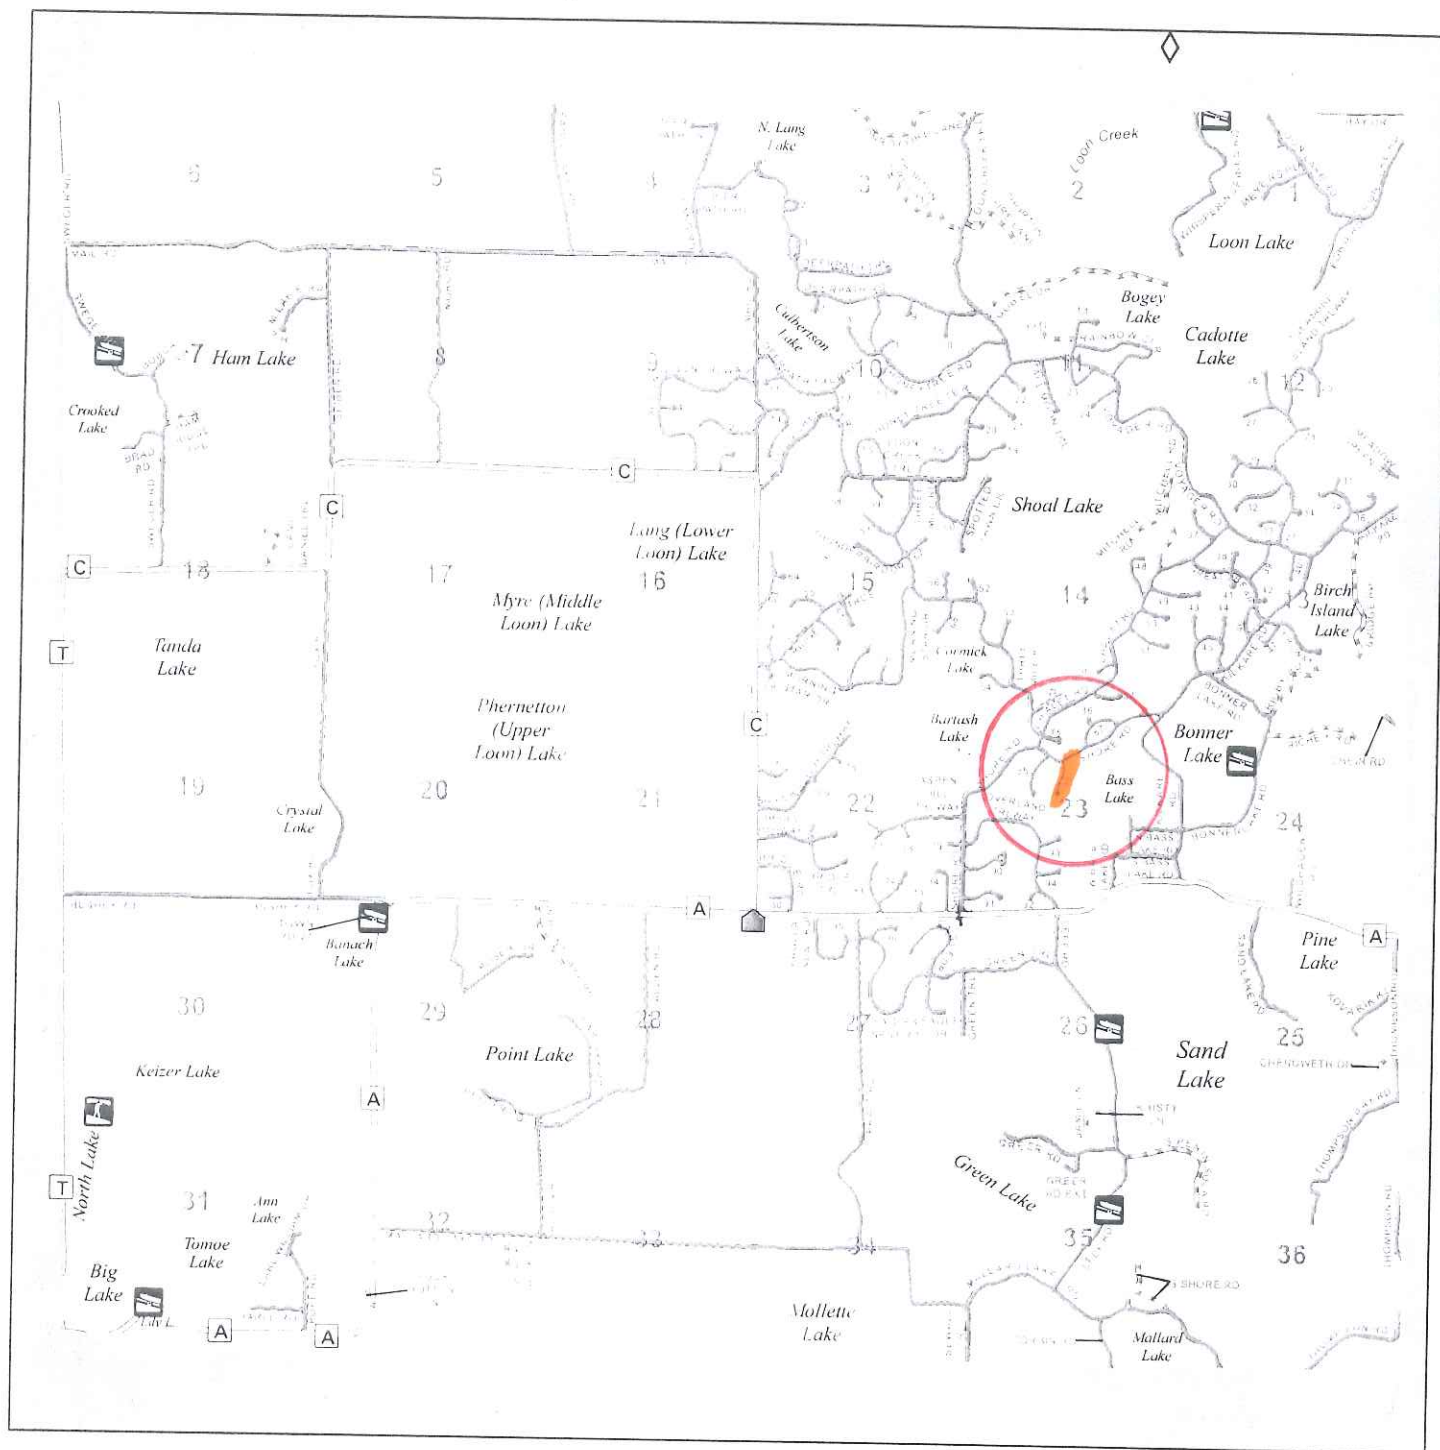

1 UNBAPTIZED
 2 UNBAPTIZED
 3 UNBAPTIZED
 4 BURNING SUNSHINE
 5 BURNING SUNSHINE
 6 BURNING SUNSHINE
 7 UNBAPTIZED WAY
 8 UNBAPTIZED WAY
 9 UNBAPTIZED
 10 UNBAPTIZED
 11 UNBAPTIZED
 12 UNBAPTIZED
 13 UNBAPTIZED
 14 UNBAPTIZED
 15 UNBAPTIZED
 16 UNBAPTIZED
 17 UNBAPTIZED
 18 UNBAPTIZED
 19 UNBAPTIZED
 20 UNBAPTIZED
 21 UNBAPTIZED
 22 UNBAPTIZED
 23 UNBAPTIZED
 24 UNBAPTIZED
 25 UNBAPTIZED
 26 UNBAPTIZED
 27 UNBAPTIZED
 28 UNBAPTIZED
 29 UNBAPTIZED
 30 UNBAPTIZED
 31 UNBAPTIZED
 32 UNBAPTIZED
 33 UNBAPTIZED
 34 UNBAPTIZED
 35 UNBAPTIZED
 36 UNBAPTIZED
 37 UNBAPTIZED
 38 UNBAPTIZED
 39 UNBAPTIZED
 40 UNBAPTIZED
 41 UNBAPTIZED
 42 UNBAPTIZED
 43 UNBAPTIZED
 44 UNBAPTIZED
 45 UNBAPTIZED
 46 UNBAPTIZED
 47 UNBAPTIZED
 48 UNBAPTIZED
 49 UNBAPTIZED
 50 UNBAPTIZED
 51 UNBAPTIZED
 52 UNBAPTIZED
 53 UNBAPTIZED
 54 UNBAPTIZED
 55 UNBAPTIZED
 56 UNBAPTIZED
 57 UNBAPTIZED
 58 UNBAPTIZED
 59 UNBAPTIZED
 60 UNBAPTIZED
 61 UNBAPTIZED
 62 UNBAPTIZED
 63 UNBAPTIZED
 64 UNBAPTIZED
 65 UNBAPTIZED
 66 UNBAPTIZED
 67 UNBAPTIZED
 68 UNBAPTIZED
 69 UNBAPTIZED
 70 UNBAPTIZED
 71 UNBAPTIZED
 72 UNBAPTIZED
 73 UNBAPTIZED
 74 UNBAPTIZED
 75 UNBAPTIZED
 76 UNBAPTIZED
 77 UNBAPTIZED
 78 UNBAPTIZED
 79 UNBAPTIZED
 80 UNBAPTIZED
 81 UNBAPTIZED
 82 UNBAPTIZED
 83 UNBAPTIZED
 84 UNBAPTIZED
 85 UNBAPTIZED
 86 UNBAPTIZED
 87 UNBAPTIZED
 88 UNBAPTIZED
 89 UNBAPTIZED
 90 UNBAPTIZED
 91 UNBAPTIZED
 92 UNBAPTIZED
 93 UNBAPTIZED
 94 UNBAPTIZED
 95 UNBAPTIZED
 96 UNBAPTIZED
 97 UNBAPTIZED
 98 UNBAPTIZED
 99 UNBAPTIZED
 100 UNBAPTIZED

40 BROWN THROAT
41 WHITE THROAT
42 WHITE THROAT
43 WHITE THROAT
44 WHITE THROAT
45 WHITE THROAT
46 WHITE THROAT
47 WHITE THROAT
48 WHITE THROAT
49 WHITE THROAT
50 WHITE THROAT
51 WHITE THROAT
52 WHITE THROAT
53 WHITE THROAT
54 WHITE THROAT
55 WHITE THROAT
56 WHITE THROAT
57 WHITE THROAT
58 WHITE THROAT
59 WHITE THROAT
60 WHITE THROAT
61 WHITE THROAT
62 WHITE THROAT
63 WHITE THROAT
64 WHITE THROAT
65 WHITE THROAT
66 WHITE THROAT
67 WHITE THROAT
68 WHITE THROAT
69 WHITE THROAT
70 WHITE THROAT
71 WHITE THROAT
72 WHITE THROAT
73 WHITE THROAT
74 WHITE THROAT
75 WHITE THROAT
76 WHITE THROAT
77 WHITE THROAT
78 WHITE THROAT
79 WHITE THROAT
80 WHITE THROAT
81 WHITE THROAT
82 WHITE THROAT
83 WHITE THROAT
84 WHITE THROAT
85 WHITE THROAT
86 WHITE THROAT
87 WHITE THROAT
88 WHITE THROAT
89 WHITE THROAT
90 WHITE THROAT
91 WHITE THROAT
92 WHITE THROAT
93 WHITE THROAT
94 WHITE THROAT
95 WHITE THROAT
96 WHITE THROAT
97 WHITE THROAT
98 WHITE THROAT
99 WHITE THROAT
100 WHITE THROAT

65 FOXHEDGE DR
 58 AND WING DR
 67 WYVENS NEST AVE
 68 AND WING DR
 69 FOXHEDGE AVE
 70 FOXHEDGE CT
 71 FOXHEDGE DR
 72 MORNING STAR LN
 73 MORNING STAR LN
 74 BIRCHWOOD RD
 75 WHITE BIRCH CT
 76 RIVER BIRCH CT
 77 ASPEN HILL PL
 78 ASPEN HILL PL
 79 ASPEN HILL LN
 80 ASPEN HILL LN

81 SHELBOURNE WAY
 82 SHELBOURNE WAY
 83 SHELBOURNE CT
 84 SHELBOURNE RD
 85 SHELBOURNE CT
 86 SHELBOURNE CT
 87 SHELBOURNE CT
 88 SHELBOURNE HILL RD
 89 SHELBOURNE HILL CT
 90 OVERLAND CIR
 91 OVERLAND RD
 92 OVERLAND CT
 93 OVERLAND DR
 94 OVERLAND TRL
 95 OVERLAND CT

Wisconsin Department of Transportation
DT2069 9/2013

Claim No.

Equipment					
Equipment Description/Type	Size or HP	Hours	Rate	Replacement	Improvement
Tandem -118		4.5	\$ 57.00	\$ 256.50	\$
444H JD Loader - 207		2.0	\$ 52.50	\$ 105.00	\$
772D JD Grader - 308		5.0	\$ 71.44	\$ 357.20	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
Equipment Total		11.5		\$ 718.70	\$

1 of 2

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENT *(continued)*

Wisconsin Department of Transportation DT2069

Materials				
Materials Description/Type	Quantity	Rate/Unit	Replacement	Improvement
3/4" Gravel (ton)	90.0	\$ 8.65	\$ 778.50	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Materials Total			\$ 778.50	\$

Contract or Force Account Work		
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
Contract or Force Account Work Total	\$	\$

Site Number <u>2011-12(61)</u> : Total Cost of Damage	\$ 1,766.39	\$
--	--------------------	-----------

PLEASE ATTACH ALL INVOICES

Town of Jackson, Burnett County

DATE	EMPLOYEE Name	EQUIPMENT (Class)	MATERIAL	LABOR HOURS	EQUIPMENT HOURS	MATERIALS	UNIT COST	LABOR COSTS	EQUIPMENT COSTS	MATERIAL COSTS	TOTAL COST	Replace %	Replace \$ Value	70% Reimburse	Non- participating Improvement
2011	Guy Lohman	ROAD FOREMAN		9.0			\$ 26.24	\$ 236.16	\$ -	\$ -	\$ 236.16	100.0%	\$ 236.16	\$ 165.31	\$ -
	Brad Huser	LABORER		2.5			\$ 13.21	\$ 33.03	\$ -	\$ -	\$ 33.03	100.0%	\$ 33.03	\$ 23.12	\$ -
		DUMP TRUCK 1118)			4.5		\$ 57.00	\$ -	\$ 256.50	\$ -	\$ 256.50	100.0%	\$ 256.50	\$ 179.55	\$ -
		J.D. GRADER (308)			5.0		\$ 71.44	\$ -	\$ 357.20	\$ -	\$ 357.20	100.0%	\$ 357.20	\$ 250.04	\$ -
		F350 PICKUP(101)			0.0		\$ 13.86	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		FRONT END LOADER(206)			2.0		\$ 52.50	\$ -	\$ 105.00	\$ -	\$ 105.00	100.0%	\$ 105.00	\$ 73.50	\$ -
		Col Patch				0	\$ 51.73	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		3/4" GRAVEL (CU YDS)				90.00	\$ 8.65	\$ -	\$ -	\$ 778.50	\$ 778.50	100.0%	\$ 778.50	\$ 544.95	\$ -
				11.5	11.5	90.0		\$ 269.19	\$ 718.70	\$ 778.50	\$ 1,766.39		\$ 1,766.39	\$ 1,236.47	\$ -

**Total Roadway width stayed the same.

100.0% =Gravel

Hired Services

Hopkinsd Sand & Gravel - Added Town gravel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	--------	------	------	------	------

	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	------	------	------	------	------

Guy Lohman	\$ 26.24	9.0	\$ 236.16	\$ 236.16	\$ -	TOTAL COST	\$ 1,766.39		\$ 1,766.39		\$ 1,236.47	\$ -
	\$ -	0.0	\$ -	\$ -	\$ -			100%		70%		0%
Brad Huser	\$ 13.21	2.5	\$ 33.03	\$ 33.03	\$ -	Replace	\$ 1,766.39					
	\$ -	0.0	\$ -	\$ -	\$ -	Improve	\$ -	100.0%	\$ 269.19	\$ 188.43		
			\$ 269.19	\$ 269.19	\$ -		\$ 1,766.39					
DUMP TRUCK	\$ 57.00	4.5	\$ 256.50	\$ 256.50	\$ -							
FRONT END LOADER(206)	\$ 52.50	2.0	\$ 105.00	\$ 105.00	\$ -							
J.D. GRADER (308)	\$ 71.44	5.0	\$ 357.20	\$ 357.20	\$ -							
F350 PICKUP(101)	\$ 13.86	0.0	\$ -	\$ -	\$ -			100.0%	\$ 718.70	\$ 503.09		
			\$ 718.70	\$ 718.70	\$ -							
3/4" GRAVEL (ton)	\$ 8.65	90.00	\$ 778.50	\$ 778.50	\$ -			100.0%	\$ 778.50	\$ 544.95		
Col Patch	\$ 51.73	0	\$ -					70% REIMBURSEMENT =	\$ 1,236.47			

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENTWisconsin Department of Transportation
DT2069 9/2013

Office Use Only

Claim No. _____

Local Government Town of Jackson		County Burnett	
Disaster Date (m/d/yyyy) 7/1/2011		Date of Inspection (m/d/yyyy)	Inspected By Lance Burger
Site Number 2011-15 (64)	Road Name Wilderness Way	Township, Range and Section <u>T40NN, R15W Sec.12</u>	Roadway Width 18'
Material Type Gravel	Sub-Structure Natural- sandy soil	Bridge/Culvert Span	
☐ Road Closed ☐ Road Impassable ☒ Damage to Highway in Response to Event \$ 86.34 (1g)(2)	Nature and Extent of Damage Logging truck damage, debris from logging operations on road, road rutted on hills, cleared debris off road, added gravel to hills, leveled and graded		
☒ Final Costs ☐ Estimated Costs		☐ Site Denied (Explain)	

Labor

Name of Person or Job Position	Hours	Rate	Replacement	Improvement
Guy Lohman - foreman	3.5	\$ 26.24	\$ 91.84	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Labor Total	3.5		\$ 91.84	\$

Equipment

Equipment Description/Type	Size or HP	Hours	Rate	Replacement	Improvement
772D JD Grader- 308		1.0	\$ 71.44	\$ 71.44	\$
Tandem -118		1.5	\$ 57.00	\$ 85.50	\$
444H JD Loader- 207		1.0	\$ 52.50	\$ 52.50	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
Equipment Total		3.5		\$ 209.44	\$

PLEASE ATTACH ALL INVOICES

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENT *(continued)*

Wisconsin Department of Transportation DT2069

Materials				
Materials Description/Type	Quantity	Rate/Unit	Replacement	Improvement
Clark Pit gravel from last years stockpile (ton)	54.0	\$ 8.65	\$ 467.10	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Materials Total			\$ 467.10	\$

Contract or Force Account Work		
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
Contract or Force Account Work Total	\$	\$

Site Number <u>2011-15 (64)</u> : Total Cost of Damage	\$ 768.38	\$
---	------------------	-----------

PLEASE ATTACH ALL INVOICES

Town of Jackson, Burnett County

DATE	EMPLOYEE Name	EQUIPMENT (Class)	MATERIAL	LABOR HOURS	EQUIPMENT HOURS	MATERIALS	UNIT COST	LABOR COSTS	EQUIPMENT COSTS	MATERIAL COSTS	TOTAL COST	Replace %	Replace \$ Value	70% Reimburse	Non- participating Improvement
2011	Guy Lohman	ROAD FOREMAN		3.5			\$ 26.24	\$ 91.84	\$ -	\$ -	\$ 91.84	100.0%	\$ 91.84	\$ 64.29	\$ -
	Brad Huser	LABORER					\$ 13.21	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		DUMP TRUCK 1118)			1.5		\$ 57.00	\$ -	\$ 85.50	\$ -	\$ 85.50	100.0%	\$ 85.50	\$ 59.85	\$ -
		J.D. GRADER (308)			1.0		\$ 71.44	\$ -	\$ 71.44	\$ -	\$ 71.44	100.0%	\$ 71.44	\$ 50.01	\$ -
		F350 PICKUP(101)					\$ 13.86	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		FRONT END LOADER(206)			1.0		\$ 52.50	\$ -	\$ 52.50	\$ -	\$ 52.50	100.0%	\$ 52.50	\$ 36.75	\$ -
		Col Patch					\$ 51.73	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		3/4" GRAVEL (Tons)				54.00	\$ 8.65	\$ -	\$ -	\$ 467.10	\$ 467.10	100.0%	\$ 467.10	\$ 326.97	\$ -
				3.5	3.5	54.0		\$ 91.84	\$ 209.44	\$ 467.10	\$ 768.38		\$ 768.38	\$ 537.87	\$ -

**Total Roadway width stayed the same.

100.0% =Gravel

Hired Services

Hopkinsd Sand & Gravel - Added Town gravel	\$ -	\$ -	\$ -	\$ -								100.0%	\$ -	\$ -	\$ -
--	------	------	------	------	--	--	--	--	--	--	--	--------	------	------	------

	\$ -	\$ -	\$ -	\$ -								\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	--	--	--	--	--	--	--	------	------	------	------


Guy Lohman	\$ 26.24	3.5	\$ 91.84	\$ 91.84	\$ -	TOTAL COST	\$ 768.38		\$ 768.38		\$ 537.87	\$ -
	\$ -	0.0	\$ -	\$ -	\$ -			100%		70%		0%
Brad Huser	\$ 13.21	0.0	\$ -	\$ -	\$ -	Replace	\$ 768.38					
	\$ -	0.0	\$ -	\$ -	\$ -	Improve	\$ -	100.0%	\$ 91.84	\$ 64.29		
			\$ 91.84	\$ 91.84	\$ -		\$ 768.38					
DUMP TRUCK	\$ 57.00	1.5	\$ 85.50	\$ 85.50	\$ -							
FRONT END LOADER(206)	\$ 52.50	1.0	\$ 52.50	\$ 52.50	\$ -							
J.D. GRADER (308)	\$ 71.44	1.0	\$ 71.44	\$ 71.44	\$ -							
F350 PICKUP(101)	\$ 13.86	0.0	\$ -	\$ -	\$ -			100.0%	\$ 209.44	\$ 146.61		
			\$ 209.44	\$ 209.44	\$ -							
3/4" GRAVEL (ton)	\$ 8.65	54.00	\$ 467.10	\$ 467.10	\$ -			100.0%	\$ 467.10	\$ 326.97		
Col Patch	\$ 51.73	0	\$ -					70% REIMBURSEMENT = \$ 537.87				



- 81 SAKLIGT WAY
 82 SAKLIGT CIR
 83 SAKLIGT CT
 84 SAKLIGT RD
 85 WINTER HILL CT
 86 WIND CT
 87 WIND LIR
 88 WINTER HILL DR
 89 WINTER HILL DR
 90 OVERLAND CIR
 91 OVERLAND RD
 92 OVERLAND CT
 93 OVERLAND DR
 94 OVERLAND DR
 95 LAGES CT
 96 LAGES DR

Town of Jackson, Burnett County

DATE	EMPLOYEE Name	EQUIPMENT (Class)	MATERIAL	LABOR HOURS	EQUIPMENT HOURS	MATERIALS	UNIT COST	LABOR COSTS	EQUIPMENT COSTS	MATERIAL COSTS	TOTAL COST	Replace %	Replace \$ Value	70% Reimburse	Non- participating Improvement
2011	Guy Lohman	ROAD FOREMAN					\$ 26.24	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
	Brad Huser	LABORER		3.0			\$ 13.21	\$ 39.63	\$ -	\$ -	\$ 39.63	100.0%	\$ 39.63	\$ 27.74	\$ -
		DUMP TRUCK 1118)					\$ 57.00	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		J.D. GRADER (308)					\$ 71.44	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		F350 PICKUP(101)			2.5		\$ 13.86	\$ -	\$ 34.65	\$ -	\$ 34.65	100.0%	\$ 34.65	\$ 24.26	\$ -
		FRONT END LOADER(206)			0.5		\$ 52.50	\$ -	\$ 26.25	\$ -	\$ 26.25	100.0%	\$ 26.25	\$ 18.38	\$ -
		Col Patch (ton)				3.8	\$ 117.64	\$ -	\$ -	\$ 447.03	\$ 447.03	100.0%	\$ 447.03	\$ 312.92	\$ -
		3/4" GRAVEL (CU YDS)				-	\$ 9.00	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
				3.0	3.0	3.8		\$ 39.63	\$ 60.90	\$ 447.03	\$ 547.56		\$ 547.56	\$ 383.29	\$ -
**Total Roadway width stayed the same. Patched then chipsealed							100.0% =Spot patching								
Hired Services															
Hopkinsd Sand & Gravel - Added Town gravel							\$ -	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
							\$ -	\$ -	\$ -	\$ -	\$ -		\$ -	\$ -	\$ -
Guy Lohman				\$ 26.24	0.0		\$ -	\$ -	\$ -	TOTAL COST	\$ 547.56		\$ 547.56	\$ 383.29	\$ -
				\$ -	0.0		\$ -	\$ -	\$ -			100%		70%	0%
Brad Huser				\$ 13.21	3.0		\$ 39.63	\$ 39.63	\$ -	Replace	\$ 547.56				
				\$ -	0.0		\$ -	\$ -	\$ -	Improve	\$ -	100.0%	\$ 39.63	\$ 27.74	
							\$ 39.63	\$ 39.63	\$ -		\$ 547.56				
DUMP TRUCK				\$ 57.00	0.0		\$ -	\$ -	\$ -						
FRONT END LOADER(206)				\$ 52.50	0.5		\$ 26.25	\$ 26.25	\$ -						
J.D. GRADER (308)				\$ 71.44	0.0		\$ -	\$ -	\$ -						
F350 PICKUP(101)				\$ 13.86	2.5		\$ 34.65	\$ 34.65	\$ -			100.0%	\$ 60.90	\$ 42.63	
							\$ 60.90	\$ 60.90	\$ -						
3/4" GRAVEL (ton)				\$ 9.00	0.00		\$ -	\$ -	\$ -			100.0%	\$ 447.03	\$ 312.92	
Col Patch				\$ 117.64	3.8		\$ 447.03					70% REIMBURSEMENT = \$ 383.29			



- 1 DEERPATH 30
- 2 DEERPATH 32
- 3 DEERPATH 34
- 4 SETTING SLUGS
- 5 SETTING SUN 1100
- 6 SETTING SUN 01
- 7 DEERPATH 34A
- 8 HONEY BEE 10
- 9 DEERPATH 34
- 10 DEERPATH 34SS
- 11 DEERPATH 30C
- 12 DEERPATH 30
- 13 HONEY BEE 10SS
- 14 WILDLIFE 34SS 10
- 15 WILDLIFE 34 10
- 16 WILDLIFE 34 10

- 55 FOX HEDGE DR
56 BLO MING DR
57 WACHS N ST apt
58 100 WINDY
59 FOX HEDGE PASS
60 FOX HEDGE CT
61 FOX HEDGE TRWAY
62 MORNING STAR LN
63 MORNING STAR CT
64 RUNWOOD RD
65 WHITE BIRCH CT
66 WHITE BIRCH CT
67 ASPEN HILL CT
68 ASPEN HILL CT
69 ASPEN HILL LN
70 ASPEN HILL LN

INVOICE

Page 1 of 1

From: **Monarch Paving**
P.O. Box 346
Turtle Lake WI 54889

715-268-2687

Invoice #: 5500018006
Date: 11/11/11
Customer No: 550161

Sold To: **Town of Jackson**
4742 County Road A
Webster, WI 54893

Delivered To:

Sale Date	Ticket	Units	UM	Unit Price	Matl Total	Haul Total	Tax Code	Tax	Total
MATERIAL:	105 HFE Mix								
11/8/11		22.520	TON	117 6400 E	2,649.25	0.00	WI00GV	0.00	2,649.25
Total:	Material	HFE Mix			2,649.25	0.00		0.00	2,649.25
Total Invoice:					2,649.25	0.00		0.00	2,649.25

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENT

Wisconsin Department of Transportation
DT2069 9/2013

Office Use Only

Claim No. _____

Local Government Town of Jackson		County Burnett	
Disaster Date (m/d/yyyy) 7/1/2011		Date of Inspection (m/d/yyyy)	Inspected By Lance Burger
Site Number 2011-23 (72)	Road Name Thompson Rd, Thompson Bay Road	Township, Range and Section T40NN, R15W Sec.25,36	Roadway Width 24', 18'
Material Type asphalt	Sub-Structure gravel	Bridge/Culvert Span	
☐ Road Closed ☐ Road Impassable ☒ Damage to Highway in Response to Event \$ 86.34 (1g)(2)	Nature and Extent of Damage Logging turck damage, spot patched broken edges, pot holes due to logging trucks		
☒ Final Costs ☐ Estimated Costs		☐ Site Denied (Explain)	

Labor				
Name of Person or Job Position	Hours	Rate	Replacement	Improvement
Brad Huser - laborer	3.0	\$ 13.21	\$ 39.63	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Labor Total	3.0		\$ 39.63	\$

Equipment					
Equipment Description/Type	Size or HP	Hours	Rate	Replacement	Improvement
444H JD Loader - 207		0.5	\$ 52.50	\$ 26.25	\$
Chev - 101		2.5	\$ 13.86	\$ 34.65	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
Equipment Total		3.0		\$ 60.90	\$

PLEASE ATTACH ALL INVOICES

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENT *(continued)*

Wisconsin Department of Transportation DT2069

Materials				
Materials Description/Type	Quantity	Rate/Unit	Replacement	Improvement
Cold patch HFE (Ton)	3.8	\$ 117.64	\$ 447.03	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Materials Total			\$ 447.03	\$

Contract or Force Account Work		
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
Contract or Force Account Work Total	\$	\$

Site Number <u>2011-23 (72)</u> : Total Cost of Damage	\$ 547.56	\$
---	------------------	-----------

PLEASE ATTACH ALL INVOICES

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENT

Wisconsin Department of Transportation
DT2069 9/2013

Office Use Only

Claim No. _____

Local Government Town of Jackson		County Burnett	
Disaster Date (m/d/yyyy) 7/1/2011		Date of Inspection (m/d/yyyy)	Inspected By Lance Burger
Site Number 2011-27(76)	Road Name Pratt Rd	Township, Range and Section T40NN, R15W Sec.27,34	Roadway Width 20'
Material Type Asphalt	Sub-Structure gravel	Bridge/Culvert Span	
☐ Road Closed ☐ Road Impassable ☒ Damage to Highway in Response to Event \$ 86.34 (1g)(2)	Nature and Extent of Damage Haul Route, logging truck damage, road edges cracked or broken, pot holes broken out, spot patched areas		
☒ Final Costs ☐ Estimated Costs		☐ Site Denied (Explain)	

Labor				
Name of Person or Job Position	Hours	Rate	Replacement	Improvement
Guy Lohman - foreman	4.0	\$ 26.24	\$ 104.96	\$
Brad Huser - laborer	4.0	\$ 13.21	\$ 52.84	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Labor Total	8.0		\$ 157.80	\$

Equipment					
Equipment Description/Type	Size or HP	Hours	Rate	Replacement	Improvement
444H JD Loader - 207		1.0	\$ 52.50	\$ 52.50	\$
Chev truck - 101		4.0	\$ 13.86	\$ 55.44	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
Equipment Total		5.0		\$ 107.94	\$

PLEASE ATTACH ALL INVOICES

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENT *(continued)*

Wisconsin Department of Transportation DT2069

Materials				
Materials Description/Type	Quantity	Rate/Unit	Replacement	Improvement
Cold Patch HFE (Ton)	3.8	\$ 117.64	\$ 447.03	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Materials Total			\$ 447.03	\$

Contract or Force Account Work		
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
Contract or Force Account Work Total	\$	\$

Site Number <u>2011-27 (76)</u> : Total Cost of Damage	\$ 712.77	\$
--	-----------	----

PLEASE ATTACH ALL INVOICES

Town of Jackson, Burnett County

DATE	EMPLOYEE Name	EQUIPMENT (Class)	MATERIAL	LABOR HOURS	EQUIPMENT HOURS	MATERIALS	UNIT COST	LABOR COSTS	EQUIPMENT COSTS	MATERIAL COSTS	TOTAL COST	Replace %	Replace \$ Value	70% Reimburse	Non- participating Improvement
2011	Guy Lohman	ROAD FOREMAN		4.0			\$ 26.24	\$ 104.96	\$ -	\$ -	\$ 104.96	100.0%	\$ 104.96	\$ 73.47	\$ -
	Brad Huser	LABORER		4.0			\$ 13.21	\$ 52.84	\$ -	\$ -	\$ 52.84	100.0%	\$ 52.84	\$ 36.99	\$ -
		DUMP TRUCK 1118)			0.0		\$ 57.00	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		J.D. GRADER (308)			0.0		\$ 71.44	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		F350 PICKUP(101)			4.0		\$ 13.86	\$ -	\$ 55.44	\$ -	\$ 55.44	100.0%	\$ 55.44	\$ 38.81	\$ -
		FRONT END LOADER(206)			1.0		\$ 52.50	\$ -	\$ 52.50	\$ -	\$ 52.50	100.0%	\$ 52.50	\$ 36.75	\$ -
		Col Patch (Ton)				3.8	\$ 117.64	\$ -	\$ -	\$ 447.03	\$ 447.03	100.0%	\$ 447.03	\$ 312.92	\$ -
		3/4" GRAVEL (CU YDS)				-	\$ 8.65	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
				8.0	5.0	3.8		\$ 157.80	\$ 107.94	\$ 447.03	\$ 712.77		\$ 712.77	\$ 498.94	\$ -

**Total Roadway width stayed the same.

100.0% =Spot patching

Hired Services

Hopkinsd Sand & Gravel - Added Town gravel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	--------	------	------	------	------

	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	------	------	------	------	------

Guy Lohman	\$ 26.24	4.0	\$ 104.96	\$ 104.96	\$ -	TOTAL COST	\$ 712.77	\$ 712.77	\$ 498.94	\$ -
	\$ -	0.0	\$ -	\$ -	\$ -			100%	70%	0%
Brad Huser	\$ 13.21	4.0	\$ 52.84	\$ 52.84	\$ -	Replace	\$ 712.77			
	\$ -	0.0	\$ -	\$ -	\$ -	Improve	\$ -	100.0%	\$ 157.80	\$ 110.46
			\$ 157.80	\$ 157.80	\$ -		\$ 712.77			
DUMP TRUCK	\$ 57.00	0.0	\$ -	\$ -	\$ -					
FRONT END LOADER(206)	\$ 52.50	1.0	\$ 52.50	\$ 52.50	\$ -					
J.D. GRADER (308)	\$ 71.44	0.0	\$ -	\$ -	\$ -					
F350 PICKUP(101)	\$ 13.86	4.0	\$ 55.44	\$ 55.44	\$ -			100.0%	\$ 107.94	\$ 75.56
			\$ 107.94	\$ 107.94	\$ -					
3/4" GRAVEL (ton)	\$ 8.65	0.00	\$ -	\$ -	\$ -			100.0%	\$ 447.03	\$ 312.92
Col Patch (Ton)	\$ 117.64	3.8	\$ 447.03					70% REIMBURSEMENT =	\$ 498.94	

Copyright © 2010 RedBarn Plat Books & Cartographic Services

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENTWisconsin Department of Transportation
DT2069 9/2013

Office Use Only

Claim No. _____

Local Government Town of Jackson		County Burnett	
Disaster Date (m/d/yyyy) 7/1/2011		Date of Inspection (m/d/yyyy)	Inspected By Lance Burger
Site Number 2011-33 (82)	Road Name Bridle Road	Township, Range and Section <u>T40NN, R15W Sec.22</u>	Roadway Width 18'
Material Type gravel	Sub-Structure gravel	Bridge/Culvert Span	
☐ Road Closed ☐ Road Impassable ☒ Damage to Highway in Response to Event \$ 86.34 (1g)(2)	Nature and Extent of Damage Logging truck damage to hill, heavy rutting, soft. added gravel to hill, leveled graded ruts out of road		
☒ Final Costs ☐ Estimated Costs		☐ Site Denied (Explain)	

Labor

Name of Person or Job Position	Hours	Rate	Replacement	Improvement
Guy Lohman - Foreman	3.5	\$ 26.24	\$ 91.84	\$
Brad Huser - Laborer	2.0	\$ 13.21	\$ 26.42	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Labor Total	5.5		\$ 118.26	\$

Equipment

Equipment Description/Type	Size or HP	Hours	Rate	Replacement	Improvement
444H JD Loader - 207		0.5	\$ 52.50	\$ 26.25	\$
Tandem- 118		1.0	\$ 57.00	\$ 57.00	\$
772D JD Grader- 308		2.0	\$ 71.44	\$ 142.88	\$
JD Tractor - 224		2.0	\$ 37.80	\$ 75.60	\$
Spring rake - 919		2.0	\$ 12.18	\$ 24.36	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
Equipment Total		7.5		\$ 326.09	\$

PLEASE ATTACH ALL INVOICES

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENT *(continued)*

Wisconsin Department of Transportation DT2069

Materials				
Materials Description/Type	Quantity	Rate/Unit	Replacement	Improvement
Clark Pit gravel	36 ton	\$ 9.20	\$ 331.20	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Materials Total			\$ 331.20	\$

Contract or Force Account Work		
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
Contract or Force Account Work Total	\$	\$

Site Number <u>2011-33 (82)</u> : Total Cost of Damage	\$ 775.55	\$
---	------------------	-----------

PLEASE ATTACH ALL INVOICES

Town of Jackson, Burnett County

DATE	EMPLOYEE Name	EQUIPMENT (Class)	MATERIAL	LABOR HOURS	EQUIPMENT HOURS	MATERIALS	UNIT COST	LABOR COSTS	EQUIPMENT COSTS	MATERIAL COSTS	TOTAL COST	Replace %	Replace \$ Value	70% Reimburse	Non- participating Improvement
2011	Guy Lohman	ROAD FOREMAN		3.5			\$ 26.24	\$ 91.84	\$ -	\$ -	\$ 91.84	100.0%	\$ 91.84	\$ 64.29	\$ -
	Brad Huser	LABORER		2.0			\$ 13.21	\$ 26.42	\$ -	\$ -	\$ 26.42	100.0%	\$ 26.42	\$ 18.49	\$ -
		DUMP TRUCK 1118)			1.0		\$ 57.00	\$ -	\$ 57.00	\$ -	\$ 57.00	100.0%	\$ 57.00	\$ 39.90	\$ -
		J.D. GRADER (308)			2.0		\$ 71.44	\$ -	\$ 142.88	\$ -	\$ 142.88	100.0%	\$ 142.88	\$ 100.02	\$ -
		F350 PICKUP(101)			0.0		\$ 13.52	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		FRONT END LOADER(206)			0.5		\$ 52.50	\$ -	\$ 26.25	\$ -	\$ 26.25	100.0%	\$ 26.25	\$ 18.38	\$ -
		J.D. TRACTOR (224)			2.0		\$ 37.80	\$ -	\$ 75.60	\$ -	\$ 75.60	100.0%	\$ 75.60	\$ 52.92	\$ -
		Spring rake (919)			2.0		\$ 12.18	\$ -	\$ 24.36	\$ -	\$ 24.36	100.0%	\$ 24.36	\$ 17.05	\$ -
		Col Patch				0	\$ 51.73	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		3/4" GRAVEL (CU YDS)				36.00	\$ 9.20	\$ -	\$ -	\$ 331.20	\$ 331.20	100.0%	\$ 331.20	\$ 231.84	\$ -
				5.5	7.5	36.0		\$ 118.26	\$ 326.09	\$ 331.20	\$ 775.55		\$ 775.55	\$ 542.89	\$ -

**Total Roadway width stayed the same.

100.0% =Removed debris & Graveled

Hired Services

Hopkinsd Sand & Gravel - Added Town gravel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	--------	------	------	------

	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	------	------	------	------

Guy Lohman	\$ 26.24	3.5	\$ 91.84	TOTAL COST	\$ 775.55	\$ 775.55	\$ 542.89	\$ -
	\$ -	0.0	\$ -			100%	70%	0%
Brad Huser	\$ 13.21	2.0	\$ 26.42	Replace	\$ 775.55			
	\$ -	0.0	\$ -	Improve	\$ -			
			\$ 118.26		\$ 775.55			
DUMP TRUCK	\$ 57.00	1.0	\$ 57.00					
FRONT END LOADER(206)	\$ 52.50	0.5	\$ 26.25					
J.D. GRADER (308)	\$ 71.44	2.0	\$ 142.88					
J.D. TRACTOR (224)	\$ 37.80	2.0	\$ 75.60					
Spring rake (919)	\$ 12.18	2.0	\$ 24.36					
F350 PICKUP(101)	\$ 13.52	0.0	\$ -					
			\$ 326.09					
3/4" GRAVEL (ton)	\$ 9.20	36.00	\$ 331.20					
Col Patch	\$ 51.73	0	\$ -			70% REIMBURSEMENT =	\$ 542.89	

Town of Jackson, Burnett County

DATE	EMPLOYEE Name	EQUIPMENT (Class)	MATERIAL	LABOR HOURS	EQUIPMENT HOURS	MATERIALS	UNIT COST	LABOR COSTS	EQUIPMENT COSTS	MATERIAL COSTS	TOTAL COST	Replace %	Replace \$ Value	70% Reimburse	Non- participating Improvement
2011	Guy Lohman	ROAD FOREMAN		9.0			\$ 26.24	\$ 236.16	\$ -	\$ -	\$ 236.16	100.0%	\$ 236.16	\$ 165.31	\$ -
	Brad Huser	LABORER		0.0			\$ 13.21	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		DUMP TRUCK 1118)			2.0		\$ 57.00	\$ -	\$ 114.00	\$ -	\$ 114.00	100.0%	\$ 114.00	\$ 79.80	\$ -
		J.D. GRADER (308)			4.5		\$ 71.44	\$ -	\$ 321.48	\$ -	\$ 321.48	100.0%	\$ 321.48	\$ 225.04	\$ -
		F350 PICKUP(101)			0.0		\$ 13.52	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		FRONT END LOADER(206)			2.5		\$ 52.50	\$ -	\$ 131.25	\$ -	\$ 131.25	100.0%	\$ 131.25	\$ 91.88	\$ -
		Col Patch				0	\$ 51.73	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		3/4" GRAVEL (ton)				38.80	\$ 9.20	\$ -	\$ -	\$ 356.96	\$ 356.96	100.0%	\$ 356.96	\$ 249.87	\$ -
				9.0	9.0	38.8		\$ 236.16	\$ 566.73	\$ 356.96	\$ 1,159.85		\$ 1,159.85	\$ 811.90	\$ -

**Total Roadway width stayed the same.

100.0% =Gravel

Hired Services

Hopkinsd Sand & Gravel - Added Town gravel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	--------	------	------	------	------


	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	------	------	------	------	------

Guy Lohman	\$ 26.24	9.0	\$ 236.16	\$ 236.16	\$ -	TOTAL COST	\$ 1,159.85	\$ 1,159.85	\$ 811.90	\$ -
	\$ -	0.0	\$ -	\$ -	\$ -			100%	70%	0%
Brad Huser	\$ 13.21	0.0	\$ -	\$ -	\$ -	Replace	\$ 1,159.85			
	\$ -	0.0	\$ -	\$ -	\$ -	Improve	\$ -	100.0%	\$ 236.16	\$ 165.31
			\$ 236.16	\$ 236.16	\$ -		\$ 1,159.85			
DUMP TRUCK	\$ 57.00	2.0	\$ 114.00	\$ 114.00	\$ -					
FRONT END LOADER(206)	\$ 52.50	2.5	\$ 131.25	\$ 131.25	\$ -					
J.D. GRADER (308)	\$ 71.44	4.5	\$ 321.48	\$ 321.48	\$ -					
F350 PICKUP(101)	\$ 13.52	0.0	\$ -	\$ -	\$ -			100.0%	\$ 566.73	\$ 396.71
			\$ 566.73	\$ 566.73	\$ -					
3/4" GRAVEL (ton)	\$ 9.20	38.80	\$ 356.96	\$ 356.96	\$ -			100.0%	\$ 356.96	\$ 249.87
Col Patch	\$ 51.73	0	\$ -					70% REIMBURSEMENT = \$ 811.90		

Town Jackson

SITE 2011-35

Copyright © 2010 RedBarn Plat Books & Cartographic Services

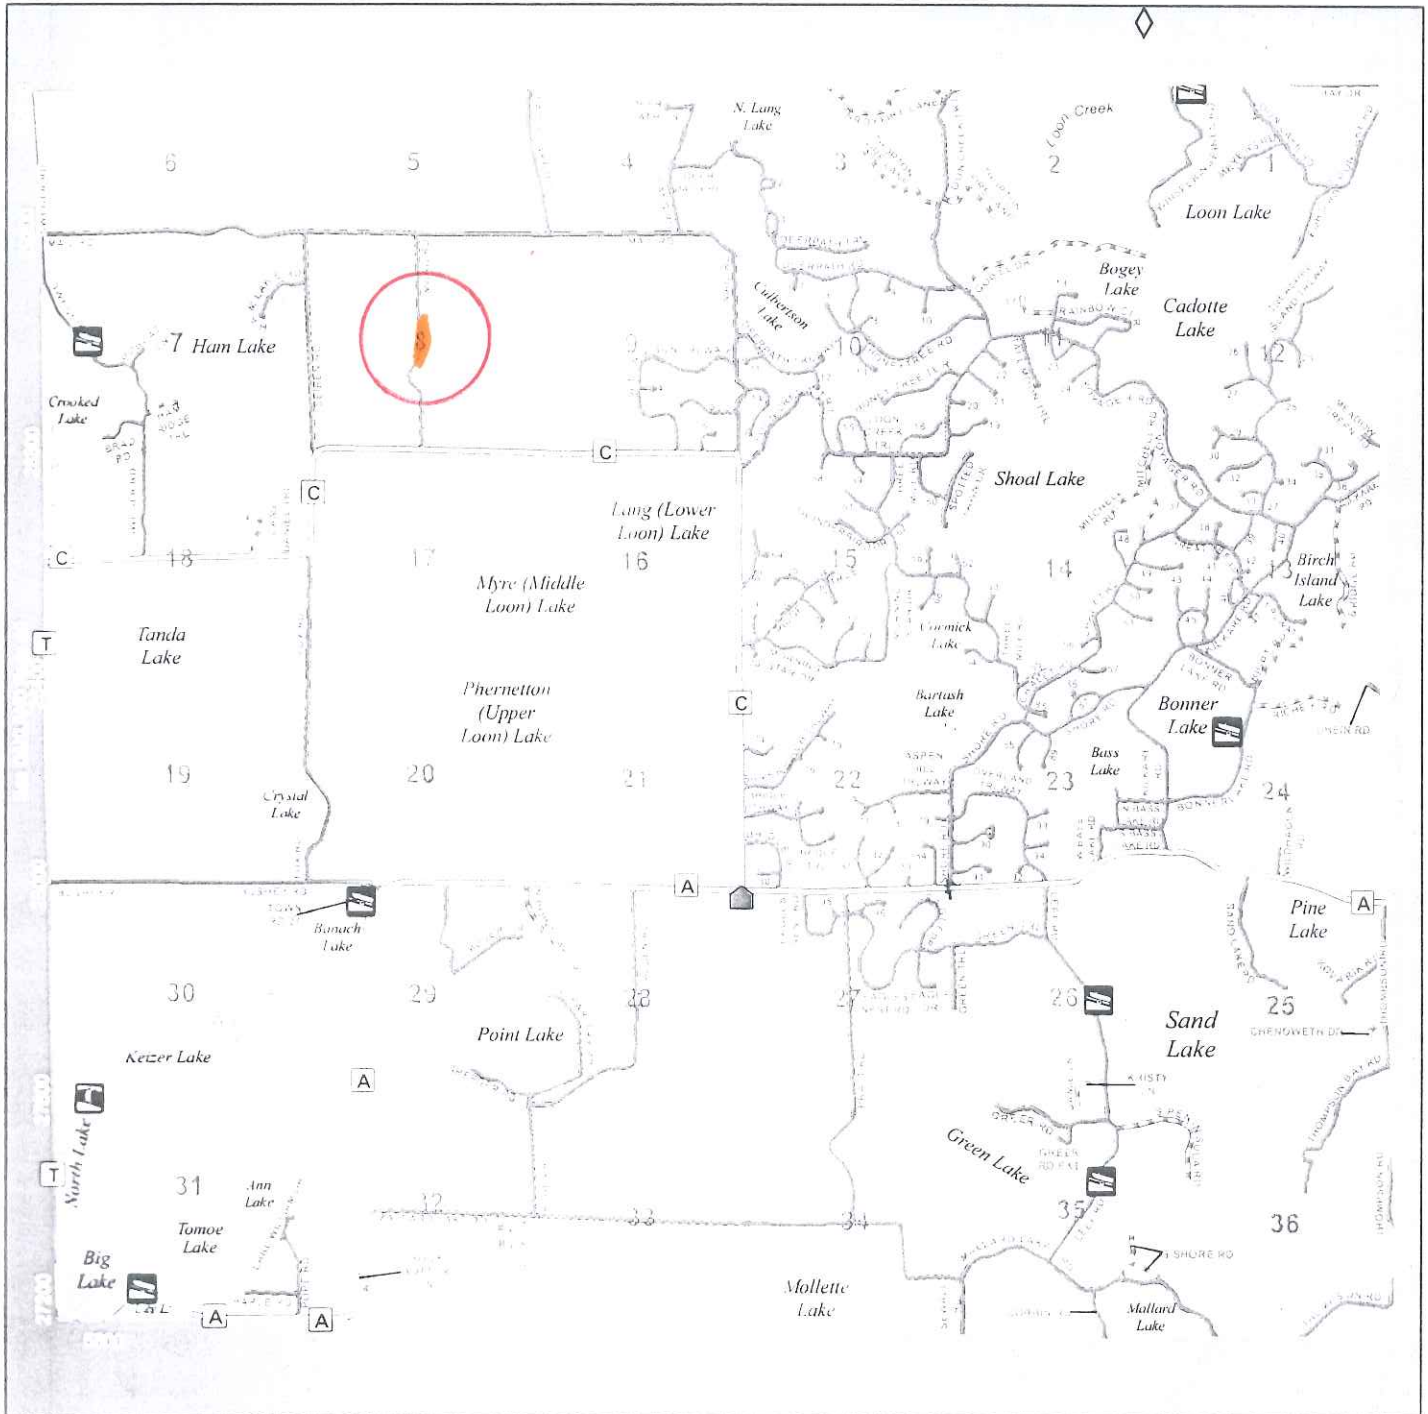

1. 1st 1/2 Sec 17
2. 2nd 1/2 Sec 17
3. 3rd 1/2 Sec 17
4. 4th 1/2 Sec 17
5. 5th 1/2 Sec 17
6. 6th 1/2 Sec 17
7. 7th 1/2 Sec 17
8. 8th 1/2 Sec 17
9. 9th 1/2 Sec 17
10. 10th 1/2 Sec 17
11. 11th 1/2 Sec 17
12. 12th 1/2 Sec 17
13. 13th 1/2 Sec 17
14. 14th 1/2 Sec 17
15. 15th 1/2 Sec 17
16. 16th 1/2 Sec 17
17. 17th 1/2 Sec 17
18. 18th 1/2 Sec 17
19. 19th 1/2 Sec 17
20. 20th 1/2 Sec 17
21. 21st 1/2 Sec 17
22. 22nd 1/2 Sec 17
23. 23rd 1/2 Sec 17
24. 24th 1/2 Sec 17
25. 25th 1/2 Sec 17
26. 26th 1/2 Sec 17
27. 27th 1/2 Sec 17
28. 28th 1/2 Sec 17
29. 29th 1/2 Sec 17
30. 30th 1/2 Sec 17
31. 31st 1/2 Sec 17
32. 32nd 1/2 Sec 17
33. 33rd 1/2 Sec 17
34. 34th 1/2 Sec 17
35. 35th 1/2 Sec 17
36. 36th 1/2 Sec 17

17. MAJESTIC WAY
18. RAINBOW CT
19. SPOTTED FAWN CT
20. SPOTTED FAWN CT
21. TALL MOON CT
22. TALL MOON CT
23. TALL MOON CT
24. TALL MOON CT
25. TREASURE ISLAND DR
26. TREASURE ISLAND DR
27. TREASURE ISLAND DR
28. TREASURE ISLAND DR
29. DEER LODGE DR
30. DEER LODGE DR
31. DEER LODGE DR
32. DEER LODGE DR

33. DEER LODGE DR
34. DEER LODGE DR
35. DEER LODGE DR
36. DEER LODGE DR
37. DEER LODGE DR
38. DEER LODGE DR
39. DEER LODGE DR
40. DEER LODGE DR
41. DEER LODGE DR
42. DEER LODGE DR
43. DEER LODGE DR
44. DEER LODGE DR
45. DEER LODGE DR
46. DEER LODGE DR
47. DEER LODGE DR
48. DEER LODGE DR
49. DEER LODGE DR
50. DEER LODGE DR
51. DEER LODGE DR
52. DEER LODGE DR
53. DEER LODGE DR
54. DEER LODGE DR
55. DEER LODGE DR
56. DEER LODGE DR
57. DEER LODGE DR
58. DEER LODGE DR
59. DEER LODGE DR
60. DEER LODGE DR
61. DEER LODGE DR
62. DEER LODGE DR
63. DEER LODGE DR
64. DEER LODGE DR
65. DEER LODGE DR
66. DEER LODGE DR
67. DEER LODGE DR
68. DEER LODGE DR
69. DEER LODGE DR
70. DEER LODGE DR
71. DEER LODGE DR
72. DEER LODGE DR
73. DEER LODGE DR
74. DEER LODGE DR
75. DEER LODGE DR
76. DEER LODGE DR
77. DEER LODGE DR
78. DEER LODGE DR
79. DEER LODGE DR
80. DEER LODGE DR
81. DEER LODGE DR
82. DEER LODGE DR
83. DEER LODGE DR
84. DEER LODGE DR
85. DEER LODGE DR
86. DEER LODGE DR
87. DEER LODGE DR
88. DEER LODGE DR
89. DEER LODGE DR
90. DEER LODGE DR
91. DEER LODGE DR
92. DEER LODGE DR
93. DEER LODGE DR
94. DEER LODGE DR
95. DEER LODGE DR
96. DEER LODGE DR
97. DEER LODGE DR
98. DEER LODGE DR
99. DEER LODGE DR
100. DEER LODGE DR

101. DEER LODGE DR
102. DEER LODGE DR
103. DEER LODGE DR
104. DEER LODGE DR
105. DEER LODGE DR
106. DEER LODGE DR
107. DEER LODGE DR
108. DEER LODGE DR
109. DEER LODGE DR
110. DEER LODGE DR
111. DEER LODGE DR
112. DEER LODGE DR
113. DEER LODGE DR
114. DEER LODGE DR
115. DEER LODGE DR
116. DEER LODGE DR
117. DEER LODGE DR
118. DEER LODGE DR
119. DEER LODGE DR
120. DEER LODGE DR
121. DEER LODGE DR
122. DEER LODGE DR
123. DEER LODGE DR
124. DEER LODGE DR
125. DEER LODGE DR
126. DEER LODGE DR
127. DEER LODGE DR
128. DEER LODGE DR
129. DEER LODGE DR
130. DEER LODGE DR
131. DEER LODGE DR
132. DEER LODGE DR
133. DEER LODGE DR
134. DEER LODGE DR
135. DEER LODGE DR
136. DEER LODGE DR
137. DEER LODGE DR
138. DEER LODGE DR
139. DEER LODGE DR
140. DEER LODGE DR
141. DEER LODGE DR
142. DEER LODGE DR
143. DEER LODGE DR
144. DEER LODGE DR
145. DEER LODGE DR
146. DEER LODGE DR
147. DEER LODGE DR
148. DEER LODGE DR
149. DEER LODGE DR
150. DEER LODGE DR

151. DEER LODGE DR
152. DEER LODGE DR
153. DEER LODGE DR
154. DEER LODGE DR
155. DEER LODGE DR
156. DEER LODGE DR
157. DEER LODGE DR
158. DEER LODGE DR
159. DEER LODGE DR
160. DEER LODGE DR
161. DEER LODGE DR
162. DEER LODGE DR
163. DEER LODGE DR
164. DEER LODGE DR
165. DEER LODGE DR
166. DEER LODGE DR
167. DEER LODGE DR
168. DEER LODGE DR
169. DEER LODGE DR
170. DEER LODGE DR
171. DEER LODGE DR
172. DEER LODGE DR
173. DEER LODGE DR
174. DEER LODGE DR
175. DEER LODGE DR
176. DEER LODGE DR
177. DEER LODGE DR
178. DEER LODGE DR
179. DEER LODGE DR
180. DEER LODGE DR
181. DEER LODGE DR
182. DEER LODGE DR
183. DEER LODGE DR
184. DEER LODGE DR
185. DEER LODGE DR
186. DEER LODGE DR
187. DEER LODGE DR
188. DEER LODGE DR
189. DEER LODGE DR
190. DEER LODGE DR
191. DEER LODGE DR
192. DEER LODGE DR
193. DEER LODGE DR
194. DEER LODGE DR
195. DEER LODGE DR
196. DEER LODGE DR
197. DEER LODGE DR
198. DEER LODGE DR
199. DEER LODGE DR
200. DEER LODGE DR

201. DEER LODGE DR
202. DEER LODGE DR
203. DEER LODGE DR
204. DEER LODGE DR
205. DEER LODGE DR
206. DEER LODGE DR
207. DEER LODGE DR
208. DEER LODGE DR
209. DEER LODGE DR
210. DEER LODGE DR
211. DEER LODGE DR
212. DEER LODGE DR
213. DEER LODGE DR
214. DEER LODGE DR
215. DEER LODGE DR
216. DEER LODGE DR
217. DEER LODGE DR
218. DEER LODGE DR
219. DEER LODGE DR
220. DEER LODGE DR
221. DEER LODGE DR
222. DEER LODGE DR
223. DEER LODGE DR
224. DEER LODGE DR
225. DEER LODGE DR
226. DEER LODGE DR
227. DEER LODGE DR
228. DEER LODGE DR
229. DEER LODGE DR
230. DEER LODGE DR
231. DEER LODGE DR
232. DEER LODGE DR
233. DEER LODGE DR
234. DEER LODGE DR
235. DEER LODGE DR
236. DEER LODGE DR
237. DEER LODGE DR
238. DEER LODGE DR
239. DEER LODGE DR
240. DEER LODGE DR
241. DEER LODGE DR
242. DEER LODGE DR
243. DEER LODGE DR
244. DEER LODGE DR
245. DEER LODGE DR
246. DEER LODGE DR
247. DEER LODGE DR
248. DEER LODGE DR
249. DEER LODGE DR
250. DEER LODGE DR

Wisconsin Department of Transportation
DT2069 9/2013

Claim No.

Equipment					
Equipment Description/Type	Size or HP	Hours	Rate	Replacement	Improvement
Tandem -118		2.0	\$ 57.00	\$ 114.00	\$
444H JD Loader - 207		3.0	\$ 52.50	\$ 157.50	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
Equipment Total		5.0		\$ 271.50	\$

1 of 2

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENT *(continued)*

Wisconsin Department of Transportation DT2069

Materials				
Materials Description/Type	Quantity	Rate/Unit	Replacement	Improvement
Gravel	36 ton	\$ 8.65	\$ 311.40	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Materials Total			\$ 311.40	\$

Contract or Force Account Work		
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
Contract or Force Account Work Total	\$	\$

Site Number <u>2011-8 (57)</u> : Total Cost of Damage	\$ 688.04	\$
---	-----------	----

PLEASE ATTACH ALL INVOICES

Town of Jackson, Burnett County

DATE	EMPLOYEE Name	EQUIPMENT (Class)	MATERIAL	LABOR HOURS	EQUIPMENT HOURS	MATERIALS	UNIT COST	LABOR COSTS	EQUIPMENT COSTS	MATERIAL COSTS	TOTAL COST	Replace %	Replace \$ Value	70% Reimburse	Non- participating Improvement
2011	Guy Lohman	ROAD FOREMAN		3.0			\$ 26.24	\$ 78.72	\$ -	\$ -	\$ 78.72	100.0%	\$ 78.72	\$ 55.10	\$ -
	Brad Huser	LABORER		2.0			\$ 13.21	\$ 26.42	\$ -	\$ -	\$ 26.42	100.0%	\$ 26.42	\$ 18.49	\$ -
		DUMP TRUCK 1118)			2.0		\$ 57.00	\$ -	\$ 114.00	\$ -	\$ 114.00	100.0%	\$ 114.00	\$ 79.80	\$ -
		J.D. GRADER (308)			0.0		\$ 71.44	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		F350 PICKUP(101)			0.0		\$ 13.86	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		FRONT END LOADER(206)			3.0		\$ 52.50	\$ -	\$ 157.50	\$ -	\$ 157.50	100.0%	\$ 157.50	\$ 110.25	\$ -
		Col Patch				0	\$ 51.73	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		3/4" GRAVEL (CU YDS)				36.00	\$ 8.65	\$ -	\$ -	\$ 311.40	\$ 311.40	100.0%	\$ 311.40	\$ 217.98	\$ -
				5.0	5.0	36.0		\$ 105.14	\$ 271.50	\$ 311.40	\$ 688.04		\$ 688.04	\$ 481.63	\$ -

**Total Roadway width stayed the same.

100.0% =Gravel


Hired Services

Hopkinsd Sand & Gravel - Added Town gravel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	--------	------	------	------	------

	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	------	------	------	------	------

Guy Lohman	\$ 26.24	3.0	\$ 78.72	\$ 78.72	\$ -	TOTAL COST	\$ 688.04	\$ 688.04	\$ 481.63	\$ -
	\$ -	0.0	\$ -	\$ -	\$ -			100%	70%	0%
Brad Huser	\$ 13.21	2.0	\$ 26.42	\$ 26.42	\$ -	Replace	\$ 688.04			
	\$ -	0.0	\$ -	\$ -	\$ -	Improve	\$ -	100.0%	\$ 105.14	\$ 73.60
			\$ 105.14	\$ 105.14	\$ -		\$ 688.04			
DUMP TRUCK	\$ 57.00	2.0	\$ 114.00	\$ 114.00	\$ -					
FRONT END LOADER(206)	\$ 52.50	3.0	\$ 157.50	\$ 157.50	\$ -					
J.D. GRADER (308)	\$ 71.44	0.0	\$ -	\$ -	\$ -					
F350 PICKUP(101)	\$ 13.86	0.0	\$ -	\$ -	\$ -			100.0%	\$ 271.50	\$ 190.05
			\$ 271.50	\$ 271.50	\$ -					
3/4" GRAVEL (ton)	\$ 8.65	36.00	\$ 311.40	\$ 311.40	\$ -			100.0%	\$ 311.40	\$ 217.98
Col Patch	\$ 51.73	0	\$ -					70% REIMBURSEMENT =	\$ 481.63	

Copyright © 2010 RedBarn Plat Books & Cartographic Services

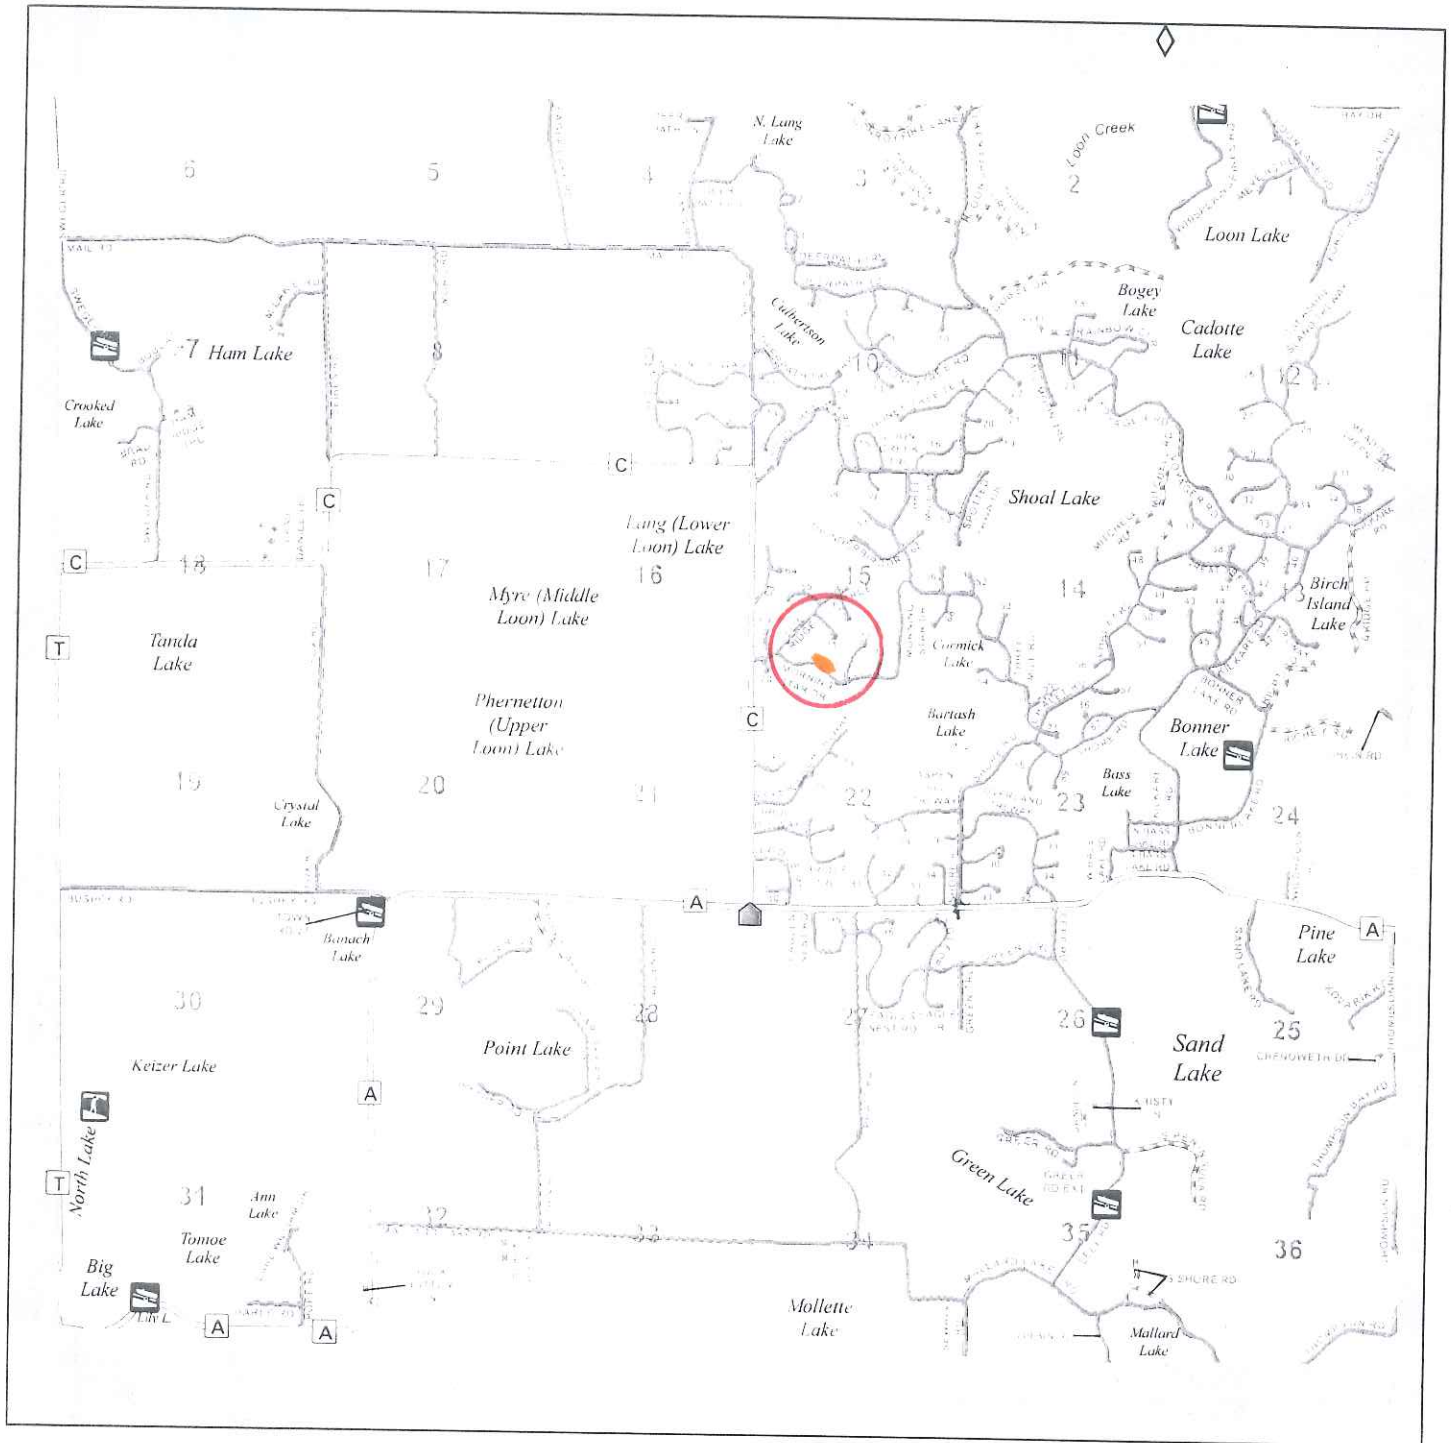

- 1 DEERPATH W/
- 2 DEERPATH DR
- 3 DEERPATH CT
- 4 EATING SUN DR
- 5 EATING SUN DR
- 6 EATING SUN CT
- 7 EATING SUN
- 8 EATING SUN DR
- 9 EATING SUN DR
- 10 EATING SUN DR
- 11 EATING SUN DR
- 12 EATING SUN DR
- 13 EATING SUN DR
- 14 EATING SUN DR
- 15 EATING SUN DR
- 16 EATING SUN DR
- 17 EATING SUN DR
- 18 EATING SUN DR
- 19 EATING SUN DR
- 20 EATING SUN DR
- 21 EATING SUN DR
- 22 EATING SUN DR
- 23 EATING SUN DR
- 24 EATING SUN DR
- 25 EATING SUN DR
- 26 EATING SUN DR
- 27 EATING SUN DR
- 28 EATING SUN DR
- 29 EATING SUN DR
- 30 EATING SUN DR
- 31 EATING SUN DR
- 32 EATING SUN DR
- 33 EATING SUN DR
- 34 EATING SUN DR
- 35 EATING SUN DR
- 36 EATING SUN DR
- 37 EATING SUN DR
- 38 EATING SUN DR
- 39 EATING SUN DR
- 40 EATING SUN DR
- 41 EATING SUN DR
- 42 EATING SUN DR
- 43 EATING SUN DR
- 44 EATING SUN DR
- 45 EATING SUN DR
- 46 EATING SUN DR
- 47 EATING SUN DR
- 48 EATING SUN DR
- 49 EATING SUN DR
- 50 EATING SUN DR
- 51 EATING SUN DR
- 52 EATING SUN DR
- 53 EATING SUN DR
- 54 EATING SUN DR
- 55 EATING SUN DR
- 56 EATING SUN DR
- 57 EATING SUN DR
- 58 EATING SUN DR
- 59 EATING SUN DR
- 60 EATING SUN DR
- 61 EATING SUN DR
- 62 EATING SUN DR
- 63 EATING SUN DR
- 64 EATING SUN DR
- 65 EATING SUN DR
- 66 EATING SUN DR
- 67 EATING SUN DR
- 68 EATING SUN DR
- 69 EATING SUN DR
- 70 EATING SUN DR
- 71 EATING SUN DR
- 72 EATING SUN DR
- 73 EATING SUN DR
- 74 EATING SUN DR
- 75 EATING SUN DR
- 76 EATING SUN DR
- 77 EATING SUN DR
- 78 EATING SUN DR
- 79 EATING SUN DR
- 80 EATING SUN DR
- 81 EATING SUN DR
- 82 EATING SUN DR
- 83 EATING SUN DR
- 84 EATING SUN DR
- 85 EATING SUN DR
- 86 EATING SUN DR
- 87 EATING SUN DR
- 88 EATING SUN DR
- 89 EATING SUN DR
- 90 EATING SUN DR
- 91 EATING SUN DR
- 92 EATING SUN DR
- 93 EATING SUN DR
- 94 EATING SUN DR
- 95 EATING SUN DR
- 96 EATING SUN DR
- 97 EATING SUN DR
- 98 EATING SUN DR
- 99 EATING SUN DR
- 100 EATING SUN DR

[illegible]

65 FOX HEDGE DR
66 WED WING LN
67 DAVES BLVD Apt
68 OLD WING LN
69 FOX HEDGE DR S
70 FOX HEDGE CT
71 FOX HEDGE TRLWAY
72 MOIR AND STAR LN
73 MORNING STAR CT
74 HUNWOOD RD
75 WHITE BIRCH CT
76 OLIVER BIRCH CT
77 ASPEN HILL PL
78 ASPEN HILL PL
79 ASPEN HILL LN
80 ASPEN HILL LN

91 DAYLIGHT WAY
92 DAYLIGHT TER
93 DAYLIGHT CT
94 DAYLIGHT RD
95 DAYLIGHT CT
96 DAYLIGHT
97 DAYTON DR
98 DAYTON HILL TRL
99 DAYTON HILL TER
100 OVERLAND RD
101 OVERLAND RD
102 OVERLAND CT
103 OVERLAND DR
104 OVERLAND TER
105 EAGLE CT

Wisconsin Department of Transportation
DT2069 9/2013

Claim No. _____

Equipment					
Equipment Description/Type	Size or HP	Hours	Rate	Replacement	Improvement
Tandem -118		2.0	\$ 57.00	\$ 114.00	\$
444H JD Loader - 207		1.0	\$ 52.50	\$ 52.50	\$
772 JD Grader - 308		2.0	\$ 71.44	\$ 142.88	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
Equipment Total		5.0		\$ 309.38	\$

1 of 2

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENT *(continued)*

Wisconsin Department of Transportation DT2069

Materials				
Materials Description/Type	Quantity	Rate/Unit	Replacement	Improvement
Gravel	36 ton	\$ 8.65	\$ 311.40	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Materials Total			\$ 311.40	\$

Contract or Force Account Work		
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
Contract or Force Account Work Total	\$	\$

Site Number <u>2011-9 (58)</u> : Total Cost of Damage	\$ 699.68	\$
---	-----------	----

PLEASE ATTACH ALL INVOICES

Town of Jackson, Burnett County

DATE	EMPLOYEE Name	EQUIPMENT (Class)	MATERIAL	LABOR HOURS	EQUIPMENT HOURS	MATERIALS	UNIT COST	LABOR COSTS	EQUIPMENT COSTS	MATERIAL COSTS	TOTAL COST	Replace %	Replace \$ Value	70% Reimburse	Non- participating Improvement
2011	Guy Lohman	ROAD FOREMAN		2.0			\$ 26.24	\$ 52.48	\$ -	\$ -	\$ 52.48	100.0%	\$ 52.48	\$ 36.74	\$ -
	Brad Huser	LABORER		2.0			\$ 13.21	\$ 26.42	\$ -	\$ -	\$ 26.42	100.0%	\$ 26.42	\$ 18.49	\$ -
		DUMP TRUCK 1118)			2.0		\$ 57.00	\$ -	\$ 114.00	\$ -	\$ 114.00	100.0%	\$ 114.00	\$ 79.80	\$ -
		J.D. GRADER (308)			2.0		\$ 71.44	\$ -	\$ 142.88	\$ -	\$ 142.88	100.0%	\$ 142.88	\$ 100.02	\$ -
		F350 PICKUP(101)			0.0		\$ 13.86	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		FRONT END LOADER(206)			1.0		\$ 52.50	\$ -	\$ 52.50	\$ -	\$ 52.50	100.0%	\$ 52.50	\$ 36.75	\$ -
		Col Patch				0	\$ 51.73	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		3/4" GRAVEL (CU YDS)				36.00	\$ 8.65	\$ -	\$ -	\$ 311.40	\$ 311.40	100.0%	\$ 311.40	\$ 217.98	\$ -
				4.0	5.0	36.0		\$ 78.90	\$ 309.38	\$ 311.40	\$ 699.68		\$ 699.68	\$ 489.78	\$ -

**Total Roadway width stayed the same.


100.0% =Gravel

Hired Services

Hopkinsd Sand & Gravel - Added Town gravel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	--------	------	------	------	------

	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	------	------	------	------	------

Guy Lohman	\$ 26.24	2.0	\$ 52.48	\$ 52.48	\$ -	TOTAL COST	\$ 699.68		\$ 699.68	\$ 489.78	\$ -
	\$ -	0.0	\$ -	\$ -	\$ -			100%		70%	0%
Brad Huser	\$ 13.21	2.0	\$ 26.42	\$ 26.42	\$ -	Replace	\$ 699.68				
	\$ -	0.0	\$ -	\$ -	\$ -	Improve	\$ -	100.0%	\$ 78.90	\$ 55.23	
			\$ 78.90	\$ 78.90	\$ -		\$ 699.68				
DUMP TRUCK	\$ 57.00	2.0	\$ 114.00	\$ 114.00	\$ -						
FRONT END LOADER(206)	\$ 52.50	1.0	\$ 52.50	\$ 52.50	\$ -						
J.D. GRADER (308)	\$ 71.44	2.0	\$ 142.88	\$ 142.88	\$ -						
F350 PICKUP(101)	\$ 13.86	0.0	\$ -	\$ -	\$ -			100.0%	\$ 309.38	\$ 216.57	
			\$ 309.38	\$ 309.38	\$ -						
3/4" GRAVEL (ton)	\$ 8.65	36.00	\$ 311.40	\$ 311.40	\$ -			100.0%	\$ 311.40	\$ 217.98	
Col Patch	\$ 51.73	0	\$ -					70% REIMBURSEMENT =	\$ 489.78		

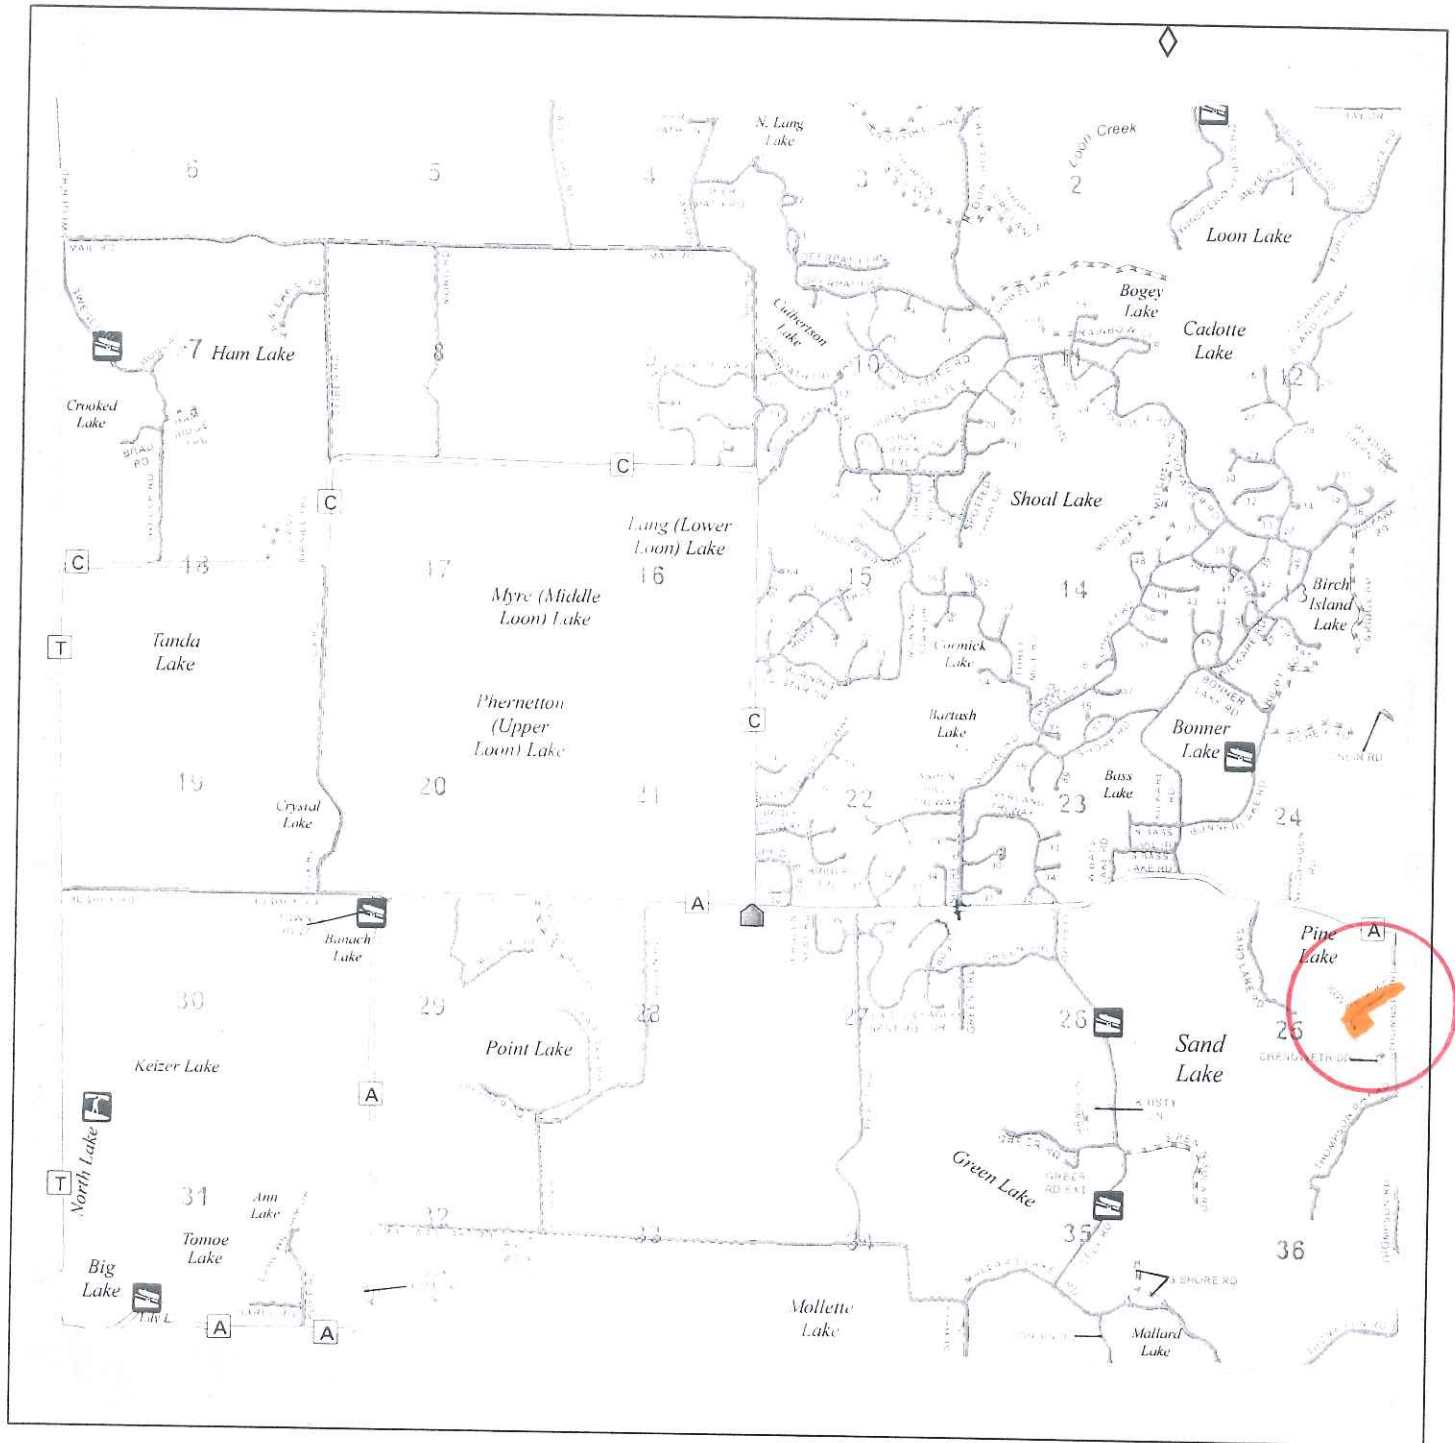

81 OVERLAND DR
 82 OVERLAND DR
 83 OVERLAND CT
 84 OVERLAND DR
 85 OVERLAND CT
 86 OVERLAND CT
 87 OVERLAND
 88 OVERLAND TRL
 89 OVERLAND HILL
 90 OVERLAND
 91 OVERLAND RD
 92 OVERLAND AVE CT
 93 OVERLAND DR
 94 OVERLAND DR
 95 OVERLAND DR
 96 OVERLAND DR

Wisconsin Department of Transportation
DT2069 9/2013

Claim No. _____

Equipment					
Equipment Description/Type	Size or HP	Hours	Rate	Replacement	Improvement
444H JD Loader- 207		1.0	\$ 53.34	\$ 53.34	\$
Tandem - 118		2.0	\$ 61.00	\$ 122.00	\$
772D JD Grader - 308		3.0	\$ 73.06	\$ 219.18	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
			\$	\$	\$
Equipment Total		6.0		\$ 394.52	\$

1 of 2

DISASTER DAMAGE AIDS REGION INVESTIGATION AND COST STATEMENT *(continued)*

Wisconsin Department of Transportation DT2069

Materials				
Materials Description/Type	Quantity	Rate/Unit	Replacement	Improvement
Clark Pit gravel	36 ton	\$ 9.20	\$ 331.20	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
		\$	\$	\$
Materials Total			\$ 331.20	\$

Contract or Force Account Work		
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
	\$	\$
Contract or Force Account Work Total	\$	\$

Site Number <u>2011-21 (70)</u> : Total Cost of Damage	\$ 852.50	\$
---	------------------	-----------

PLEASE ATTACH ALL INVOICES

Town of Jackson, Burnett County

DATE	EMPLOYEE Name	EQUIPMENT (Class)	MATERIAL	LABOR HOURS	EQUIPMENT HOURS	MATERIALS	UNIT COST	LABOR COSTS	EQUIPMENT COSTS	MATERIAL COSTS	TOTAL COST	Replace %	Replace \$ Value	70% Reimburse	Non- participating Improvement
2012	Guy Lohman	ROAD FOREMAN		3.0			\$ 27.73	\$ 83.19	\$ -	\$ -	\$ 83.19	100.0%	\$ 83.19	\$ 58.23	\$ -
	Brad Huser	LABORER		3.0			\$ 14.53	\$ 43.59	\$ -	\$ -	\$ 43.59	100.0%	\$ 43.59	\$ 30.51	\$ -
		DUMP TRUCK 1118)			2.0		\$ 61.00	\$ -	\$ 122.00	\$ -	\$ 122.00	100.0%	\$ 122.00	\$ 85.40	\$ -
		J.D. GRADER (308)			3.0		\$ 73.06	\$ -	\$ 219.18	\$ -	\$ 219.18	100.0%	\$ 219.18	\$ 153.43	\$ -
		F350 PICKUP(101)			0.0		\$ -	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		FRONT END LOADER(206)			1.0		\$ 53.34	\$ -	\$ 53.34	\$ -	\$ 53.34	100.0%	\$ 53.34	\$ 37.34	\$ -
		Col Patch				0	\$ -	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -
		3/4" GRAVEL (CU YDS)				36.00	\$ 9.20	\$ -	\$ -	\$ 331.20	\$ 331.20	100.0%	\$ 331.20	\$ 231.84	\$ -
				6.0	6.0	36.0		\$ 126.78	\$ 394.52	\$ 331.20	\$ 852.50		\$ 852.50	\$ 596.75	\$ -

**Total Roadway width stayed the same.

100.0% =Gravel

Hired Services

Hopkinsd Sand & Gravel - Added Town gravel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	100.0%	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	--------	------	------	------	------

	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
--	------	------	------	------	------	------	------	------	------	------

Guy Lohman	\$ 27.73	3.0	\$ 83.19	\$ 83.19	\$ -	TOTAL COST	\$ 852.50	\$ 852.50	\$ 596.75	\$ -
	\$ -	0.0	\$ -	\$ -	\$ -			100%	70%	0%
Brad Huser	\$ 14.53	3.0	\$ 43.59	\$ 43.59	\$ -	Replace	\$ 852.50			
	\$ -	0.0	\$ -	\$ -	\$ -	Improve	\$ -	100.0%	\$ 126.78	\$ 88.75
			\$ 126.78	\$ 126.78	\$ -		\$ 852.50			
DUMP TRUCK	\$ 61.00	2.0	\$ 122.00	\$ 122.00	\$ -					
FRONT END LOADER(206)	\$ 53.34	1.0	\$ 53.34	\$ 53.34	\$ -					
J.D. GRADER (308)	\$ 73.06	3.0	\$ 219.18	\$ 219.18	\$ -					
F350 PICKUP(101)	\$ -	0.0	\$ -	\$ -	\$ -			100.0%	\$ 394.52	\$ 276.16
			\$ 394.52	\$ 394.52	\$ -					
3/4" GRAVEL (ton)	\$ 9.20	36.00	\$ 331.20	\$ 331.20	\$ -			100.0%	\$ 331.20	\$ 231.84
Col Patch	\$ -	0	\$ -					70% REIMBURSEMENT =	\$ 596.75	

Hopkins Sand & Gravel Inc

27760 State Road 35
Webster, WI 54893
715-866-4157

Invoice

Date	Invoice #
6/26/2012	211758

Bill To
JACKSON TOWNSHIP % JEAN RADKE 4742 CTY RD A WEBSTER WI 548930

Ship To
STOCK PILE

Terms	Due Date	Ship Date
Net 30	7/26/2012	6/26/2012

Qty	Description	Price Each	Class	Amount
181.44	ROAD GRAVEL PER TON - CLARK TO STOCK PILE	9.20	W	1,669.25
Sales Tax (5.5%)				\$0.00
Total				\$1,669.25

e-mail:
info@hopkinsgravel.com

visit our website:
www.hopkinsgravel.com

