


CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2011

Project ID	1030-15-70	Highway	IH-41/94	Project Title	IH 94	Date of Letting	April 14, 2020
Work Type	HFST	County	Milwaukee	Project Limits	N-S & S-N CURVE THRU THE MITCHELL IC	Probable Date of Beginning	June 1, 2020

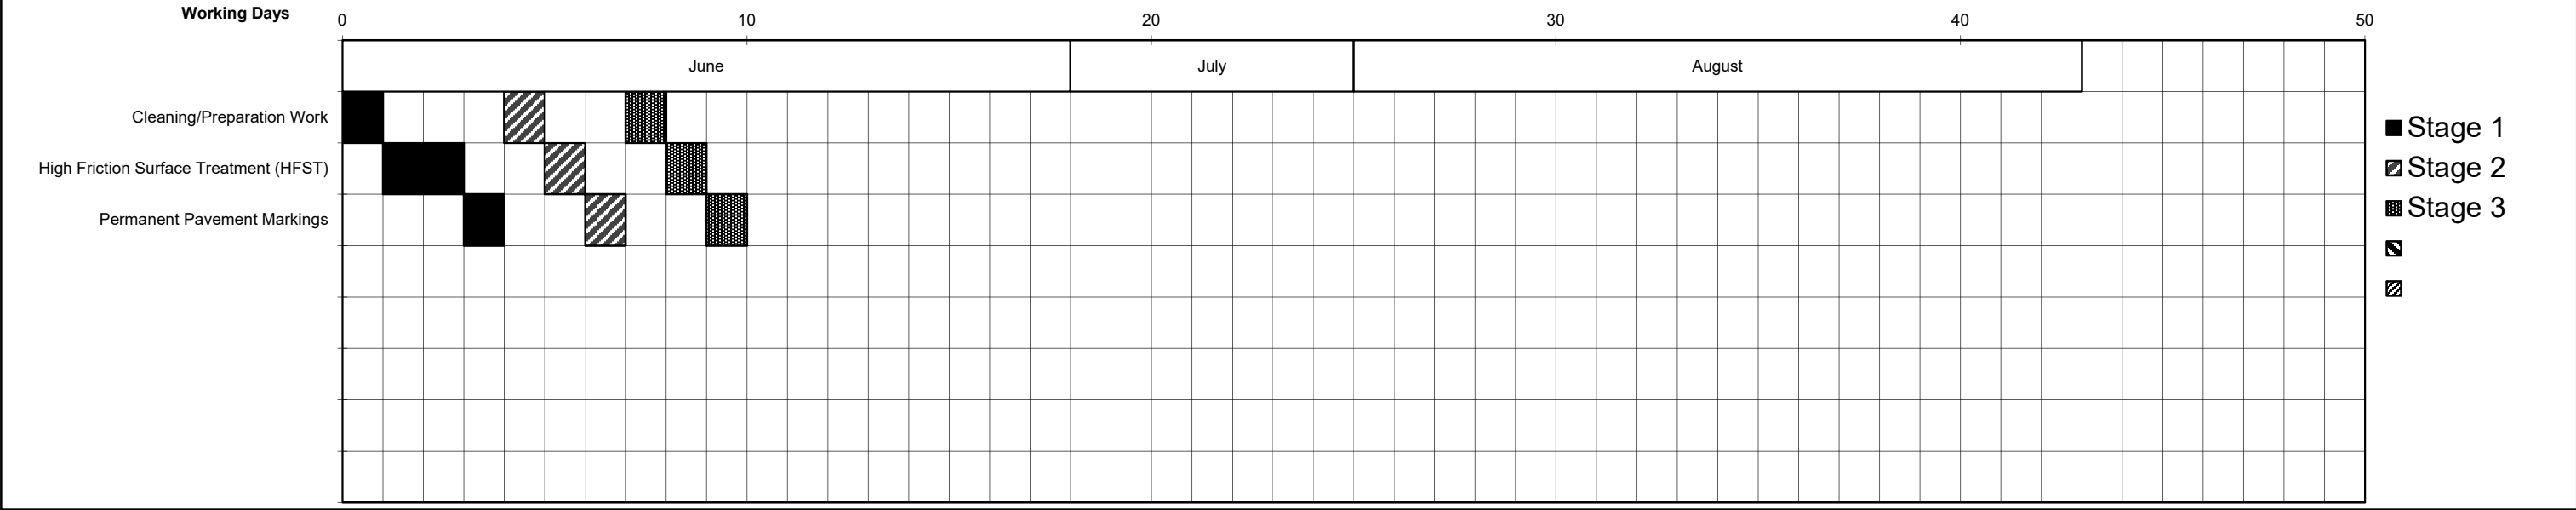

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3					
	Stage 1	Stage 2	Stage 3							Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
Cleaning/Preparation Work	1	1	1			3	DAY	1	1 / 1 / 1 / /	0	1	4	5	7	8				
High Friction Surface Treatment (HFST)	20,414	5,935	863			27,212	SY	18000	2 / 1 / 1 / /	1	3	5	6	8	9				
Permanent Pavement Markings	1	1	1			3	DAY	1	1 / 1 / 1 / /	3	4	6	7	9	10				

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
June	6/1/2020	6/30/2020	30	30	0	22	81	18	18
July	7/1/2020	7/31/2020	31	61	15	8	85	7	25
August	8/1/2020	8/31/2020	31	92	0	21	85	18	43

REMARKS

Work Restrictions: DNC (7/10/20 - 7/19/20)

Calendar Days	92
Working Days	43
Completion Date	September 1, 2020
Prepared By	Amanda Johansen & Nicholas Becker
