

CONTRACT TIME FOR COMPLETION


Wisconsin Department of Transportation DT1923 04/2011

Project ID 2040-20-70
Work Type BRIDGE REHABILITATION

Highway STH 100
County MILWAUKEE

Project Title RYAN RD
Project Limits BRIDGE OVER RR - B-40-0530

Date of Letting May 10, 2022
Probable Date of Beginning April 3, 2023

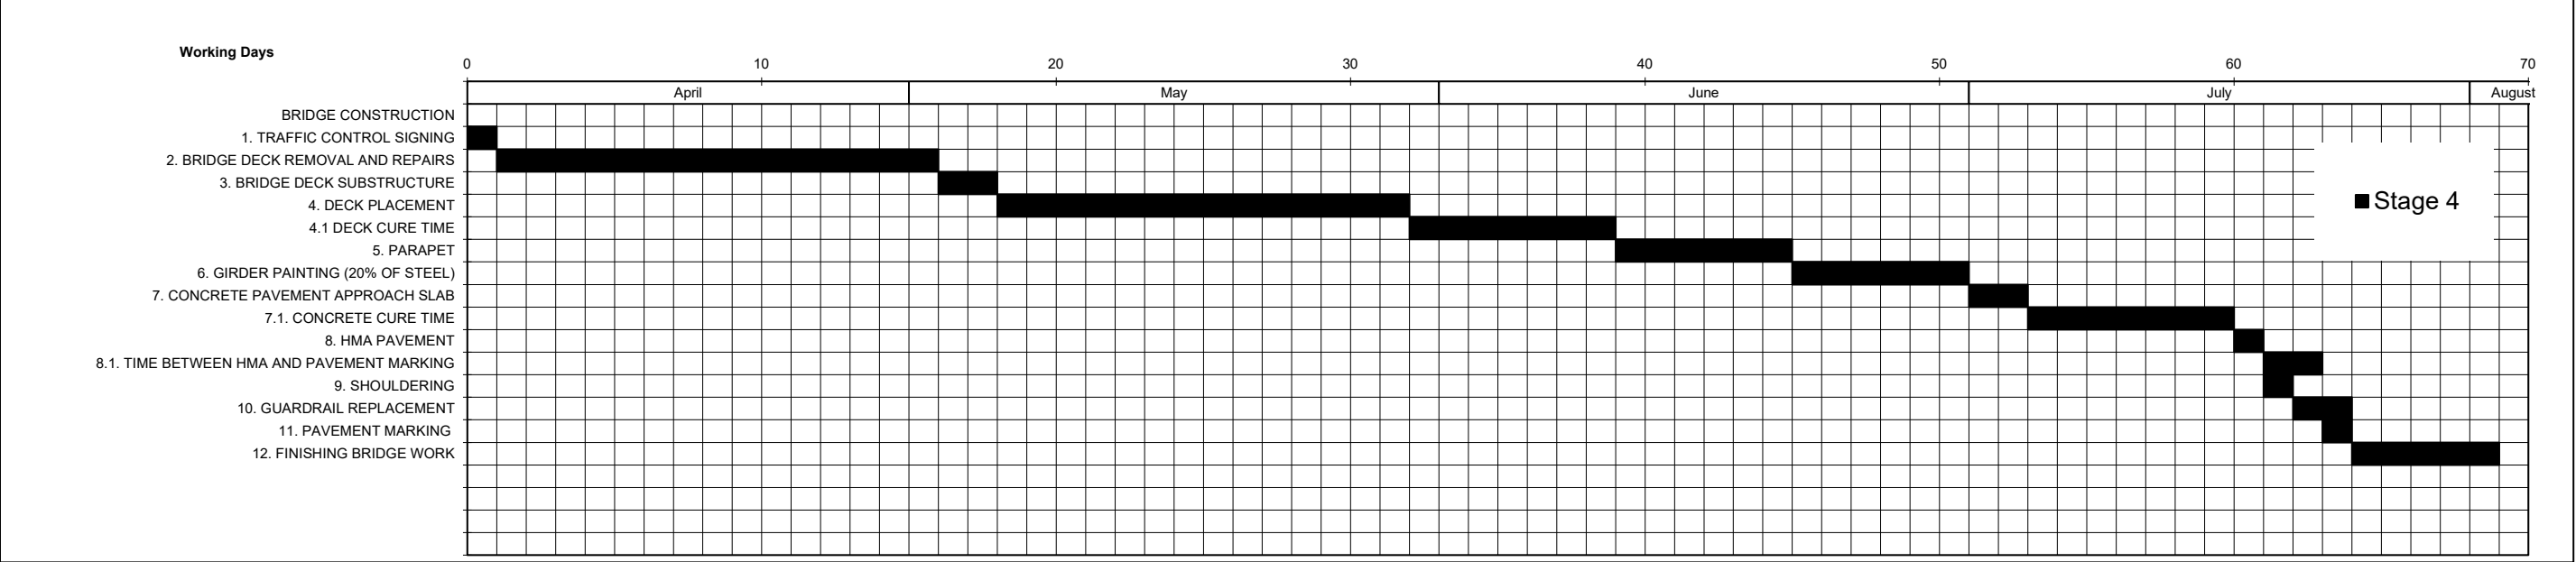

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 4		Stage 5		Stage 6		Stage 7		Stage 8	
	Stage 4	Stage 5	Stage 6	Stage 7	Stage 8					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
BRIDGE CONSTRUCTION									/ / / /										
1. TRAFFIC CONTROL SIGNING	1					1	DAYS	1	1 / / / /	0	1								
2. BRIDGE DECK REMOVAL AND REPAIRS	15					15	DAYS	1	15 / / / /	1	16								
3. BRIDGE DECK SUBSTRUCTURE	4					4	EACH	2	2 / / / /	16	18								
4. DECK PLACEMENT	6,805					6,805	SF	500	14 / / / /	18	32								
4.1 DECK CURE TIME	7					7	DAYS	1	7 / / / /	32	39								
5. PARAPET	280					280	LF	50	6 / / / /	39	45								
6. GIRDER PAINTING (20% OF STEEL)	1,200					1,200	SF	200	6 / / / /	45	51								
7. CONCRETE PAVEMENT APPROACH SLAB	173					173	SY	100	2 / / / /	51	53								
7.1. CONCRETE CURE TIME	7					7	DAYS	1	7 / / / /	53	60								
8. HMA PAVEMENT	120					120	TONS	500	1 / / / /	60	61								
8.1. TIME BETWEEN HMA AND PAVEMENT MARKING	2					2	DAYS	1	2 / / / /	61	63								
9. SHOULDERING	30					30	TONS	200	1 / / / /	61	62								
10. GUARDRAIL REPLACEMENT	290					290	LF	200	2 / / / /	62	64								
11. PAVEMENT MARKING	4,500					4,500	LF	10000	1 / / / /	63	64								
12. FINISHING BRIDGE WORK	5					5	DAYS	1	5 / / / /	64	69								
									/ / / /										
									/ / / /										
									/ / / /										
									/ / / /										

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0	0	0	0
			0	0		0	0	0	0
			0	0		0	0	0	0
April	4/3/2023	4/30/2023	28	28		20	77	15	15
May	5/1/2023	5/31/2023	31	59	1	22	80	18	33
June	6/1/2023	6/30/2023	30	89		22	80	18	51
July	7/1/2023	7/31/2023	31	120	1	20	85	17	68
August	8/1/2023	8/3/2023	3	123	0	3	85	3	71
			0	123	1	-1	80	0	71
			0	123	0	0	27	0	71
			0	123		0	0	0	71
			0	123		0	0	0	71

REMARKS

STAGE 4 IS THE BRIDGE DECK REPLACEMENT PROJECT (ID 2040-20-70); WORK INCLUDES B-40-0530 DECK REPLACEMENT; GUARDRAIL REPLACEMENT AT B-40-0530;

TRAFFIC CONTROL: EB DIRECTIONAL DETOUR

Calendar Days	123
Working Days	71
Completion Date	August 3, 2023
Prepared By	CLS

CONSTRUCTION YEAR: 2023
