

Wisconsin Department of Transportation DT1923 04/2011

Date of Letting	August 11, 2020
Probable Date of Beginning	September 14, 2020



ITEM ANALYSIS

[illegible]

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
September	9/14/2020	9/30/2020	17	17		13	70	9	9
October	10/1/2020	10/23/2020	23	40		17	70	12	21
			0	40		0	50	0	21
			0	40		0	50	0	21

REMARKS

This schedule is for the first phase of the project to construct the crossovers in the fall of 2020. The project will then be suspended over winter. The next stage will be allowed to begin 4/1/2021.


Calendar Days	40
Working Days	21
Completion Date	
Prepared By	

CONSTRUCTION YEAR: 2020

CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2011

Project ID	2240-00-77	Highway	STH 36	Project Title	Milwaukee Avenue	Date of Letting	August 11, 2020
Work Type	Resurface	County	Racine	Project Limits	STH 20 to CTH Y	Probable Date of Beginning	September 14, 2020

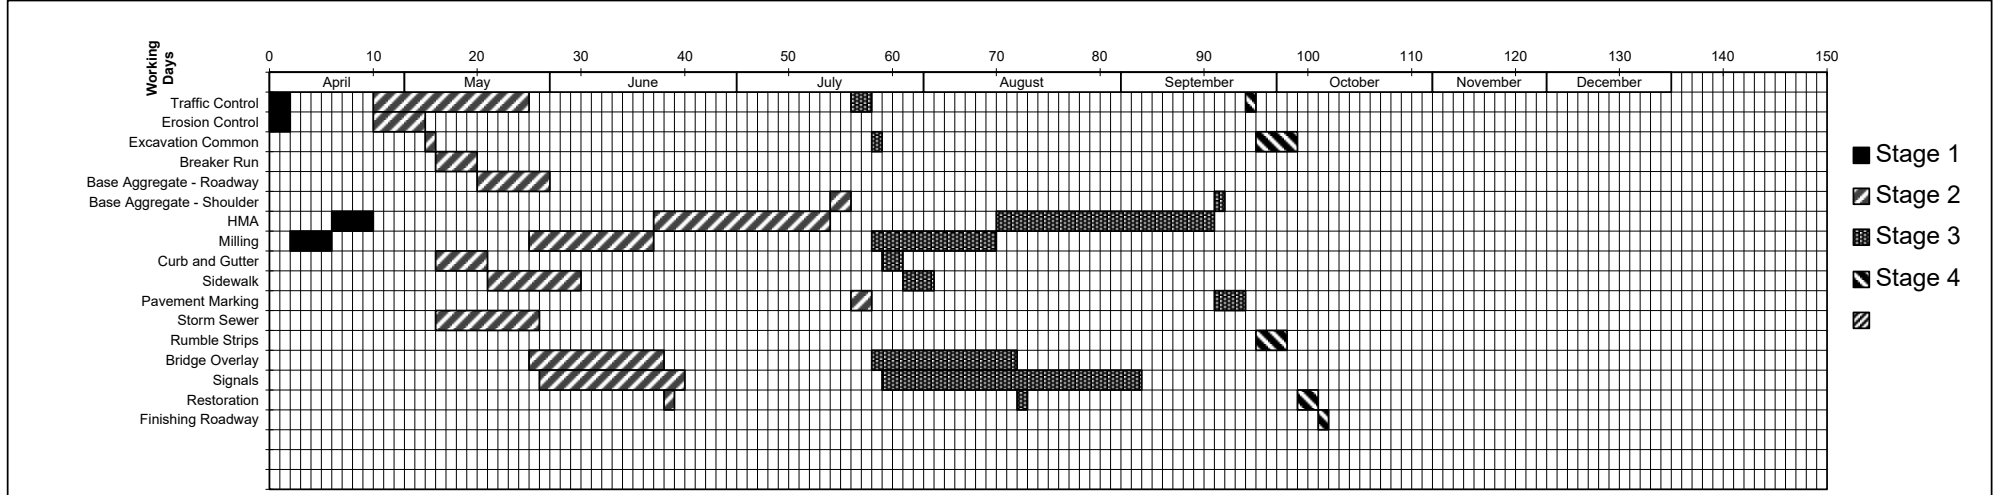

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4			
	Stage 1	Stage 2	Stage 3	Stage 4	0					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
Traffic Control	2	15	2	1		20	Days	1	2 / 15 / 2 / 1 /	0	2	10	25	56	58	94	95		
Erosion Control	2	5				7	Days	1	2 / 5 / / / /	0	2	10	15						
Excavation Common		700	74	2,795		3,569	CY	920	/ 1 / 1 / 4 /			15	16	58	59	95	99		
Breaker Run		6,295				6,295	Tons	1800	/ 4 / / / /			16	20						
Base Aggregate - Roadway		6,114				6,114	Tons	1000	/ 7 / / / /			20	27						
Base Aggregate - Shoulder		1,150	814			1,964	Tons	1000	/ 2 / 1 / / /			54	56	91	92				
HMA	4,678	22,910	28,460			56,048	Tons	1400	4 / 17 / 21 / / /	6	10	37	54	70	91				
Milling	4,678	16,232	16,232			37,142	Tons	1400	4 / 12 / 12 / / /	2	6	25	37	58	70				
Curb and Gutter		3,723	911			4,634	LF	850	/ 5 / 2 / / /			16	21	59	61				
Sidewalk		15,774	4,517			20,291	SF	1800	/ 9 / 3 / / /			21	30	61	64				
Pavement Marking		74,326	85,307			159,633	LF	40000	/ 2 / 3 / / /			56	58	91	94				
Storm Sewer		995				995	LF	100	/ 10 / / / /			16	26						
Rumble Strips				77,730		77,730	LF	35000	/ / / 3 /							95	98		
Bridge Overlay		18,540	20,320			38,860	SF	1500	/ 13 / 14 / / /			25	38	58	72				
Signals		14	25			39	Days	1	/ 14 / 25 / / /			26	40	59	84				
Restoration		1	1	2		4	Days	1	/ 1 / 1 / 2 /			38	39	72	73	99	101		
Finishing Roadway				1		1	Days	1	/ / / 1 /							101	102		
									/ / / / /										
									/ / / / /										
									/ / / / /										

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0	50	0	0
			0	0		0	50	0	0
			0	0		0	50	0	0
April	4/1/2021	4/30/2021	30	30		22	60	13	13
May	5/1/2021	5/31/2021	31	61	1	20	70	14	27
June	6/1/2021	6/30/2021	30	91		22	80	18	45
July	7/1/2021	7/31/2021	31	122	1	21	85	18	63
August	8/1/2021	8/31/2021	31	153		22	85	19	82
September	9/1/2021	9/30/2021	30	183	1	21	70	15	97
October	10/1/2021	10/31/2021	31	214		21	70	15	112
November	11/1/2021	11/30/2021	30	244		22	50	11	123
December	12/1/2021	12/31/2021	31	275		23	50	12	135

REMARKS

This schedule is for the restart of the project after the winter suspension.

Calendar Days	275
Working Days	135
Completion Date	
Prepared By	

CONSTRUCTION YEAR: 2021
