


CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2011

Project ID 1067-02-75 Highway IH 94 Project Title Lake Mills - Oconomowoc Date of Letting February 12, 2019
 Work Type Bridge Rehabilitation County Jefferson Project Limits CTH X & CTH D Bridges Probable Date of Beginning April 1, 2019

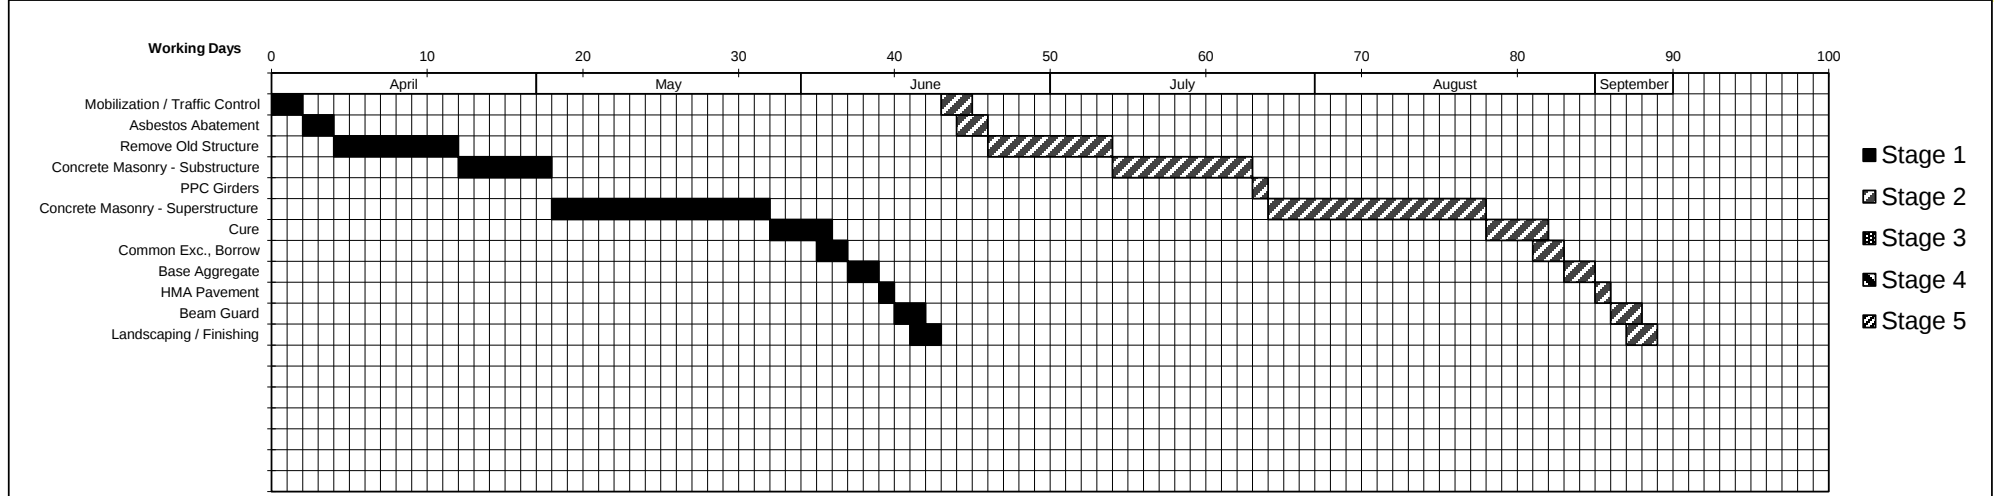

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5	
	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
Mobilization / Traffic Control	1	1				2	LS	0.5	2 / 2 / / / /	0	2	43	45						
Asbestos Abatement	1	1				2	LS	0.5	2 / 2 / / / /	2	4	44	46						
Remove Old Structure	1	1				2	LS	0.125	8 / 8 / / / /	4	12	46	54						
Concrete Masonry - Substructure	60	84				144	CY	10	6 / 9 / / / /	12	18	54	63						
PPC Girders	0	4				4	EACH	4	0 / 1 / / / /	18	18	63	64						
Concrete Masonry - Superstructure	240	240				480	CY	18	14 / 14 / / / /	18	32	64	78						
Cure	1	1				2	LS	0.25	4 / 4 / / / /	32	36	78	82						
Common Exc., Borrow	829	1,431				2,260	CY	800	2 / 2 / / / /	35	37	81	83						
Base Aggregate	850	1,120				1,970	TON	800	2 / 2 / / / /	37	39	83	85						
HMA Pavement	490	770				1,260	TON	1000	1 / 1 / / / /	39	40	85	86						
Beam Guard	970	545				1,515	LF	500	2 / 2 / / / /	40	42	86	88						
Landscaping / Finishing	1	1				2	LS	0.5	2 / 2 / / / /	41	43	87	89						
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										
									/ / / / /										

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0		0	0
			0	0		0		0	0
April	4/1/2019	4/30/2019	30	30		22	77	17	17
May	5/1/2019	5/31/2019	31	61	2	21	80	17	34
June	6/1/2019	6/30/2019	30	91		20	80	16	50
July	7/1/2019	7/31/2019	31	122	3	20	85	17	67
August	8/1/2019	8/31/2019	31	153	1	21	85	18	85
September	9/1/2019	9/10/2019	10	163	1	6	80	5	90
			0	163		0		0	90
			0	163		0		0	90
			0	163		0		0	90
			0	163		0		0	90

REMARKS

Completion date - 9/13/2019 or 90 working days??
 Stage 1 is CTH : D
 Stage 2 is CTH X

Calendar Days 163
 Working Days 90
 Completion Date
 Prepared By OMNNI Associates

CONSTRUCTION YEAR: 2019
