

CONTRACT TIME FOR COMPLETION


Wisconsin Department of Transportation DT1923 04/2011

Project ID 3670-00-73
Work Type RECONDITION

Highway STH 89
County DODGE

Project Title LAKE MILLS - COLUMBUS
Project Limits CTH T/DALMAN ROAD INTERSECTION

Date of Letting February 11, 2020
Probable Date of Beginning June 1, 2020

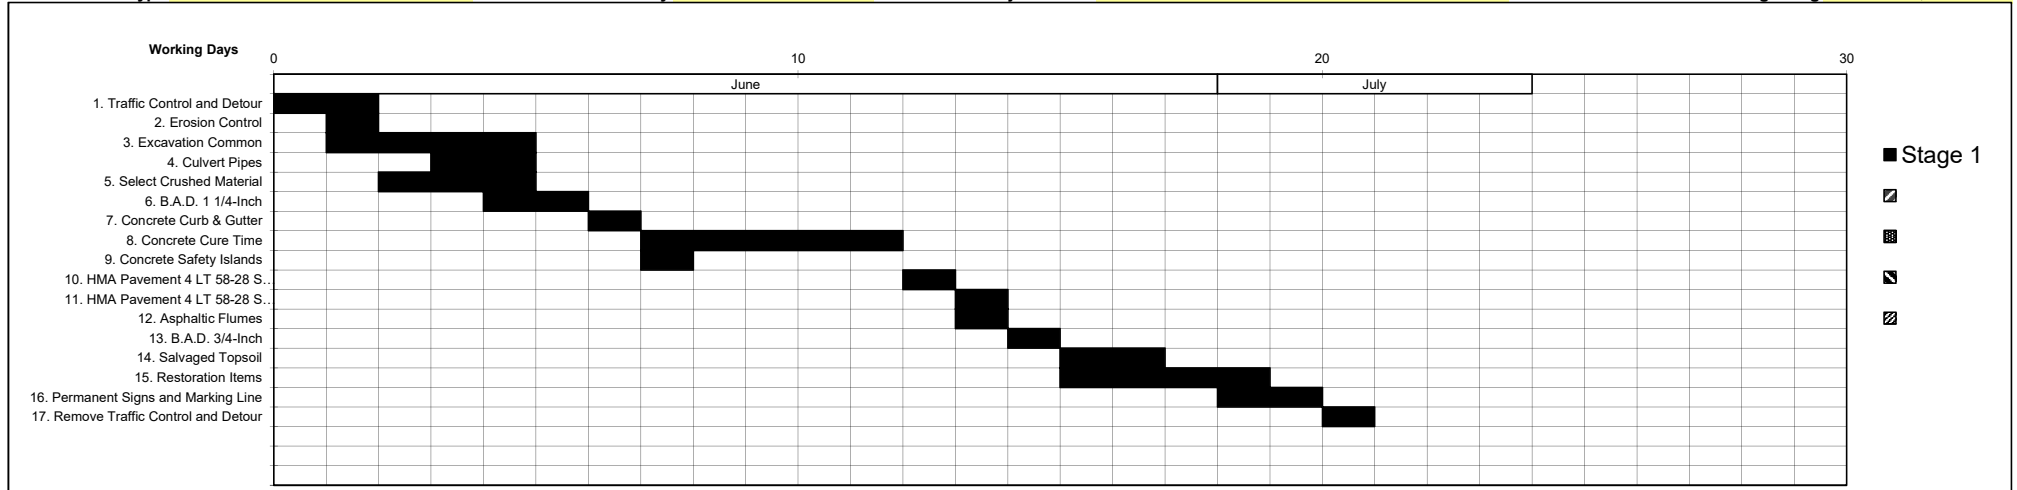

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Begin	End	Begin	End	Begin	End	Begin	End
	Stage 1	0	0	0	0					Begin	End								
1. Traffic Control and Detour	2					2	DAY	1	2 / / / / /	0	2								
2. Erosion Control	1					1	DAY	1	1 / / / / /	1	2								
3. Excavation Common	3,789					3,789	CY	1000	4 / / / / /	1	5								
4. Culvert Pipes	104					104	LF	52	2 / / / / /	3	5								
5. Select Crushed Material	2,425					2,425	TON	1000	3 / / / / /	2	5								
6. B.A.D. 1 1/4-Inch	1,543					1,543	TON	860	2 / / / / /	4	6								
7. Concrete Curb & Gutter	329					329	LF	350	1 / / / / /	6	7								
8. Concrete Cure Time	5					5	DAY	1	5 / / / / /	7	12								
9. Concrete Safety Islands	572					572	SF	5850	1 / / / / /	7	8								
10. HMA Pavement 4 LT 58-28 S (Lower Layer)	387					387	TON	720	1 / / / / /	12	13								
11. HMA Pavement 4 LT 58-28 S (Upper Layer)	387					387	TON	720	1 / / / / /	13	14								
12. Asphaltic Flumes	22					22	SY	60	1 / / / / /	13	14								
13. B.A.D. 3/4-Inch	137					137	TON	470	1 / / / / /	14	15								
14. Salvaged Topsoil	3,716					3,716	SY	3240	2 / / / / /	15	17								
15. Restoration Items	4					4	DAY	1	4 / / / / /	15	19								
16. Permanent Signs and Marking Line	2					2	DAY	1	2 / / / / /	18	20								
17. Remove Traffic Control and Detour	1					1	DAY	1	1 / / / / /	20	21								
									/ / / / /										
									/ / / / /										
									/ / / / /										

Month	Date		Days			Possible Work Days	Probable Working Days		
	Begin	End	Month	Total	Holiday		%	Month	Total
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
			0	0		0		0	0
June	6/1/2020	6/30/2020	30	30	0	22	81	18	18
July	7/1/2020	7/10/2020	10	40	1	7	85	6	24
			0	40		0		0	24
			0	40		0		0	24
			0	40		0		0	24
			0	40		0		0	24
			0	40		0		0	24

REMARKS

The contract will be a Calendar Day contract of 40 Calendar Days. A completion date of October 1, 2020 was added to avoid impacts with the fall harvest season.

Calendar Days
Working Days
Completion Date
Prepared By

40

TJD & MRL & JMH

CONSTRUCTION YEAR: 2020
