CONTRACT TIME FOR COMPLETION

Wisconsin Department of Transportation DT1923 04/2022

Project ID	1060-53-70	**Highway**	Various Highways	**Project Title**	Various Noise Wall Locations
Work Type	Preservation	**County**	Southeast Regionwide	**Project Limits**	Locations on STN Per Annual Plan

Date of Letting November 8, 2022
Probable Date of Beginning June 5, 2023

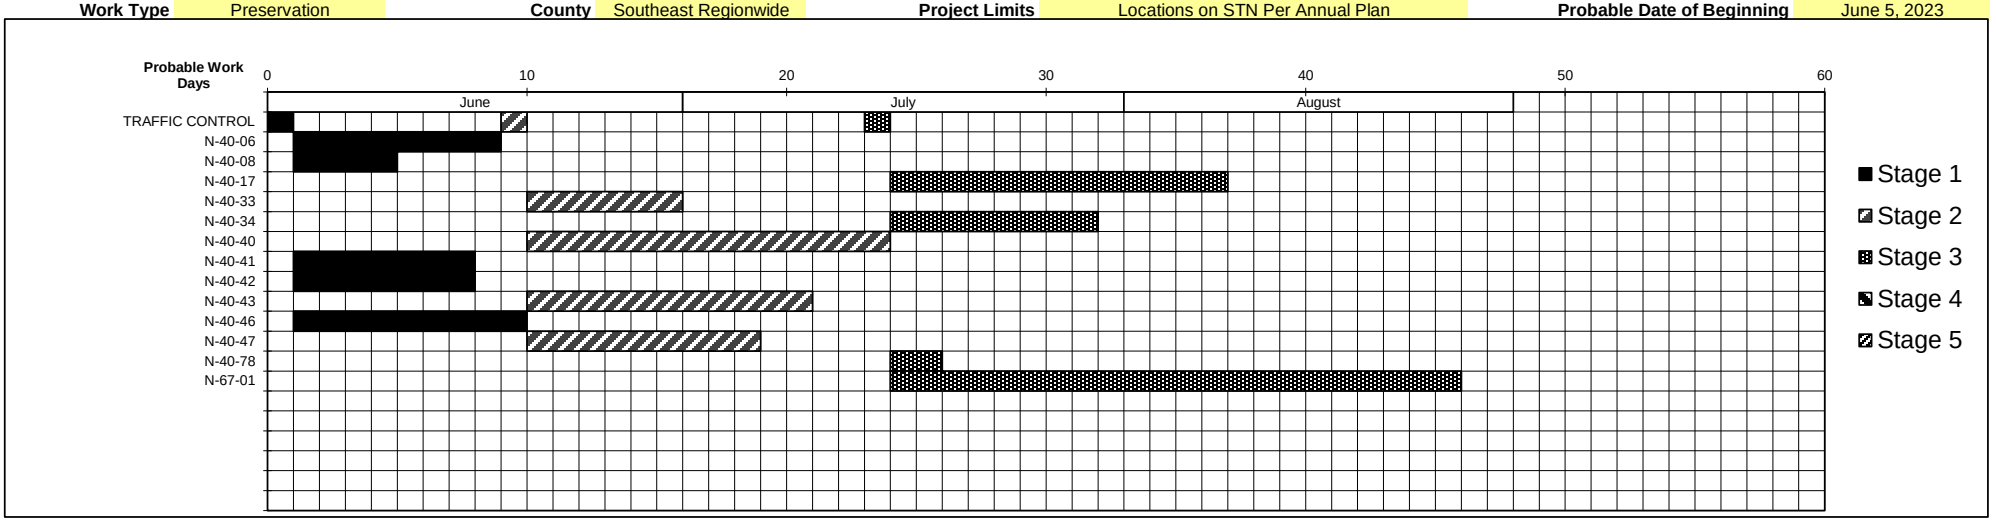

ITEM ANALYSIS

Item	Contract Quantity per Stage					Total Quantity	Unit	Production Rate	Working Days (per Stage)	Stage 1		Stage 2		Stage 3		Stage 4		Stage 5	
	Stage 1	Stage 2	Stage 3	Stage 4	Stage 5					Begin	End	Begin	End	Begin	End	Begin	End	Begin	End
TRAFFIC CONTROL	1	1	1			3	DAY	1	1 / 1 / 1 / /	0	1	9	10	23	24				
N-40-06	8					8	DAY	1	8 / / / /	1	9								
N-40-08	4					4	DAY	1	4 / / / /	1	5								
N-40-17			13			13	DAY	1	/ / 13 / /					24	37				
N-40-33		6				6	DAY	1	/ 6 / / /			10	16						
N-40-34			8			8	DAY	1	/ / 8 / /					24	32				
N-40-40		14				14	DAY	1	/ 14 / / /			10	24						
N-40-41	7					7	DAY	1	7 / / / /	1	8								
N-40-42	7					7	DAY	1	7 / / / /	1	8								
N-40-43		11				11	DAY	1	/ 11 / / /			10	21						
N-40-46	9					9	DAY	1	9 / / / /	1	10								
N-40-47		9				9	DAY	1	/ 9 / / /			10	19						
N-40-78			2			2	DAY	1	/ / 2 / /					24	26				
N-67-01			22			22	DAY	1	/ / 22 / /					24	46				
									/ / / /										
									/ / / /										
									/ / / /										
									/ / / /										
									/ / / /										
									/ / / /										

Month	Date		Days			Possible Work Days	Additional Work Days Modifier	Adjusted Possible Work Days	Probable Work Days		
	Begin	End	Month	Total	Holiday				%	Month	Total
			0	0		0		0		0	0
			0	0		0		0		0	0
			0	0		0		0		0	0
			0	0		0		0		0	0
			0	0		0		0		0	0
June	6/5/2023	6/30/2023	26	26		20		20	80	16	16
July	7/1/2023	7/31/2023	31	57	1	20		20	85	17	33
August	8/1/2023	8/25/2023	25	82		19		19	80	15	48
			0	82		0		0		0	48
			0	82		0		0		0	48
			0	82		0		0		0	48
			0	82		0		0		0	48

Note: Chart is based on the assumption of work not occuring on weekends or holidays. If work is expected to occur on these days, adjust Possible Work Days by adding days to the Additional Work Days Modifier column. See FDM 19-10-30.

REMARKS

Stage 1 - N-40-06, 08, 41, 42 & 46
Stage 2 - N-40-33, 40, 43 & 47
Stage 3 - N-40-17,34, 78 & N-67-01

Contract Work Type

☐ Calendar Day	82
☐ Working Day	48
☐ Completion Date	

Prepared By
Andy Smieja

CONSTRUCTION YEAR: 2023
