

**From:** Bielefeldt, Heath - DOT  
**Sent:** Thursday, November 1, 2018 7:15 AM  
**To:** Koepp, David - DOT  
**Subject:** FW: 7110-05-02,72 STH 37, IH 94-USH 12 - Conflict  
**Attachments:** Scanned from a Xerox Multifunction Printer.pdf

ATT and Charter were asking for when the path would be staked to confirm their relocations were adequate. I do not recall them asking for the path to be staked prior to their relocation. -Heath

---

**From:** Bielefeldt, Heath - DOT  
**Sent:** Friday, June 1, 2018 6:26 AM  
**To:** Mounir, Mohamed - DOT <[Mohamed.Mounir@dot.wi.gov](mailto:Mohamed.Mounir@dot.wi.gov)>  
**Cc:** Koepp, David - DOT <[David.Koepp@dot.wi.gov](mailto:David.Koepp@dot.wi.gov)>; Yoder, Shane J <[Shane.Yoder@charter.com](mailto:Shane.Yoder@charter.com)>  
**Subject:** FW: 7110-05-02,72 STH 37, IH 94-USH 12 - Conflict

Mohamed, can you please look into when the path will be staked and see if that can be moved up to be sure that Charter and AT&T WI are no longer in conflict with it? Thank you. -Heath

---

**From:** Bielefeldt, Heath - DOT  
**Sent:** Thursday, May 24, 2018 3:20 PM  
**To:** Koepp, David - DOT <[David.Koepp@dot.wi.gov](mailto:David.Koepp@dot.wi.gov)>  
**Subject:** FW: 7110-05-02,72 STH 37, IH 94-USH 12 - Conflict

I spoke to Rick with AT&T WI and now Shane from Charter below and with their relocates they believe that are no longer in conflict with the path; however, do to some of the redesign, and perhaps issues with the survey marker etc, they want to be sure that there will be no issues with the path. I'm guessing they still have access to some crews to do additional work right now.

At any rate, can you please ask if they path will be staked anytime soon?

Thanks.  
-Heath

---

**From:** Yoder, Shane J [<mailto:Shane.Yoder@charter.com>]  
**Sent:** Thursday, May 24, 2018 3:17 PM  
**To:** Bielefeldt, Heath - DOT <[Heath.Bielefeldt@dot.wi.gov](mailto:Heath.Bielefeldt@dot.wi.gov)>  
**Subject:** 7110-05-02,72 STH 37, IH 94-USH 12 - Conflict

Would it be possible to have our (AT&T/Spectrum) pedestals verified if they are now out of conflict with the bike path?



Shane Yoder | Construction Coordinator  
1201 McCann Dr. Altoona, WI 54720  
715.831. 8940 X51113

The contents of this e-mail message and any attachments are intended solely for the addressee(s) and may contain confidential and/or legally privileged information. If you are not the intended recipient of this message or if this message has been addressed to you in error, please immediately alert the sender by reply e-mail and then delete this message and any attachments. If you are not the intended recipient, you are notified that any use, dissemination, distribution, copying, or storage of this message or any attachment is strictly prohibited.

**From:** Bielefeldt, Heath - DOT  
**Sent:** Monday, October 29, 2018 11:06 AM  
**To:** Koepp, David - DOT  
**Subject:** FW: CONCERN - EAU CLAIRE -WisDOT ID 7110-05-72 -STH 37 from US12 toi94. Front of RCU & Red Lobster  
**Attachments:** message.wav

---

**From:** PODOLAK, RICK T [mailto:rp4514@att.com]  
**Sent:** Monday, October 29, 2018 10:18 AM  
**To:** Bielefeldt, Heath - DOT <Heath.Bielefeldt@dot.wi.gov>  
**Subject:** RE: CONCERN - EAU CLAIRE -WisDOT ID 7110-05-72 -STH 37 from US12 toi94. Front of RCU & Red Lobster

According to the VM Craig Haas sent me, he spoke with USIC Craig and USIC Craig was to relay to both Shane and I that we needed to adjust the peds. Craig said Jim with KL Eng was standing right there when he had the conversation. I attached the VM for your listening pleasure.

**Rick Podolak**  
Manager, OSP Planning & Engineering Design  
AT&T Technology Operations, Midwest C&E -Legal Mandate

**AT&T Wisconsin**  
304 S Dewey St, Eau Claire, WI 54701  
o 715.839.5565 | m 715.410.0656 | [rp4514@att.com](mailto:rp4514@att.com)

MOBILIZING **YOUR** WORLD

---

**From:** Bielefeldt, Heath - DOT [<mailto:Heath.Bielefeldt@dot.wi.gov>]  
**Sent:** Monday, October 29, 2018 9:59 AM  
**To:** PODOLAK, RICK T <[rp4514@att.com](mailto:rp4514@att.com)>  
**Subject:** Re: CONCERN - EAU CLAIRE -WisDOT ID 7110-05-72 -STH 37 from US12 toi94. Front of RCU & Red Lobster

Yeah, I emailed the PM again this morning and he called the construction project leader again and was told that Haas had discussed this location with ATT during construction. Will probably need to dig into field notes to see if anything was documented. -Heath

---

**From:** PODOLAK, RICK T <[rp4514@att.com](mailto:rp4514@att.com)>

**Sent:** Monday, October 29, 2018 9:28 AM

**To:** Bielefeldt, Heath - DOT

**Subject:** RE: CONCERN - EAU CLAIRE -WisDOT ID 7110-05-72 -STH 37 from US12 toi94. Front of RCU & Red Lobster

Appreciate that. The Prime-Craig Hass called me shortly after I sent you the email and his response was somewhat interesting.

Rick

---

**From:** Bielefeldt, Heath - DOT [<mailto:Heath.Bielefeldt@dot.wi.gov>]

**Sent:** Monday, October 29, 2018 7:59 AM

**To:** PODOLAK, RICK T <[rp4514@att.com](mailto:rp4514@att.com)>

**Subject:** Re: CONCERN - EAU CLAIRE -WisDOT ID 7110-05-72 -STH 37 from US12 toi94. Front of RCU & Red Lobster

Hi Rick. I am on vacation, from this past Thursday until tomorrow. I forwarded the issue to the PM, who should be gathering some information from the contractor and field staff. I hope to have a response tomorrow. Thanks. -Heath

---

**From:** PODOLAK, RICK T <[rp4514@att.com](mailto:rp4514@att.com)>

**Sent:** Friday, October 26, 2018 2:56 PM

**To:** Bielefeldt, Heath - DOT

**Cc:** Yoder, Shane J

**Subject:** RE: CONCERN - EAU CLAIRE -WisDOT ID 7110-05-72 -STH 37 from US12 toi94. Front of RCU & Red Lobster

Heath,

Here is what we found today when we exposed our ped/splice in order to help determine the limits of our solution. At this point, I'm waiting to hear from my splicers on Monday about their take on a possible solution.

Rick Podolak  
Manager, OSP Planning & Engineering Design  
AT&T Technology Operations, Midwest C&E -Legal Mandate

AT&T Wisconsin  
304 S Dewey St, Eau Claire, WI 54701  
o 715.839.5565 | m 715.410.0656 | [rp4514@att.com](mailto:rp4514@att.com)

MOBILIZING YOUR WORLD

-----Original Message-----

From: PODOLAK, RICK T

Sent: Thursday, October 25, 2018 12:40 PM

To: Bielefeldt, Heath - DOT ([Heath.Bielefeldt@dot.wi.gov](mailto:Heath.Bielefeldt@dot.wi.gov)) <[Heath.Bielefeldt@dot.wi.gov](mailto:Heath.Bielefeldt@dot.wi.gov)>

Cc: 'Yoder, Shane J' <[Shane.Yoder@charter.com](mailto:Shane.Yoder@charter.com)>

Subject: CONCERN - EAU CLAIRE -WisDOT ID 7110-05-72 -STH 37 from US12 to I94. Front of RCU & Red Lobster

Heath,

I performed a drive-by on the above titled project and I noticed a very LARGE concern with both Charter's and AT&T's half buried pedestal now sitting within 3ft of the newly paved path. Please see the attached photos.

A couple quick questions surrounding this observation:

1. Why was no contact made to Shane or myself that these peds needed to be adjusted prior to the final grade work?
2. Who should we coordinate with in order to help us get our peds set to new grade?

Note that due to the proximity of ped and new pavement, it looks like we may have to disturb the newly paved path.

Looking forward to hearing more on this situation.

Sincerely,

Rick Podolak

Manager, OSP Planning & Engineering Design

AT&T Technology Operations, Midwest C&E -Legal Mandate

AT&T Wisconsin

304 S Dewey St, Eau Claire, WI 54701

o 715.839.5565 | m 715.410.0656 | [rp4514@att.com](mailto:rp4514@att.com)

MOBILIZING YOUR WORLD

**From:** Bielefeldt, Heath - DOT  
**Sent:** Monday, October 29, 2018 8:01 AM  
**To:** Koepp, David - DOT  
**Subject:** Re: CONCERN - EAU CLAIRE -WisDOT ID 7110-05-72 -STH 37 from US12 toi94. Front of RCU & Red Lobster

ATT thinks they may need to dig up the path to resolve the issue on their end. Did anyone notice these getting buried during construction? -Heath

---

**From:** Bielefeldt, Heath - DOT  
**Sent:** Thursday, October 25, 2018 1:18 PM  
**To:** Koepp, David - DOT  
**Subject:** Fw: CONCERN - EAU CLAIRE -WisDOT ID 7110-05-72 -STH 37 from US12 toi94. Front of RCU & Red Lobster

Dave, I am out until Tuesday. Has this previously been discussed?

-Heath

Heath Bielefeldt | Utility Coordinator  
Northwest Region, Eau Claire Office | Wisconsin Dept. of Transportation  
718 W. Clairemont Avenue, Suite 200 | Eau Claire, WI 54701-5108  
715-836-2729 (Office) | heath.bielefeldt@dot.wi.gov

---

**From:** PODOLAK, RICK T <rp4514@att.com>  
**Sent:** Thursday, October 25, 2018 12:40:27 PM  
**To:** Bielefeldt, Heath - DOT  
**Cc:** Yoder, Shane J  
**Subject:** CONCERN - EAU CLAIRE -WisDOT ID 7110-05-72 -STH 37 from US12 toi94. Front of RCU & Red Lobster

Heath,

I performed a drive-by on the above titled project and I noticed a very LARGE concern with both Charter's and AT&T's half buried pedestal now sitting within 3ft of the newly paved path Please see the attached photos.

A couple quick questions surrounding this observation:

1. Why was no contact made to Shane or myself that these peds needed to be adjusted prior to the final grade work?
2. Who should we coordinate with in order to help us get our peds set to new grade?

Note that due to the proximity of ped and new pavement, it looks like we may have to disturb the newly paved path.

Looking forward to hearing more on this situation.

Sincerely,

Rick Podolak  
Manager, OSP Planning & Engineering Design  
AT&T Technology Operations, Midwest C&E -Legal Mandate

AT&T Wisconsin  
304 S Dewey St, Eau Claire, WI 54701  
o 715.839.5565 | m 715.410.0656 | rp4514@att.com

MOBILIZING YOUR WORLD

**From:** Bielefeldt, Heath - DOT  
**Sent:** Thursday, October 25, 2018 1:19 PM  
**To:** Koepp, David - DOT  
**Subject:** Fw: CONCERN - EAU CLAIRE -WisDOT ID 7110-05-72 -STH 37 from US12 toi94. Front of RCU & Red Lobster  
**Attachments:** IMG\_2474.jpg; IMG\_2473.jpg; IMG\_2472.jpg; IMG\_2471.jpg

Dave, I am out until Tuesday. Has this previously been discussed?

-Heath

Heath Bielefeldt | Utility Coordinator  
Northwest Region, Eau Claire Office | Wisconsin Dept. of Transportation  
718 W. Clairemont Avenue, Suite 200 | Eau Claire, WI 54701-5108  
715-836-2729 (Office) | heath.bielefeldt@dot.wi.gov

---

**From:** PODOLAK, RICK T <rp4514@att.com>  
**Sent:** Thursday, October 25, 2018 12:40:27 PM  
**To:** Bielefeldt, Heath - DOT  
**Cc:** Yoder, Shane J  
**Subject:** CONCERN - EAU CLAIRE -WisDOT ID 7110-05-72 -STH 37 from US12 toi94. Front of RCU & Red Lobster

Heath,

I performed a drive-by on the above titled project and I noticed a very LARGE concern with both Charter's and AT&T's half buried pedestal now sitting within 3ft of the newly paved path Please see the attached photos.

A couple quick questions surrounding this observation:

1. Why was no contact made to Shane or myself that these peds needed to be adjusted prior to the final grade work?
2. Who should we coordinate with in order to help us get our peds set to new grade?

Note that due to the proximity of ped and new pavement, it looks like we may have to disturb the newly paved path.

Looking forward to hearing more on this situation.

Sincerely,

Rick Podolak  
Manager, OSP Planning & Engineering Design  
AT&T Technology Operations, Midwest C&E -Legal Mandate

AT&T Wisconsin  
304 S Dewey St, Eau Claire, WI 54701  
o 715.839.5565 | m 715.410.0656 | rp4514@att.com

MOBILIZING YOUR WORLD

**From:** Bielefeldt, Heath - DOT  
**Sent:** Friday, May 4, 2018 8:13 AM  
**To:** DOT DTSD NW EC PERMIT COORDINATION  
**Subject:** RE: AT&T WI Permit dt1553i for Eau Claire County -STH 37 - 7110-05-72

This is ok from a project utility coordination perspective. -Heath

---

**From:** PODOLAK, RICK T [mailto:rp4514@att.com]  
**Sent:** Friday, May 4, 2018 7:56 AM  
**To:** DOT DTSD NW EC PERMIT COORDINATION <DOTDTSDNWECPERMITCOORDINATION@dot.wi.gov>  
**Cc:** Bielefeldt, Heath - DOT <Heath.Bielefeldt@dot.wi.gov>  
**Subject:** AT&T WI Permit dt1553i for Eau Claire County -STH 37 - 7110-05-72

Attached is our permit req. in order to make ready for the STH 37 road project #7110-05-72. With precon scheduled for May 11<sup>th</sup>, our expected start date is week of May 21<sup>st</sup>.

Thanks,

**Rick Podolak**

Manager, OSP Planning & Engineering Design  
AT&T Technology Operations, Midwest C&E -Legal Mandate

**AT&T Wisconsin**

304 S Dewey St, Eau Claire, WI 54701

o 715.839.5565 | m 715.410.0656 | [rp4514@att.com](mailto:rp4514@att.com)

MOBILIZING YOUR WORLD

**From:** PODOLAK, RICK T <rp4514@att.com>  
**Sent:** Friday, May 4, 2018 7:56 AM  
**To:** DOT DTSD NW EC PERMIT COORDINATION  
**Cc:** Bielefeldt, Heath - DOT  
**Subject:** AT&T WI Permit dt1553i for Eau Claire County -STH 37 - 7110-05-72  
**Attachments:** AT&T WI Permit dt1553i for Eau Claire County -STH 37 - 7110-05-72.docx;  
AT&T WI Work Sketch - Eau Claire County STH 37 id7110-05-72.pdf

Attached is our permit req. in order to make ready for the STH 37 road project #7110-05-72. With precon scheduled for May 11<sup>th</sup>, our expected start date is week of May 21<sup>st</sup>.

Thanks,

**Rick Podolak**  
Manager, OSP Planning & Engineering Design

AT&T Technology Operations, Midwest C&E -Legal Mandate

**AT&T Wisconsin**

304 S Dewey St, Eau Claire, WI 54701  
o 715.839.5565 | m 715.410.0656 | [rp4514@att.com](mailto:rp4514@att.com)

MOBILIZING **YOUR** WORLD

**From:** DOT DTSD CO Utility Coordination  
**Sent:** Monday, February 12, 2018 11:56 AM  
**To:** Bielefeldt, Heath - DOT  
**Cc:** DOT DTSD CO Utility Coordination  
**Subject:** RE: DocuSign: CMA AT&T WI (COMLN),7110-05-22\_30.pdf; STH 37, IH 94 to USH 12, Eau Claire Co

Heath – Parcel 1 on TPP 4.01 is owned by the City of Eau Claire. Since AT&T does not have a recorded easement, they are not eligible for Prescriptive Rights. §893.28 and 29 copied for reference (refer to teal highlighted section).

Please update the legal description for the COR (removing or striking out parcel 1). AT&T will need to concur with the change; resubmit their concurrence with the new or updated waiver packet via DocuSign.

Let me know if you have any questions,  
Connie

#### **893.28 Prescriptive rights by adverse user.**

[893.28\(1\)](#) **(1)** Continuous adverse use of rights in real estate of another for at least 20 years, **except as provided in s. [893.29](#) establishes the prescriptive right to continue the use.** Any person who in connection with his or her predecessor in interest has made continuous adverse use of rights in the land of another for 20 years, except as provided by s. [893.29](#), may commence an action to establish prescriptive rights under ch. [843](#).

[893.28\(2\)](#) **(2)** Continuous use of rights in real estate of another for at least 10 years by a domestic corporation organized to furnish telegraph or telecommunications service or transmit heat, power or electric current to the public or for public purposes, by a cooperative association organized under ch. [185](#) or [193](#) to furnish telegraph or telecommunications service, or by a cooperative organized under ch. [185](#) to transmit heat, power or electric current to its members, establishes the prescriptive right to continue the use, except as provided by s. [893.29](#). A person who has established a prescriptive right under this subsection may commence an action to establish prescriptive rights under ch. [843](#).

[893.28\(3\)](#) **(3)** The mere use of a way over unenclosed land is presumed to be permissive and not adverse.

**893.28 History** **History:** [1979 c. 323](#); [1985 a. 297](#) s. [76](#); [2005 a. 441](#).

**893.28 Annotation** Once the right to a prescriptive easement has accrued by virtue of compliance with sub. (1) for the requisite 20-year period, the holder of the prescriptive easement must comply with the recording requirements within 30 years under s. [893.33](#) (2) or lose the right to continued use. *Schauer v. Baker*, [2004 WI App 41](#), [270 Wis. 2d 714](#), [678 N.W.2d 258](#), [02-1674](#).

**893.28 Annotation** As sub. (1) is written, it is more natural to read “of another” to modify “real estate,” rather than “rights.” That is, by continuous use, one may gain a prescriptive right in another’s real estate. The real estate in which a right is gained must belong to another person. A setback restriction in an owner’s deed was not a “right in real estate” belonging to “another” that the owner could use adversely by continually violating the setback. *Hall v. Liebovich Living Trust*, [2007 WI App 112](#), [300 Wis. 2d 725](#), [731 N.W.2d 649](#), [06-0040](#).

**893.28 Annotation** Sub. (2) applies to permissive uses. An agreement that permitted an electric utility to construct and maintain electrical poles and transmission lines on a landowner’s property that was revocable upon 30 days’ written notice gave the utility “rights in real estate of another” under sub. (2). Use of the property for more than 10 years by the utility established the

prescriptive right to continue the use. Williams v. American Transmission Company, LLC, [2007 WI App 246](#), [306 Wis. 2d 181](#), [742 N.W.2d 882](#), 07-0052.

**[893.29](#) 893.29 No adverse possession by or against the state or political subdivisions.**

[893.29\(1\)](#) (1) Except as provided in sub. [\(2\)\(b\)](#), no title to or interest in real property belonging to the state or a city, village, town, county, school district, sewerage commission, sewerage district or any other unit of government within this state may be obtained by adverse possession under s. [893.25](#), [893.26](#), or [893.27](#) or by continuous adverse use under s. [893.28](#).

[893.29\(1m\)](#) (1m) Except as provided in sub. [\(2\)\(d\)](#), no city, village, town, county, school district, sewerage commission, sewerage district, or any other unit of government within this state may obtain title to private property, as defined in s. [943.13 \(1e\)\(e\)](#), by adverse possession under s. [893.25](#), [893.26](#), or [893.27](#).

[893.29\(2\)](#) (2)

[893.29\(2\)\(a\)](#) (a) Subsection [\(1\)](#) applies to a claim of title to or interest in real property based on adverse possession or continuous adverse use that began on or after March 3, 1996.

[893.29\(2\)\(b\)](#) (b) Subsection [\(1\)](#) does not affect title to or interest in real property obtained on or before March 3, 2016, by adverse possession under s. [893.25](#), [893.26](#), or [893.27](#) or by continuous adverse use under s. [893.28](#).

[893.29\(2\)\(c\)](#) (c)

[893.29\(2\)\(c\)1.](#) 1. Subsection [\(1m\)](#) applies to a claim of title to real property based on adverse possession under s. [893.25](#) that began after March 3, 1996.

[893.29\(2\)\(c\)2.](#) 2. Subsection [\(1m\)](#) applies to a claim of title to real property based on adverse possession under s. [893.26](#) that began after March 3, 2006.

[893.29\(2\)\(c\)3.](#) 3. Subsection [\(1m\)](#) applies to a claim of title to real property based on adverse possession under s. [893.27](#) that began after March 3, 2009.

[893.29\(2\)\(d\)](#) (d) Subsection [\(1m\)](#) does not affect title to real property obtained on or before March 3, 2016, by adverse possession under s. [893.25](#), [893.26](#), or [893.27](#).

**893.29 History** **History:** [1979 c. 323](#); [1983 a. 178](#); [1983 a. 189](#) s. [329 \(16\)](#); [1997 a. 108](#); [2015 a. 219](#).

**893.29 Annotation** This section does not apply to a railroad. A railroad right-of-way is subject to adverse possession, the same as other lands. *Maiers v. Wang*, [192 Wis. 2d 115](#), [531 N.W.2d 54](#) (1995).

**893.29 Annotation** In the absence of an express provision to the contrary, one who adversely possesses under an earlier version of the adverse possession statute may continue possession under the terms of that statute even after its repeal and re-creation.

*Department of Natural Resources v. Building and All Related or Attached Structures*, [2011 WI App 119](#), [336 Wis. 2d 642](#), [803 N.W.2d 86](#), 10-2076.

---

**From:** DocuSign System [mailto:dse\_na2@docusign.net]

**Sent:** Friday, February 09, 2018 9:50 AM

**To:** DOT DTSD CO Utility Coordination <DOTDTSDCOUtilityCoordination@dot.wi.gov>

**Subject:** DocuSign: CMA AT&T WI (COMLN),7110-05-22\_30.pdf; STH 37, IH 94 to USH 12, Eau Claire Co





Heath Bielefeldt sent you a document to review and sign.

**REVIEW DOCUMENTS**



**Heath Bielefeldt**

[heath.bielefeldt@dot.wi.gov](mailto:heath.bielefeldt@dot.wi.gov)

Statewide Utility Projects Coordinator,

Please DocuSign CMA AT&T WI (COMLN), 7110-05-22\_30.pdf, SNR 7110-05-22\_30 ATT WI (COMLN), 7110-05-72.pdf, COR 7110-05-22\_30 ATT WI (COMLN), 7110-05-72.pdf, TCE 7110-05-22\_30 ATT WI (COMLN), 7110-05-72.pdf, Work Plan AT&T WI (COMLN), 7110-05-72.pdf, Plat 7110-05-22\_30 AT&T WI (COMLN).pdf, Plan 7110-05-72 (excerpt).pdf

Thank You, Heath Bielefeldt

**Do Not Share This Email**

This email contains a secure link to DocuSign. Please do not share this email, link, or access code with others.

**Alternate Signing Method**

Visit DocuSign.com, click 'Access Documents', and enter the security code:  
613574504A9B4741A50286C576847E932

**About DocuSign**

Sign documents electronically in just minutes. It's safe, secure, and legally binding. Whether you're

in an office, at home, on-the-go -- or even across the globe -- DocuSign provides a professional trusted solution for Digital Transaction Management™.

**Questions about the Document?**

If you need to modify the document or have questions about the details in the document, please reach out to the sender by emailing them directly.

If you are having trouble signing the document, please visit the [Help with Signing](#) page on our [Support Center](#).



[Download the DocuSign App](#)

This message was sent to you by Heath Bielefeldt who is using the DocuSign Electronic Signature Service. If you would rather not receive email from this sender you may contact the sender with your request.

**From:** Bielefeldt, Heath - DOT  
**Sent:** Monday, October 30, 2017 6:36 PM  
**To:** Krug, Gary - DOT  
**Cc:** Koepp, David - DOT  
**Subject:** 7110-05-72 USR, Utilities special, and Plan Contact revisions  
**Attachments:** 71100572\_usr.pdf; 71100572\_eau-Utilities.docx

Attached is the USR for the esubmittal. Current Utilities special provision attached. Revisions will be required when all work plans are received, anticipated in the next month.

Please revise plan contacts, either now or when PSE review comments return:

AT&T LEGACY  
BRAD KEMPH (LOCATOR)  
715-254-5238  
COPY ALL CORRESPONDENCE TO:  
BILL KOENIG (ENGINEER)  
JMC ENGINEERS & ASSOCIATES  
128 W SUNSET AVENUE  
APPLETON, WI 54911  
608-628-0575 (MOBILE)  
[wekoenig@att.net](mailto:wekoenig@att.net)

AT&T WISCONSIN  
RICK PODOLAK  
304 SOUTH DEWEY STREET, 4TH FLOOR  
EAU CLAIRE, WI 54701  
715-839-5565 (OFFICE)  
715-410-0656 (MOBILE)  
[rp4514@att.com](mailto:rp4514@att.com)

City of Eau Claire (SEWR and WATR)  
Lane Berg  
910 Forest St.  
Eau Claire, WI 54703  
715-839-1876 (Office)  
715-828-6801 (Mobile)  
[Lane.Berg@eauclairewi.gov](mailto:Lane.Berg@eauclairewi.gov)

Windstream  
Dennis Ruess  
8531 CTH FF  
Wisconsin Rapids, WI 54494  
812-456-1249 (Office)  
608-512-5587 (Mobile)  
[Dennis.Ruess@windstream.com](mailto:Dennis.Ruess@windstream.com)

Charter Communications (Spectrum)

Shane Yoder  
1201 McCann Drive  
Altoona, WI 54720  
715-831-8940 ext 51113 (Office)  
715-370-7870 (Mobile)  
[shane.yoder@charter.com](mailto:shane.yoder@charter.com)

Xcel Energy (Electric Distribution)  
Dan Klein  
PO BOX 8  
Eau Claire, WI 54702-0008  
715-737-4203 (Office)  
715 577-7729 (Mobile)  
[daniel.j.klein@xcelenergy.com](mailto:daniel.j.klein@xcelenergy.com)

Xcel Energy (Gas)  
Brady Gardow  
PO Box 8  
Eau Claire, WI 54702-0008  
715-737-1450 (Office)  
715-563-4081 (Mobile)  
[brady.p.gardow@xcelenergy.com](mailto:brady.p.gardow@xcelenergy.com)

Also, there are a couple “Excel” labels in the plan that should be changed to “Xcel”.

-Heath

**Heath Bielefeldt** | Utility Coordinator  
Northwest Region, Eau Claire Office | Wisconsin Dept. of Transportation  
718 W. Clairemont Avenue, Suite 200 | Eau Claire, WI 54701-5108  
715-836-2729 (Office) | [heath.bielefeldt@dot.wi.gov](mailto:heath.bielefeldt@dot.wi.gov)

**From:** Wahler, Scott - DOT  
**Sent:** Tuesday, August 1, 2017 9:00 AM  
**To:** Bielefeldt, Heath - DOT  
**Subject:** Re: 2236 Plans??? - RE: REVISED Project Plan; RE: 7110-05-72 WisDOT TRANS 220 - DT1078 Project Plan Submittal, STH 37, IH 94 to USH 12, Eau Claire Co, WI

Hello Heath,

He's right the cross section don't match the plan/profiles. That's because they don't follow the side road profiles. The curbs in the quadrants have their own alignments\profiles. I left a print of the alignment diagram on my desk, the cross sections match the quadrant alignments. It might have been good to have those alignments on the plan\profiles, at least for the utilities. I meant to send this last night but forgot, sorry.

Good day,  
Scott

---

**From:** Bielefeldt, Heath - DOT  
**Sent:** Monday, July 31, 2017 11:22 AM  
**To:** Wahler, Scott - DOT  
**Subject:** FW: 2236 Plans??? - RE: REVISED Project Plan; RE: 7110-05-72 WisDOT TRANS 220 - DT1078 Project Plan Submittal, STH 37, IH 94 to USH 12, Eau Claire Co, WI

---

**From:** PODOLAK, RICK T [mailto:rp4514@att.com]  
**Sent:** Monday, July 31, 2017 11:08 AM  
**To:** Bielefeldt, Heath - DOT  
**Subject:** 2236 Plans??? - RE: REVISED Project Plan; RE: 7110-05-72 WisDOT TRANS 220 - DT1078 Project Plan Submittal, STH 37, IH 94 to USH 12, Eau Claire Co, WI

Heath,

Hate to be last minute with this question, but I'm trying to put the finals on the 2236 and just noticed for the Short St and Hamilton P&P Sta vs x-sec Sta don't match. Hamilton P&P 25+00-28+00 & Short P&P 40+00 – 45+00 AND the Hamilton x-sec Sta 0+00 to 1+75 & Short 5+00 to 10+00

I was thinking No conflicts based off facility depths we found, but xsec Hamilton North Quad has my attention with proposed cuts.

**Rick Podolak**

Manager, OSP Planning & Engineering Design  
AT&T Technology Operations, Midwest C&E -Legal Mandate

**AT&T Wisconsin**

304 S Dewey St, Eau Claire, WI 54701  
o 715.839.5565 | m 715.410.0656 | [rp4514@att.com](mailto:rp4514@att.com)

**MOBILIZING YOUR WORLD**

---

**From:** Bielefeldt, Heath - DOT [mailto:[Heath.Bielefeldt@dot.wi.gov](mailto:Heath.Bielefeldt@dot.wi.gov)]  
**Sent:** Thursday, May 25, 2017 7:20 AM  
**To:** 'Yoder, Shane J' <[Shane.Yoder@charter.com](mailto:Shane.Yoder@charter.com)>; PODOLAK, RICK T <[rp4514@att.com](mailto:rp4514@att.com)>  
**Subject:** FW: REVISED Project Plan; RE: 7110-05-72 WisDOT TRANS 220 - DT1078 Project Plan Submittal, STH 37, IH 94 to USH 12, Eau Claire Co, WI

Attached. Please note the path stationing does not mirror the roadway. -Heath

---

**From:** Krug, Gary - DOT

**Sent:** Thursday, May 25, 2017 7:19 AM

**To:** Bielefeldt, Heath - DOT <[Heath.Bielefeldt@dot.wi.gov](mailto:Heath.Bielefeldt@dot.wi.gov)>

**Subject:** RE: REVISED Project Plan; RE: 7110-05-72 WisDOT TRANS 220 - DT1078 Project Plan Submittal, STH 37, IH 94 to USH 12, Eau Claire Co, WI

---

**From:** Bielefeldt, Heath - DOT

**Sent:** Thursday, May 25, 2017 6:16 AM

**To:** Krug, Gary - DOT <[Gary.Krug@dot.wi.gov](mailto:Gary.Krug@dot.wi.gov)>

**Subject:** FW: REVISED Project Plan; RE: 7110-05-72 WisDOT TRANS 220 - DT1078 Project Plan Submittal, STH 37, IH 94 to USH 12, Eau Claire Co, WI

Gary, do you have cross sections for STA 92-102 that depict the new path? Thanks. -Heath

---

**From:** Yoder, Shane J [<mailto:Shane.Yoder@charter.com>]

**Sent:** Wednesday, May 24, 2017 3:03 PM

**To:** Bielefeldt, Heath - DOT <[Heath.Bielefeldt@dot.wi.gov](mailto:Heath.Bielefeldt@dot.wi.gov)>; 'PODOLAK, RICK T' <[rp4514@att.com](mailto:rp4514@att.com)>

**Subject:** RE: REVISED Project Plan; RE: 7110-05-72 WisDOT TRANS 220 - DT1078 Project Plan Submittal, STH 37, IH 94 to USH 12, Eau Claire Co, WI

Heath

Can I get the cross cuts for the new redesign maps from STA+92 to 102

Thank you



Shane Yoder | Construction Coordinator

1201 McCann Dr. Altoona, WI 54720

715.831. 8940 X51113

**From:** Krug, Gary - DOT  
**Sent:** Thursday, May 25, 2017 7:19 AM  
**To:** Bielefeldt, Heath - DOT  
**Subject:** RE: REVISED Project Plan; RE: 7110-05-72 WisDOT TRANS 220 - DT1078 Project Plan Submittal, STH 37, IH 94 to USH 12, Eau Claire Co, WI  
**Attachments:** 050301\_pp-path (1).pdf

---

**From:** Bielefeldt, Heath - DOT  
**Sent:** Thursday, May 25, 2017 6:16 AM  
**To:** Krug, Gary - DOT  
**Subject:** FW: REVISED Project Plan; RE: 7110-05-72 WisDOT TRANS 220 - DT1078 Project Plan Submittal, STH 37, IH 94 to USH 12, Eau Claire Co, WI

Gary, do you have cross sections for STA 92-102 that depict the new path? Thanks. -Heath

---

**From:** Yoder, Shane J [<mailto:Shane.Yoder@charter.com>]  
**Sent:** Wednesday, May 24, 2017 3:03 PM  
**To:** Bielefeldt, Heath - DOT <[Heath.Bielefeldt@dot.wi.gov](mailto:Heath.Bielefeldt@dot.wi.gov)>; 'PODOLAK, RICK T' <[rp4514@att.com](mailto:rp4514@att.com)>  
**Subject:** RE: REVISED Project Plan; RE: 7110-05-72 WisDOT TRANS 220 - DT1078 Project Plan Submittal, STH 37, IH 94 to USH 12, Eau Claire Co, WI

Heath

Can I get the cross cuts for the new redesign maps from STA+92 to 102

Thank you



Shane Yoder | Construction Coordinator  
1201 McCann Dr. Altoona, WI 54720  
715.831. 8940 X51113

**From:** Krug, Gary - DOT  
**Sent:** Thursday, May 4, 2017 9:16 AM  
**To:** Bielefeldt, Heath - DOT  
**Subject:** RE: AT&T WI (AT&T/D) Facility Info for - WisDOT 7110-05-72 for STH 37

I guess the problems are going to be location 5 & 10. Also in the one picture are location 10, you can see another one that is not part of any location identified.

---

**From:** Bielefeldt, Heath - DOT  
**Sent:** Friday, April 28, 2017 9:11 AM  
**To:** Krug, Gary - DOT  
**Subject:** FW: AT&T WI (AT&T/D) Facility Info for - WisDOT 7110-05-72 for STH 37

See attached. Thanks. -Heath

---

**From:** PODOLAK, RICK T [<mailto:rp4514@att.com>]  
**Sent:** Friday, April 28, 2017 9:08 AM  
**To:** Bielefeldt, Heath - DOT <[Heath.Bielefeldt@dot.wi.gov](mailto:Heath.Bielefeldt@dot.wi.gov)>  
**Cc:** PODOLAK, RICK T <[rp4514@att.com](mailto:rp4514@att.com)>  
**Subject:** AT&T WI (AT&T/D) Facility Info for - WisDOT 7110-05-72 for STH 37

Heath,

Just following up with our facility information as requested from the utility meeting we had on 4-26. I marked/highlight the NB P&Ps with that information & also identified some locations that correspond to the attached deck of slide photos.

As far as "path shifting" goes in effort to help us protect our above ground appearance points, I'd like to request some sort of path shift from Sta 58+00 Rt to Sta 70+00 Rt & Sta 87+00 Rt to Sta 100+00. I highlighted those area on the attached NG P&Ps.

Hope this helps and I appreciate the time/consideration.

Rick

**From:** Bielefeldt, Heath - DOT  
**Sent:** Friday, April 28, 2017 9:11 AM  
**To:** Krug, Gary - DOT  
**Subject:** FW: AT&T WI (AT&T/D) Facility Info for - WisDOT 7110-05-72 for STH 37  
**Attachments:** AT&T WI Photos - WisDOT 7110-05-72 for STH 37.pdf; AT&T WI Facility - WisDOT 7110-05-72 for STH 37.pdf

[See attached. Thanks. -Heath](#)

---

**From:** PODOLAK, RICK T [mailto:rp4514@att.com]  
**Sent:** Friday, April 28, 2017 9:08 AM  
**To:** Bielefeldt, Heath - DOT  
**Cc:** PODOLAK, RICK T  
**Subject:** AT&T WI (AT&T/D) Facility Info for - WisDOT 7110-05-72 for STH 37

Heath,  
Just following up with our facility information as requested from the utility meeting we had on 4-26. I marked/highlight the NB P&Ps with that information & also identified some locations that correspond to the attached deck of slide photos.

As far as "path shifting" goes in effort to help us protect our above ground appearance points, I'd like to request some sort of path shift from Sta 58+00 Rt to Sta 70+00 Rt & Sta 87+00 Rt to Sta 100+00. I highlighted those area on the attached NG P&Ps.

Hope this helps and I appreciate the time/consideration.

Rick

**From:** William Koenig <wekoenig@att.net>  
**Sent:** Tuesday, April 11, 2017 7:10 AM  
**To:** Bielefeldt, Heath - DOT  
**Cc:** Carl Donahue; JB Overmyer  
**Subject:** WDOT 7110-05-72  
**Attachments:** WDOT Eau Claire81.doc

WDOT 7110-05-72

I-94/STH 37

Eau Claire County

WDOT DT2236 Utility Worksheet

Your message is ready to be sent with the following file or link attachments:

WDOT Eau Claire81

Note: To protect against computer viruses, e-mail programs may prevent sending or receiving certain types of file attachments. Check your e-mail security settings to determine how attachments are handled.

**From:** Martin, Christina - DOT  
**Sent:** Thursday, February 2, 2017 2:30 PM  
**To:** Krug, Gary - DOT; Holme, William G - DOT; Bielefeldt, Heath - DOT  
**Subject:** FW: FW: 71100502 37, IH 94 to USH 12, Eau Claire Co  
**Attachments:** additional util 2-1-2017.dwg; additional util 2-1-2017 - DOT.csv

Let us know if you need anything else ☺

Christina Martin, PLS  
NW Region Plat Coordinator  
Cell: (715) 225-9316

---

**From:** tlarson [<mailto:tlarson@faa-engineers.com>]  
**Sent:** Thursday, February 02, 2017 2:26 PM  
**To:** Martin, Christina - DOT  
**Subject:** Re: FW: 71100502 37, IH 94 to USH 12, Eau Claire Co

Christina,

Attached is a .dwg with the utilities from the two additional topo areas. If you guys need anything else or have any questions please feel free to give me a call.

Tony Larson

FAA Engineers

715.299.7214

On 1/23/2017 1:47 PM, Martin, Christina - DOT wrote:

Thanks for the quick turn around. Bill Holme will be reviewing the data and forwarding it on to the designer.

Christina Martin, PLS  
NW Region Plat Coordinator  
Cell: (715) 225-9316

---

**From:** tlarson [<mailto:tlarson@faa-engineers.com>]  
**Sent:** Monday, January 23, 2017 1:32 PM  
**To:** Martin, Christina - DOT ; Mueller, John  
**Subject:** Re: FW: 71100502 37, IH 94 to USH 12, Eau Claire Co

Christina,

We picked up additional topo around the new McDonald's lot and around the fence by Xcel Energy. Xcel's fence is 4'-8' behind the highway R/W lines. Attached are a couple photos of the two areas in question behind the fence. One is of a newer utility cabinet and the other is of the object in question. It's a old frame of some sort, not anchored to the ground by anything. The utility locate tickets have been called in and those lines will be collected after the tickets clear.

Thanks.

Tony Larson

On 1/19/2017 10:17 AM, Martin, Christina - DOT wrote:

John –  
Heath and I discussed the utility locate for Xcel. We think the best course to take would be for FAA to call in a diggers ticket and then FAA follow up with Dan Klein at Xcel to see if the locate can be expedited.

The cabinet is at approximately 65+10. Can you tell if the existing fence on the existing r/w in the area.

Christina Martin, PLS  
NW Region Plat Coordinator  
Cell: (715) 225-9316

---

**From:** Martin, Christina - DOT  
**Sent:** Wednesday, January 18, 2017 12:27 PM  
**To:** Mueller, John ; 'Skip Bertrand'  
**Subject:** 71100502 37, IH 94 to USH 12, Eau Claire Co

John -  
Additional work is needed on the above listed project. Please give me a call and we can discuss further.

Thanks

Christina

---

**From:** Holme, William G - DOT  
**Sent:** Wednesday, January 18, 2017 12:02:27 PM  
**To:** Martin, Christina - DOT  
**Subject:** RE: New Xcel electrical cabinet and lines; 7110-05-02, 72 STH 37, IH 94 to USH 12, Eau Claire Co

Christina,

We need the information Heath asked for about Xcel and the boxes behind the fence and here is what Gary wanted in the fence area: pick up everything within 20' of the fence. The contact for xcel is Traca Skogstad. She is the facility manager. [traca.a.skogstad@xcelenergy.com](mailto:traca.a.skogstad@xcelenergy.com) 715-737-2600 , cell is 715-577-1420.

Tammy and Gary would like the McD building located and the C&G of the parking lot near the intersection, this is what I sent you this morning. I would say pick up the sign even though we do have it on the plan already just because this job is all of a sudden full of surprise and I don't want another.

Bill

---

**From:** Martin, Christina - DOT  
**Sent:** Wednesday, January 18, 2017 9:57 AM  
**To:** Bielefeldt, Heath - DOT <[Heath.Bielefeldt@dot.wi.gov](mailto:Heath.Bielefeldt@dot.wi.gov)>; Ricksecker, Tammy - DOT <[Tammy.Ricksecker@dot.wi.gov](mailto:Tammy.Ricksecker@dot.wi.gov)>; Holme, William G - DOT <[William.Holme@dot.wi.gov](mailto:William.Holme@dot.wi.gov)>; Koepp, David - DOT <[David.Koepp@dot.wi.gov](mailto:David.Koepp@dot.wi.gov)>  
**Cc:** Dresel, Heather L - DOT <[Heather.Dresel@dot.wi.gov](mailto:Heather.Dresel@dot.wi.gov)>; Krug, Gary - DOT <[Gary.Krug@dot.wi.gov](mailto:Gary.Krug@dot.wi.gov)>; Martin, Christina - DOT <[Christina.Martin@dot.wi.gov](mailto:Christina.Martin@dot.wi.gov)>  
**Subject:** RE: New Xcel electrical cabinet and lines; 7110-05-02,72 STH 37, IH 94 to USH 12, Eau Claire Co

Thanks for the update Heath! Bill would you please look at the survey to see if the utilities are current and also the building corners for McDonald's along with the McDonalds sign.

Is it possible for all of us to get together and discuss the project schedule and expectations with the possible changes that may occur?

Christina Martin, PLS  
NW Region Plat Coordinator  
Cell: (715) 225-9316

---

**From:** Bielefeldt, Heath - DOT  
**Sent:** Wednesday, January 18, 2017 8:22 AM  
**To:** Ricksecker, Tammy - DOT <[Tammy.Ricksecker@dot.wi.gov](mailto:Tammy.Ricksecker@dot.wi.gov)>; Holme, William G - DOT <[William.Holme@dot.wi.gov](mailto:William.Holme@dot.wi.gov)>; Koepp, David - DOT <[David.Koepp@dot.wi.gov](mailto:David.Koepp@dot.wi.gov)>  
**Cc:** Dresel, Heather L - DOT <[Heather.Dresel@dot.wi.gov](mailto:Heather.Dresel@dot.wi.gov)>; Martin, Christina - DOT <[Christina.Martin@dot.wi.gov](mailto:Christina.Martin@dot.wi.gov)>; Krug, Gary - DOT

<[Gary.Krug@dot.wi.gov](mailto:Gary.Krug@dot.wi.gov)>

**Subject:** New Xcel electrical cabinet and lines; 7110-05-02, 72 STH 37, IH 94 to USH 12, Eau Claire Co

Below is a map of the new Xcel Energy electrical that was apparently installed this past summer. We will need to confirm location for the TPP and project plans, and as Klein says below, avoid if possible.

The compensability of the facilities is a bit unknown at this time. In the past, RE and Utility would both acquire the rights and pay as appropriate (RE for the land use and Utility for the facility moves), but recently CO Utility Unit discussed the policy with OGC and decided we would only pay for the land OR the facilities, not both. This policy shift was presented to the major Wisconsin utilities at an IRWA meeting in September 2016 and it was decided there would be further dialogue at higher levels as they of course did not agree.

Therefore, if any of these presumably high cost facilities need to be relocated, I will need to get the most up-to-date policy from CO as to whether or not we will still pay for both the facilities and the land use.

But first we need to know for sure where they fall. FAA did re-survey utilities in the area late last fall and should have collected this cabinet, so please verify they are collected.

Thanks.  
-Heath

---

**From:** Klein, Daniel J [<mailto:daniel.j.klein@xcelenergy.com>]


**Sent:** Wednesday, January 18, 2017 7:58 AM

**To:** Bielefeldt, Heath - DOT <[Heath.Bielefeldt@dot.wi.gov](mailto:Heath.Bielefeldt@dot.wi.gov)>

**Subject:** RE: Project I.D. 7110-05-02

Heath: The cabinet you are referring to is a new Switch Cabinet which is tied into our main line feeder cable. We have several cables in this area also the grade around the cabinet can't be disturbed. Please let me know if you need anything else.

Thanks, Dan

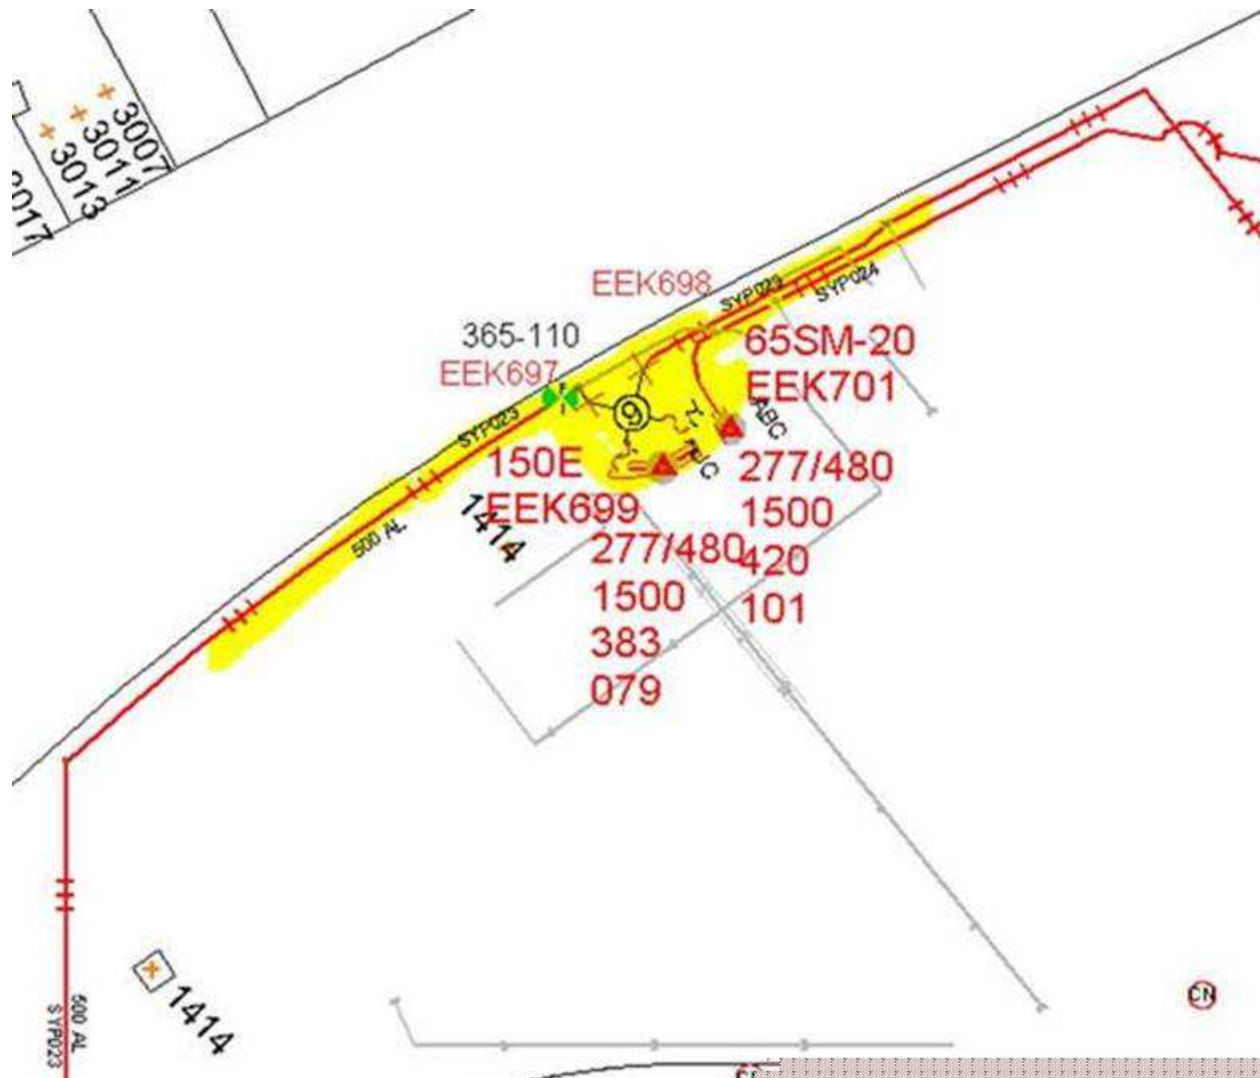

**From:** Koepp, David - DOT  
**Sent:** Wednesday, November 18, 2015 10:48 AM  
**To:** Ricksecker, Richard - DOT; DOT DTSD NW EC PERMIT COORDINATION  
**Cc:** Bielefeldt, Heath - DOT; Krug, Gary - DOT  
**Subject:** RE: 18-15-U33,W37-85,AT&T WI,A009EJ7,T-Brunswick,11.16.15

We are just in the beginning stages of this design. No conflicts are known at this point. We'll work with Heath as we progress through.

Thanks,

## **DAVE KOEPP, P.E.**

DEPARTMENT OF TRANSPORTATION, NW REGION  
718 W. CLAIREMONT AVE.  
EAU CLAIRE, WI 54701  
OFFICE: (715) 836-2078  
CELL: (715) 563-8402  
[david.koepp@dot.wi.gov](mailto:david.koepp@dot.wi.gov)

---

**From:** Ricksecker, Richard - DOT  
**Sent:** Tuesday, November 17, 2015 7:45 AM  
**To:** DOT DTSD NW EC PERMIT COORDINATION ; Koepp, David - DOT  
**Cc:** Bielefeldt, Heath - DOT  
**Subject:** RE: 18-15-U33,W37-85,AT&T WI,A009EJ7,T-Brunswick,11.16.15

My concerns would be related to construction; temp lanes, staging, stock piling, borrow, etc. which are best answered by Dave. No apparent Maintenance concerns.

Richard

---

**From:** DOT DTSD NW EC PERMIT COORDINATION  
**Sent:** Monday, November 16, 2015 12:14 PM  
**To:** Koepp, David - DOT <[David.Koepp@dot.wi.gov](mailto:David.Koepp@dot.wi.gov)>  
**Cc:** Bielefeldt, Heath - DOT <[Heath.Bielefeldt@dot.wi.gov](mailto:Heath.Bielefeldt@dot.wi.gov)>; Ricksecker, Richard - DOT <[Richard.Ricksecker@dot.wi.gov](mailto:Richard.Ricksecker@dot.wi.gov)>  
**Subject:** FW: 18-15-U33,W37-85,AT&T WI,A009EJ7,T-Brunswick,11.16.15

Hi Everyone,

Please review this utility application to make sure there isn't any conflicts on I-94 with installing telecom and the future pavement replacement project # 7110-05-72 that is slated for PS&E in February of 2019. Do you have a stipulation for the depth of bury for this installation? Any other concerns or comments that are not listed below?

Thank you,  
Vicki

---

**From:** DOT DTSD NW EC PERMIT COORDINATION  
**Sent:** Monday, November 16, 2015 12:01 PM  
**To:** 'REITER, RICHARD T' <[rr3631@att.com](mailto:rr3631@att.com)>  
**Subject:** RE: 18-15-U33,W37-85,AT&T WI,A009EJ7,T-Brunswick,11.16.15

Rick,

What will be the depth of the installation of the cable/PVC under I -94? There is guardrail going north and south between the I-94 lanes and guardrail going east and west along the lanes.

There is a WisDOT pavement replacement project # 7110-05-72 slated for 2019 on STH 37/85 from I-94 to USH 12. This application will be forwarded to our utility coordinator and project manager for their review and comments.

Thank you,  
Vicki

---

**From:** REITER, RICHARD T [<mailto:rr3631@att.com>]  
**Sent:** Friday, November 13, 2015 8:52 AM  
**To:** DOT DTSD NW EC PERMIT COORDINATION <[DOTDTSDNWECPERMITCOORDINATION@dot.wi.gov](mailto:DOTDTSDNWECPERMITCOORDINATION@dot.wi.gov)>  
**Subject:** 18-15-U33,W37-85,AT&T WI,A009EJ7,T-Brunswick,11.16.15

Thank you,

**Rick Reiter**  
**AT&T Wisconsin**  
**Manager – Design Engineering**  
**304 South Dewey St – 4<sup>th</sup> Flr**  
**Eau Claire, WI 54703**

**PH: 715-839-5807**  
**Mobile: 715-271-8163**  
**FAX: 715-839-5929**  
**EMAIL: [rr3631@att.com](mailto:rr3631@att.com)**

"This e-mail and any files transmitted with it are the property of AT&T Communications and/or its affiliates, are confidential, and are intended solely for the use of the individual or entity to whom this e-mail is addressed. If you are not one of the named recipients or otherwise have reason to believe that you have received this message in error, please notify the sender at 715-839-5807 and delete this message immediately from your computer. Any other use, retention, dissemination, forwarding, printing, or copying of this e-mail is strictly prohibited."

**From:** Bielefeldt, Heath - DOT  
**Sent:** Thursday, November 12, 2015 3:09 PM  
**To:** Mueller, John  
**Cc:** Holme, William G - DOT  
**Subject:** RE: Fwd: STH 37 Diggers; 7110-05-02,72 STH 37, IH 94 to USH 12, Eau Claire Co  
**Attachments:** 7110-05-02,72 Missing Locates.zip

Woody,

Attached are the Trans 220 contacts and the returned system maps (or descriptions) for the missing facilities.

Please note that CCI Systems maintains (and marks) the CINC facilities. And AT&T Distribution is AT&T Wisconsin. I do not know what Phillips Plastics is marking. Please let me know if you find out. Thanks.

Let me know if you need anything else.

Thanks.  
-Heath

Heath Bielefeldt | Utility Coordinator  
Northwest Region, Eau Claire Office | Wisconsin Dept. of Transportation  
718 W. Clairemont Avenue, Suite 200 | Eau Claire, WI 54701-5108  
715-836-2729 (Office) | heath.bielefeldt@dot.wi.gov

-----Original Message-----

From: Holme, William G - DOT  
Sent: Thursday, November 12, 2015 2:56 PM  
To: Bielefeldt, Heath - DOT <Heath.Bielefeldt@dot.wi.gov>  
Subject: FW: Fwd: STH 37 Diggers

Heath,

The utilities that didn't mark the project are:

- Charter Communications
- Windstream
- Phillips Plastics
- CCI Systems
- AT&T Distribution - did send maps

-----Original Message-----

From: John Mueller [mailto:woody@faa-engineers.com]  
Sent: Thursday, November 12, 2015 2:24 PM  
To: Armstrong, Thomas A - DOT <Thomas.Armstrong@dot.wi.gov>; 'Tony Larson' <tlarson@faa-engineers.com>

Cc: Holme, William G - DOT <William.Holme@dot.wi.gov>; Slick, Diane - DOT <Diane.Slick@dot.wi.gov>;  
Bruce Heath <bheath@menomonie-wi.gov>; Piller, Michael - DOT (DTSD NW TSS Supervisor)  
<Michael.Piller@dot.wi.gov>  
Subject: Re: Fwd: STH 37 Diggers

Could the department send me the region wide utility contact list that is used for the trans220 process?

Thanks & Have a Great Day

Woody.

John Mueller  
Professional Land Surveyor  
Fleming, Andre & Associates, Inc.  
3615 North Hastings Way, Suite 100  
Eau Claire, WI 54703  
OFFICE:715-832-8400  
CELL:715-299-7202  
FAX:715-832-1367  
E-mail : woody@faa-engineers.com

On 11/12/2015 1:48 PM, Armstrong, Thomas A - DOT wrote:

> Tony,

>

> Sorry for letting this project slip. I think I was looking into amending this contract per Woody's request and found that it could not be amended because it is a "lump sum" contract. Then I was looking into what we can do about the utility locate.

>

> Another locate ticket and a meeting with the locators would be beneficial explaining the previous time you were out that the markings were old and old markings are not adequate for your purpose. So at this time it will require your persistence with the locaters to complete the utility mapping. We have one system map submitted from AT&T, let me know if that would be beneficial to you.

>

> We have been looking into how the issues of locates being incomplete can/will be handled. So far we have no short term solutions. The long term solution is tracking the locate ticket and the specific utilities that were not located and sending the information to Central Office. Beyond that I have not heard how it will be handled.

>

> Please call me if it would be beneficial,

>

> -----Original Message-----

> From: Tony Larson [mailto:tlarson@faa-engineers.com]

> Sent: Monday, November 09, 2015 1:46 PM

> To: Armstrong, Thomas A - DOT <Thomas.Armstrong@dot.wi.gov>

> Cc: Mueller, John <woody@faa-engineers.com>

> Subject: Re: Fwd: STH 37 Diggers

>

> Hi Tom,

>  
> Just a follow up, have you guys decided what actions, if any, to take  
> regarding the utility survey for STH 37. Do you think calling in  
> another locate ticket and setting up a meeting with utility locators  
> would be beneficial? In the past I have had some luck with those  
> meetings but not always.  
>  
> If you have any questions or would like to discuss this further please  
> feel free to give me a call.  
>  
> Thanks.  
> Tony Larson  
> FAA Engineers  
> 715.299.7214  
>  
>  
> Tony Larson wrote:  
>> Tom,  
>>  
>> Project: Ancillary survey  
>>  
>> 7110-05-02  
>> Mondovi - Eau Claire  
>> IH 94 to USH 12  
>> STH 37  
>> Eau Claire County  
>>  
>>  
>> As stated in the e-mail thread below we are having some issues with  
>> the utilities being located in the field. As well as having the  
>> system maps being delivered. The first 'field' locate was due by  
>> 10/2/2015. For this stretch of roadway there were 6 tickets  
>> submitted. On those tickets there are a total of 11 different  
>> utilities. By 10/2/2015 only 3 of the 11 had marked anything in the  
>> field. There were areas with old paint marks on the roadway for some  
>> of the other utilities. But were not re-marked under the new locate  
>> tickets. A re-mark ticket was submitted and was due to be clear on  
>> 10-8-2015. No additional marking was completed under that ticket.  
>> The ticket that requested the system maps for this project was clear  
>> by 10-13-2015. I have received maps from only 3 companies.  
>>  
>> The companies that have located their utilities and that have been  
>> surveyed are: Xcel Energy Inc, City of Eau Claire, and Wisconsin DOT  
>> District #6  
>>  
>> The ones who have sent system maps are: City of Eau Claire, Wisconsin  
>> DOT District #6, and AT&T Distribution.  
>>

>> I did speak with the Xcel Energy locator and asked him if he knew who  
>> was supposed to located the other utilities but he didn't know the  
>> main contact people for the other companies. He did also mention  
>> that they have been very busy around town and that when locaters see  
>> the 'SURVEY LOCATE' on the top of the Diggers Hotline ticket they do  
>> not give it very high priority.

>>

>> Attached to this email are all Diggers Hotline tickets and system  
>> maps received to date.

>>

>> Please feel free to call me with any questions.

>>

>> Thanks.

>>

>> Tony Larson  
>> FAA Engineers  
>> 715.299.7214

>>

>>

>>

>>

>>

>>

>>

>> John Mueller wrote:

>>> Tony-

>>>

>>> Read below and see if we now have what we need out there or do we  
>>> still have issues with the locators.

>>>

>>> Thanks & Have a Great Day

>>>

>>> Woody.

>>>

>>> John Mueller

>>> Professional Land Surveyor

>>> Fleming, Andre & Associates, Inc.

>>> 3615 North Hastings Way, Suite 100

>>> Eau Claire, WI 54703

>>> OFFICE:715-832-8400

>>> CELL:715-299-7202

>>> FAX:715-832-1367

>>> E-mail : woody@faa-engineers.com

>>>

>>>

>>> ----- Forwarded Message -----

>>> Subject: STH 37 Diggers

>>> Date: Mon, 12 Oct 2015 15:48:33 +0000

>>> From: Holme, William G - DOT <William.Holme@dot.wi.gov>  
>>> To: Armstrong, Thomas A - DOT <Thomas.Armstrong@dot.wi.gov>,  
>>> Piller, Michael - DOT (DTSD NW TSS Supervisor)  
>>> <Michael.Piller@dot.wi.gov>  
>>> CC: Bielefeldt, Heath - DOT <Heath.Bielefeldt@dot.wi.gov>,  
>>> Mueller, John <woody@faa-engineers.com>  
>>>  
>>>  
>>>  
>>> Tom,  
>>>  
>>> I walk part of the project, from STH 12 to Craig Rd, and have found  
>>> the following utilities marked gas, electric, water, sewer. I did  
>>> not see telephone marked although there were some old faint markings  
>>> and I saw some pedestals. With that said someone did mow down some  
>>> of the gas and electric flags just south of the STH 12 but the  
>>> ground marking are still there and the electric marks for the stop  
>>> and go lights at the intersection are somewhat vague. Looking down  
>>> the project further the gas line was marked but runs in the ditch  
>>> and may be hidden with the tall grass.  
>>> \*Bill Holme\*  
>>> \*P.L.S. 2772\*  
>>> \*/NW Regional Surveyor Coordinator/\* /WisDOT -NW Region/  
>>> /Office: 715-836-3913/  
>>> /Cell: 715-450-0977/  
>>> /718 W. Clairemont Ave. Eau Claire , WI 54701/  
>>> /e-mail: //\_william.holme@dot.wi.gov\_  
>>> <mailto:thomas.armstrong@dot.wi.gov>/ /  
>>>  
>>>  
>>>  
>>>  
>>>
